

Comal County Environmental Health

OSSF Inspection Sheet

Installer Name: _____

OSSF Installer #: _____

1st Inspection Date: _____

2nd Inspection Date: _____

3rd Inspection Date: _____

Inspector Name: _____

Inspector Name: _____

Inspector Name: _____

Permit#:

Address:

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials		285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)				
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards		285.91(10) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)		285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot		285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)		285.32(a)(5)				
6	PRETREATMENT Installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

Inspector Notes:

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1) (E) 285.91(2) 285.32(b)(1) (F) 285.32(b)(1)(E) (iii) 285.32(b)(1)(E)(ii) (II) 285.32(b)(1)(E)(ii) (I) 285.32(b)(1)(E) (i) 285.32(b)(1) (D) 285.32(b)(1)(C) (ii) 285.32(b)(1)(C) (i) 285.32(b)(1) (B) 285.32(b)(1) (A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed						
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number						
16	DISPOSAL SYSTEM Absorptive		285.33(a)(4) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(3) 285.33(a)(4) 285.33(a)(1) 285.33(a)(2)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(4) 285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(a)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(v)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
32	EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling EFFLUENT DISPOSAL SYSTEM Topographic Slopes < 2.0% EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field (1000 Linear ft. for 2 bedrooms or Less & an additional 400 ft. for each additional bedroom) EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. & Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) & Pipe Holes (3/16 - 1/4" dia. Hole Size) 5 ft. Apart		285.33(b)(3)(A) 285.33(b)(3)(A) 285.33(b)(3)(B) 285.91(13) 285.33(b)(3)(D) 285.33(b)(3)(F)				
33	AEROBIC TREATMENT UNIT Is Aerobic Unit Installed According to Approved Guidelines.		285.32(c)(1)				
34	AEROBIC TREATMENT UNIT Inspection/Clean Out Port & Risers Provided AEROBIC TREATMENT UNIT Secondary restraint system provided AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions						
35	AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.						
36	PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials & construction PUMP TANK Sampling Port Provided in the Treated Effluent Line PUMP TANK Check Valve and/or Anti- Siphon Device Present When Required PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump						
37	PUMP TANK Inspection/Clean Out Port & Risers Provided PUMP TANK Secondary restraint system provided PUMP TANK Riser permanently fastened to lid or cast into tank PUMP TANK Riser cap protected against unauthorized intrusions						
38	PUMP TANK Secondary restraint system provided						
39	PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried						

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?		285.33(d)(2)(G)(iii)(II) 285.33(d)(2)(G)(iii)(III) 285.33(d)(2)(G)(v) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)				
41	APPLICATION AREA Low Angle Nozzles Used / Pressure is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed		285.33(d)(2)(G) (i)285.33(d)(2) (A)285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						



COMAL COUNTY

ENGINEER'S OFFICE

Permit of Authorization to Construct an On-Site Sewage Facility Permit Valid For One Year From Date Issued

Permit Number: 118467
Issued This Date: 04/08/2025
This permit is hereby given to: TJITSE MILLER & KAITLIN MILLER

To start construction of a private, on-site sewage facility located at:

1805 MISTY HOLW
NEW BRAUNFELS, TX 78132

Subdivision: ROYAL FORREST
Unit: 0
Lot: 339
Block: 0
Acreage: 3.5800

APPROVED MINIMUM SIZES AS PER ATTACHED DESIGN

Type of System: Aerobic
Surface Irrigation

This permit gives permission for the construction of the above referenced on-site facility to commence. Installation must be completed by an installer holding a valid registration card from the Texas Commission on Environmental Quality (TCEQ). Installation and inspection must comply with current TCEQ and Comal County requirements.

Call (830) 608-2090 to schedule inspections.



COMAL COUNTY
ENGINEER'S OFFICE

ON-SITE SEWAGE FACILITY APPLICATION

195 DAVID JONAS DR
NEW BRAUNFELS, TX 78132
(830) 606-2090
WWW.CC100.ORG

Date February 25, 2025

Permit Number 118467

1. APPLICANT / AGENT INFORMATION

Owner Name TJITSE MILLER & KAITLIN MILLER
Mailing Address 3013 SANDSTONE WAY
City, State, Zip NEW BRAUNFELS TEXAS 78130
Phone # 239-994-3471
Email kateej94@gmail.com

Agent Name GREG JOHNSON, P.E.
Agent Address 170 HOLLOW OAK
City, State, Zip NEW BRAUNFELS TEXAS 78132
Phone # 830-905-2778
Email gregjohnsonpe@yahoo.com

2. LOCATION

Subdivision Name ROYAL FORREST Unit Lot 339 Block

Survey Name / Abstract Number Acreage

Address 1805 MISTY HOLLOW City NEW BRAUNFELS State TX Zip 78132

3. TYPE OF DEVELOPMENT

☒ Single Family Residential

Type of Construction (House, Mobile, RV, Etc.) HOUSE & DETACHED LIVING & PERSONAL RV

Number of Bedrooms 1+1

Indicate Sq Ft of Living Area 700+500

☐ Non-Single Family Residential

(Planning materials must show adequate land area for doubling the required land needed for treatment units and disposal area)

Type of Facility

Offices, Factories, Churches, Schools, Parks, Etc. - Indicate Number Of Occupants

Restaurants, Lounges, Theaters - Indicate Number of Seats

Hotel, Motel, Hospital, Nursing Home - Indicate Number of Beds

Travel Trailer/RV Parks - Indicate Number of Spaces

Miscellaneous

Estimated Cost of Construction: \$ 200,000 (Structure Only)

Is any portion of the proposed OSSF located in the United States Army Corps of Engineers (USACE) flowage easement?

☐ Yes ☒ No (If yes, owner must provide approval from USACE for proposed OSSF improvements within the USACE flowage easement)

Source of Water ☐ Public ☐ Private Well ☒ Rainwater Collection

4. SIGNATURE OF OWNER

By signing this application, I certify that:

- The completed application and all additional information submitted does not contain any false information and does not conceal any material facts. I certify that I am the property owner or I possess the appropriate land rights necessary to make the permitted improvements on said property.
- Authorization is hereby given to the permitting authority and designated agents to enter upon the above described property for the purpose of site/soil evaluation and inspection of private sewage facilities.
- I understand that a permit of authorization to construct will not be issued until the Floodplain Administrator has performed the reviews required by the Comal County Flood Damage Prevention Order.
- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

Tjitse Miller Kaitlin Miller
Signature of Owner

2/26/25
Date



COMAL COUNTY
ENGINEER'S OFFICE

ON-SITE SEWAGE FACILITY APPLICATION

ROYAL FOREST LOT 339

195 DAVID JONAS DR
NEW BRAUNFELS, TX 78132
(830) 608-2090
WWW.CCEO.ORG

Planning Materials & Site Evaluation as Required Completed By GREG W. JOHNSON, P.E.

System Description PROPRIETARY; AEROBIC TREATMENT AND SURFACE IRRIGATION

Size of Septic System Required Based on Planning Materials & Soil Evaluation

Tank Size(s) (Gallons) CLEARSTREAM 800NC2 / 1200 PUMP Absorption/Application Area (Sq Ft) 6742

Gallons Per Day (As Per TCEQ Table 111) 420 DESIGN RATE

(Sites generating more than 5000 gallons per day are required to obtain a permit through TCEQ.)

Is the property located over the Edwards Recharge Zone? ☒ Yes ☐ No

(if yes, the planning materials must be completed by a Registered Sanitarian (R.S.) or Professional Engineer (P.E.))

Is there an existing TCEQ approved WPAP for the property? ☐ Yes ☒ No

(if yes, the R.S. or P.E. shall certify that the OSSF design complies with all provisions of the existing WPAP.)

Is there at least one acre per single family dwelling as per 285.40(c)(1)? ☒ Yes ☐ No

If there is no existing WPAP, does the proposed development activity require a TCEQ approved WPAP? ☐ Yes ☒ No

(if yes, the R.S or P.E. shall certify that the OSSF design will comply with all-provisions of the proposed WPAP. A Permit to Construct will not be issued for the proposed OSSF until the proposed WPAP has been approved by the appropriate regional office.)

Is the property located over the Edwards Contributing Zone? ☐ Yes ☒ No

Is there an existing TCEQ approval CZP for the property? ☐ Yes ☒ No


(if yes, the P.E. or R.S. shall certify that the OSSF design complies with all provisions of the existing CZP.)

If there is no existing CZP, does the proposed development activity require a TCEQ approved CZP? ☐ Yes ☒ No

(if yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed CZP. A Permit to Construct will not be issued for the proposed OSSF until the UP has been approved by the appropriate reg

Is this property within an incorporated city? ☐ Yes ☒ No

If yes, indicate the city: _____



FIRM #2585

By signing this application, I certify that:

- The information provided above is true and correct to the best of my knowledge.
- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

Signature of Designer

February 26, 2025
Date



On-Site Sewage Facility (OSSF) Service Agreement

- I. **General:** This Work for Hire Agreement (hereinafter referred to as "Agreement") is entered into by and between TJITSE & KAITLIN MILLER, (hereinafter referred to as "Client") and SOTX Septic Services (hereinafter to as "Contractor"). By this agreement, Contractor agrees to render services, as described herein, and the Client agrees to fulfill his/her/their responsibilities under this agreement as described herein.
- II. **Effective Dates:** This agreement commences on receipt of full payment and runs for two (2) years. Agreement's... Starting Date: (Date License to Operate is Issued) Ending Date: (2yrs. From Date of LTO)
- III. **Services by Contractor:** Contractor will provide the following services (hereinafter referred to as the "Services"):
 1. In compliance with Agency (TCEQ and/or County) and manufacturer's requirements, inspect and perform routine maintenance on the On-Site Sewage Facility (hereinafter referred to as the "OSSF") three (3) times per year (approximately once every four (4) months).
 2. Report to the appropriate regulatory authority and to the Client, as is required by both the State's on-site rules and the local Agency's rules, if more stringent. All findings must be reported to the local Agency within 14 days.
 3. If any components of the OSSF are found to need repair during the inspection, the Contractor will notify the Client of the repairs needed.
 4. Visit in response to Client's request(s) for unscheduled service(s) within two business days from the date of Contractor's receipt of Client's request. All unscheduled responses are in addition to the fee covered by this Agreement and will be billed to the Client.
 5. Provide notification of arrival to site to the homeowner or to site personnel. Additionally, written notification of the visit will be left at the site or with site personnel upon completion or inspection, as well as, forwarded to agency within 14 days.
- IV. **Site Location:** The Services are to be performed at the property located at:

1805 MISTY HOLLOW

ROYAL FORREST, LOT 339
- V. **Payment(s):** The fee for this Agreement only covers the Services describes herein. This fee does not cover equipment, parts or labor supplied for the repairs or charges for unscheduled Client-request trips to the site. Payments for such additional services are due when service is provided or rendered. Payments not received within 30 days from due date will be subjected to a \$20.00 late penalty and / or a 1.5% carrying charge, whichever is greater, in addition the reasonable attorney's fees and all costs of collection incurred by Contractor in collection of any unpaid debt(s). By signing this contract, the Client is authorizing the Contractor to remove any parts which were installed but not paid for at the end of 30 days. The Client is still responsible for any labor costs associated with the installation and remove of said parts.

Initials...

Customer: TJM/KEMContractor: CDH

Client's Responsibilities: The Client is responsible for each and all the following:

1. Maintain chlorinator and provide proper chlorine supply, if OSSF is equipped with same.
2. Provide all necessary yard or lawn maintenance and removal of obstacles as needed to allow the OSSF to function properly, and to allow Contractor easy access to all parts of the OSSF.
3. Maintain a current license to operate and abide by the conditions and limitations of that license and all requirements for on-site sewage facilities (OSSF's) from the State and local regulatory agency, as well as manufacturer's recommendations.
4. Immediately notify the Contractor and Agency of all problems with, including the failure of the OSSF.
5. Upon receiving a written notification of services needed from the Contractor, it becomes the Client's responsibility to contact the Contractor to authorize the service. If the Client chooses to use a different contractor to perform the service, the Client's responsible for ensuring the contractor holds the proper license (Installer II) and is certified by the manufacturer. Also, the Client is responsible for ensuring proper notification is given to the Agency, as required by the State and local Agency rules.
6. Provide the Contractor with water usage records, upon request, for evaluation by the Contractor of the OSSF performance.
7. Clients residing in Harris County should allow for samples at both the Inlet and outlet to the OSSF to be obtained by the Contractor for the purpose of evaluating the OSSF's performance when requested by the Client. If these samples are sent to the lab for testing, the Client will directly pay the lab for the cost of the testing plus pay the Contractor for all man-hours expended in providing this additional service at the rate of \$75.00 per hour measured from office to site, site to lab, and lab to office, otherwise known as portal to portal.
8. Not allow the backwash from water treatment or water conditioning equipment to enter the OSSF.
9. Provide for pumping of tanks, when needed, at Clients expense.
10. Maintain site drainage to prevent adverse effects on OSSF.
11. Promptly and fully pay Contractor's bills, fees, or invoices as described herein.
- VI. **Access by Contractor:** Contractor, or personnel authorized by the Contractor, may enter the property at reasonable times without prior notice for the purpose of performing the above-described Services. Contractor will require access to the OSSF electrical and physical components, including tanks, by means of manways or risers for the purpose of evaluations required by manufacturer, and/ or rules. If such manways or risers are not in place, excavation together with other labor and materials will be required and will be billed to Client as additional service at the rate of \$75.00 per hour, plus materials billed at list price. Excavated soil is to be replaced as best as reasonably possible.
- VII. **Application or Transfer of Payments:** The fees paid for this agreement may transfer to subsequent owner(s); however, this agreement will not transfer. The subsequent owner(s) must sign a similar agreement authorizing Contractor to perform the above-described Services and accepting Client's responsibilities. This replacement Agreement must be signed and received within 30 days of transfer of ownership. Contractor will apply all funds received from Client first to any past due obligations arising from this Agreement including late charges, return check charges, and charges for repairs or services not paid within 30 days of invoicing. The consumption of the payment in this manner may lead to early termination of the agreement by Contractor.
- VIII. **Termination of Agreement:** This Agreement may be terminated by either party within 30 days written notice in the event of substantial failure to perform in accordance with its terms by the other party without fault of the terminating party. If this Agreement is so terminated, Contractor shall be paid at the rate of \$75.00 per hour for any work performed, but not yet paid. The party terminating will immediately notify the other party, the equipment manufacturer, and the regulatory agency of the termination.
- IX. **Limits of Liability:** In no event shall the Contractor be liable for indirect, consequential, incidental or punitive damages, whether in contract tort or any other theory. In no event the Contractor's liability for direct damages exceed the price for the Services described in this Agreement.
- X. **Severability:** If any provision in the Agreement shall be held to be invalid or unenforceable for any reason, the remaining provisions shall continue to be valid and enforceable. If court finds that any provision of this

Initials...

Customer:

TJM/KEM

Contractor:

CDH

Agreement is invalid or unenforceable, but that by limiting such provision it would become valid and enforceable, then such provision shall be written, construed, and enforced as so limited.

XI. **Performance of Agreement:** Commencement of performance by Contractor under this agreement is contingent on the following conditions (1) Contractor receiving a fully execute original copy of this agreement. (2) Contractor receiving payment in full for the fee as described in Section V. If the above conditions are not met, then Contractor is not obligated to perform any portion of this agreement.

XII. **Entire Agreement:** This agreement contains the entire agreement parties, and there are no other promises or conditions in any other agreement, oral or written.

Client... (And/or authorized agent)

Printed Name: TJITSE MILLER Signature: *Tj Miller* Date: 2/26/25

Printed Name: KAITLIN MILLER Signature: *Kaitlin Miller* Date: _____

Physical Address: 1805 MISTY HOLLOW, NEW BRAUNFEL Zip: 78132

Mailing Address: 3013 SANDSTONE WAY, NEW BRAUNFELS Zip: 78130

Phone # _____ Cell# 239-994-3471 County: COMAL

Email: katee94@gmail.com Gate Code: _____

===== Contractor ===== Contractor =====

SOTX Septic Services

15656 Cranes Mill Rd.

Canyon Lake, TX 78133

830-481-3249

sotxservices@gmail.com

Clarence D. Hinds Jr *Clarence D Hinds Jr.*

Lic #: OSSF Installer II #: OS0030965

Maintenance Provider #: MP0002439

Installer Name: BRAD PARKER

Phone #: 830-310-2344

Email: parker.construction@yahoo.com

Lic #: OS#0035249

Manufacturer: CLEARSTREAM 800 NC2

GPD: 600 800 1000 Other: _____

Disposal: Spray Drip Other: _____

Initials...

Customer: *TJM/KE*

Contractor: *CDH*

Greg W. Johnson, P.E.
170 Hollow Oak
New Braunfels, Texas 78132
830/905-2778

February 26, 2025

Comal County Office of Environmental Health
195 David Jonas Drive
New Braunfels, Texas 78132-3760


RE- SEPTIC DESIGN
1805 MISTY HOLLOW
ROYAL FORREST, LOT 339
NEW BRAUNFELS, TX 78132
MILLER RESIDENCE

Brandon/Brenda,


The referenced property is located within the Edwards Aquifer Recharge Zone. This property is exempt from a WPAP because it is not a regulated activity according to §213.5(h)(2) "exempt ... does not exceed 20 % impervious cover on the site. To my knowledge no WPAP exists for this property.

Temporary erosion and sedimentation controls should be utilized as necessary prior to construction. If any sensitive feature (caves, solution cavities, sink holes, etc.) is discovered during construction, activities must be suspended immediately and the applicant or his agent must immediately notify the TCEQ Regional Office. After that operations can only proceed after the Executive Director approves required additional engineered impact plans.

Designed in accordance with Chapter 285, Subchapter D, §285.40, 285.4 1, & 285.42, Texas Commission on Environmental Quality (Effective December 29, 2016).

 02/26/25

Greg W. Johnson, P.E. No. 67587/F#2585
170 Hollow Oak
New Braunfels, Texas 78132 - 830/905-2778



**ON-SITE SEWERAGE FACILITY
SOIL EVALUATION REPORT INFORMATION**

Date Soil Survey Performed: February 25, 2025

Site Location: ROYAL FORREST, LOT 339

Proposed Excavation Depth: N/A

Requirements:

At least two soil excavations must be performed on the site, at opposite ends of the proposed disposal area.

Locations of soil boring or dug pits must be shown on the site drawing.


For subsurface disposal, soil evaluations must be performed to a depth of at least two feet below the proposed excavation depth. For surface disposal, the surface horizon must be evaluated.

Describe each soil horizon and identify any restrictive features on the form. Indicate depths where features appear.

SOIL BORING NUMBER <u> </u> SURFACE EVALUATION <u> </u>						
Depth (Feet)	Texture Class	Soil Texture	Gravel Analysis	Drainage (Mottles/ Water Table)	Restrictive Horizon	Observations
0	III	CLAY LOAM	N/A	NONE OBSERVED	LIMESTONE @ 8"	BROWN
1						
2						
3						
4						
5						

SOIL BORING NUMBER <u> </u> SURFACE EVALUATION <u> </u>						
Depth (Feet)	Texture Class	Soil Texture	Gravel Analysis	Drainage (Mottles/ Water Table)	Restrictive Horizon	Observations
0	SAME		AS		ABOVE	
1						
2						
3						
4						
5						

I certify that the findings of this report are based on my field observations and are accurate to the best of my ability.


Greg W. Johnson, P.E. 67587-F2585, S.E. 11561

02/25/25
Date

OSSF SOIL EVALUATION REPORT INFORMATION

Date: February 26, 2025

Applicant Information:

Name: TJITSE & KAITLIN MILLER
Address: 3013 SANDSTONE WAY
City: NEW BRAUNFELS State: TEXAS
Zip Code: 78130 Phone: (239) 994-3471

Site Evaluator Information:

Name: Greg W. Johnson, P.E., R.S., S.E. 11561
Address: 170 Hollow Oak
City: New Braunfels State: Texas
Zip Code: 78132 Phone & Fax (830)905-2778

Property Location:

Lot 339 Unit Blk Subd. ROYAL FORREST
Street Address: 1805 MISTY HOLLOW
City: NEW BRAUNFELS Zip Code: 78132
Additional Info.:

Installer Information:

Name:
Company:
Address:
City: State:
Zip Code: Phone

Topography: Slope within proposed disposal area: 4 %

Presence of 100 yr. Flood Zone: YES NO X
Existing or proposed water well in nearby area. YES NO X
Presence of adjacent ponds, streams, water impoundments YES NO X
Presence of upper water shed YES NO X
Organized sewage service available to lot YES NO X

**NOTE: USING A RAINWATER
COLLECTION SYSTEM**

Design Calculations for Aerobic Treatment with Spray Irrigation:

Commercial

Q = GPD

Residential Water conserving fixtures to be utilized? Yes X No

Number of Bedrooms the septic system is sized for: Total sq. ft. living area

Q gal/day = (Bedrooms +1) * 75 GPD - (20% reduction for water conserving fixtures)

Q = (+1)*75-(20%)= 420

Trash Tank Size 500 Gal.

**NOTE: 1 BDRM. + 1 BDRM DETACHED LIVING @ 240
GPD + RV DROP @ 114 = 354 GPD - USING A DESIGN
RATE OF 420 GPD**

TCEQ Approved Aerobic Plant Size 800 G.P.D.

Req'd Application Area = Q/Ri = 420 / 0.064 = 6563 sq. ft.

Application Area Utilized = 6842 sq. ft.

Pump Requirement 12 Gpm @ 41 Psi (Redjacket 0.5 HP 18 G.P.M. series or equivalent)

Dosing Cycle: ON DEMAND or X TIMED TO DOSE IN PREDAWN HOURS

Pump Tank Size = 1200 Gal. 19.6 Gal/inch.

Reserve Requirement = 140 Gal. 1/3 day flow.

Alarms: Audible & Visual High Water Alarm & Visual Air Pump malfunction

With Chlorinator NSF/TCEQ APPROVED

SCH-40 or SDR-26 3" or 4" sewer line to tank

Two way cleanout

Pop-up rotary sprinkler heads w/ purple non-potable lids

1" Sch-40 PVC discharge manifold


APPLICATION AREA SHOULD BE SEEDED AND MAINTAINED WITH VEGETATION.

EXPOSED ROCK WILL BE COVERED WITH SOIL .


I HAVE PERFORMED A THOROUGH INVESTIGATION BEING A REGISTERED PROFESSIONAL ENGINEER
AND SITE EVALUATOR IN ACCORDANCE WITH CHAPTER 285, SUBCHAPTER D, §285.30, & §285.40
(REGARDING RECHARGE FEATURES), TEXAS COMMISSION OF ENVIRONMENTAL QUALITY
(EFFECTIVE DECEMBER 29, 2016)

GREG W. JOHNSON, P.E. F#002585 - S.E. 11561



02/26/25
DATE



FIRM #2585


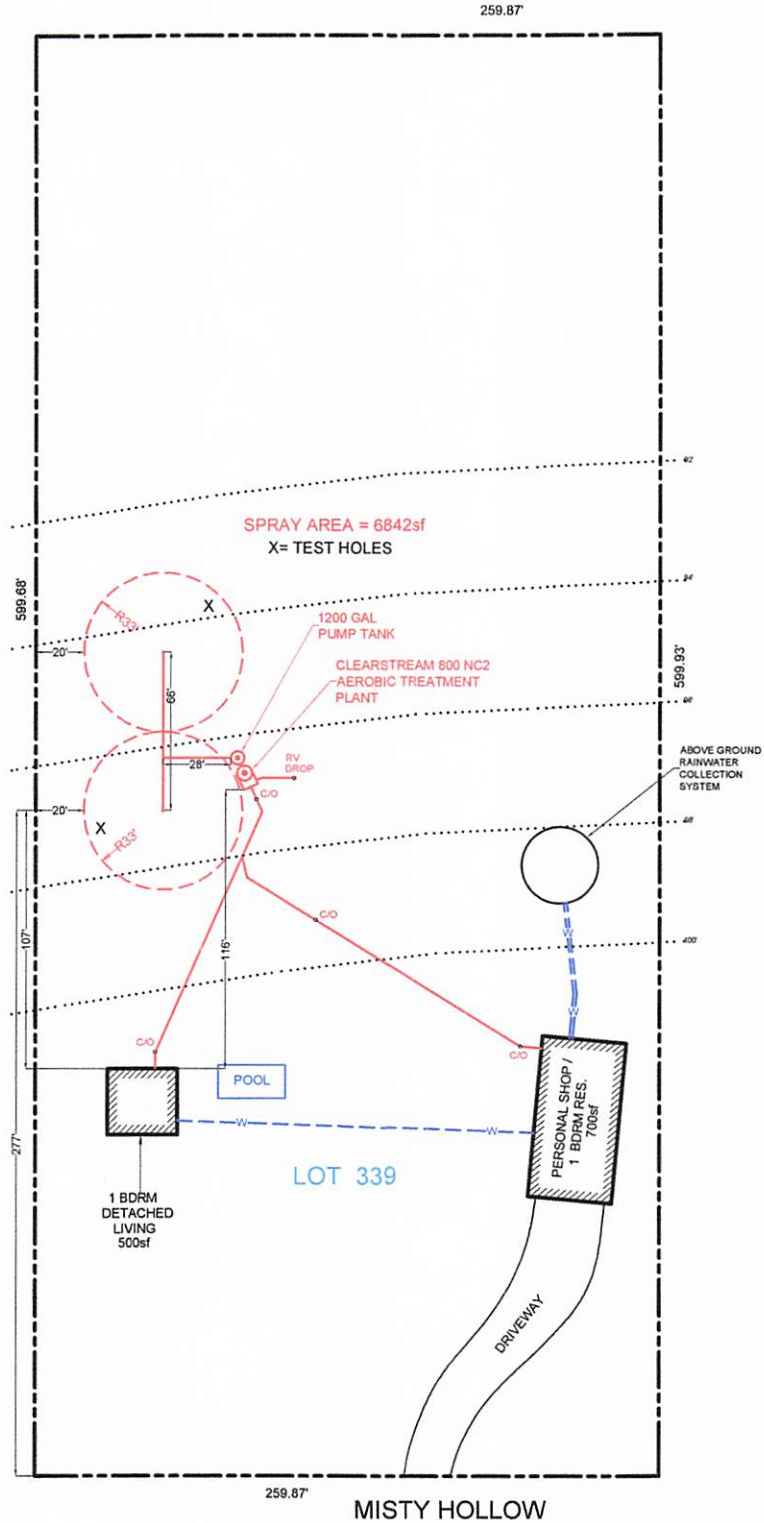


OWNER: TJITSE & KAITLIN MILLER				DRAWN BY: EJS III		
STREET ADDRESS: 1805 MISTY HOLLOW						
LEGAL DESC: ROYAL FORREST			UNIT/SECTION/PHASE:		BLOCK:	LOT: 339
PREPARED BY: GREG W. JOHNSON, P.E. F#002585		SCALE: 1"=80'	DATE: 2/26/2025		REVISED: 3/6/2025	

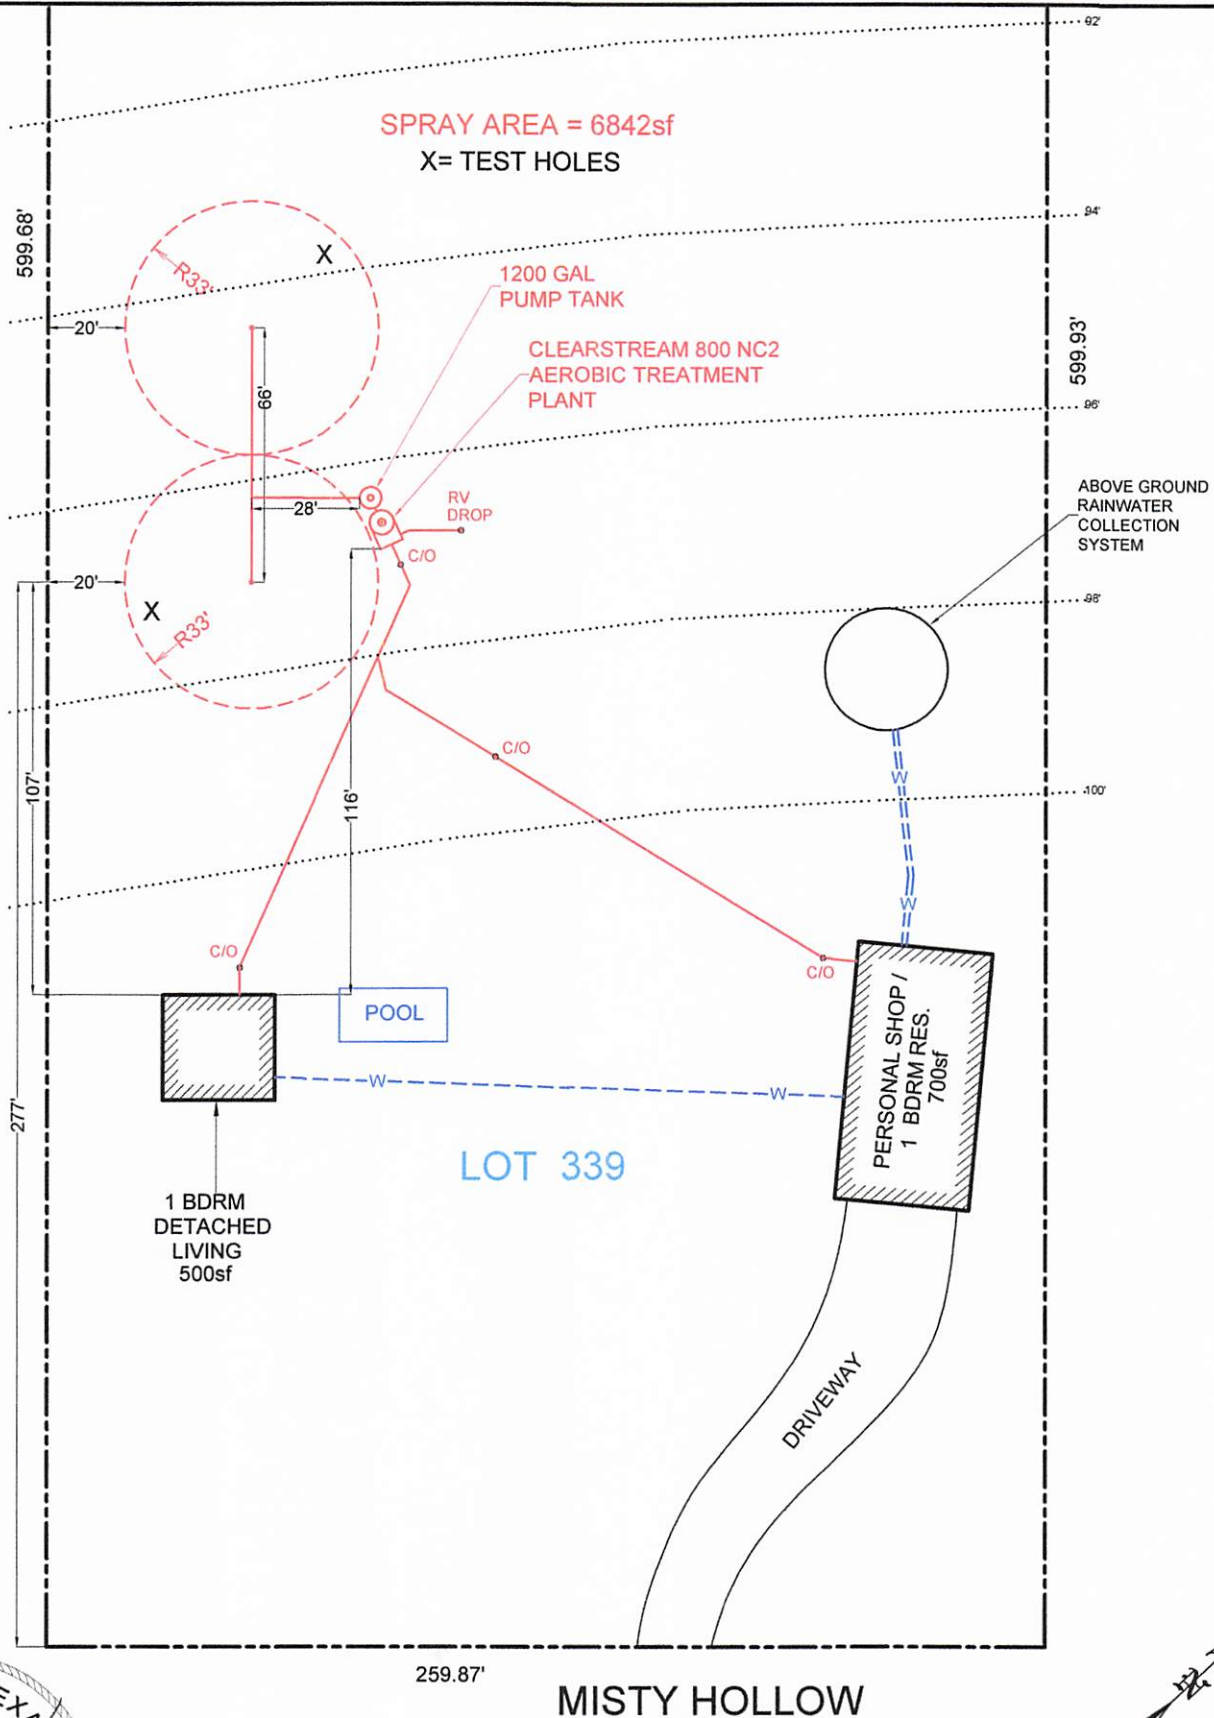

OWNER: TJITSE & KAITLIN MILLER		DRAWN BY: EJS III	
STREET ADDRESS: 1805 MISTY HOLLOW			
LEGAL DESC: ROYAL FORREST	UNIT/SECTION/PHASE:	BLOCK:	LOT: 339
PREPARED BY: GREG W. JOHNSON, P.E. F#002585	SCALE: 1"=50'	DATE: 2/26/2025	REVISED: 3/6/2025


DESIGN DRAWINGS

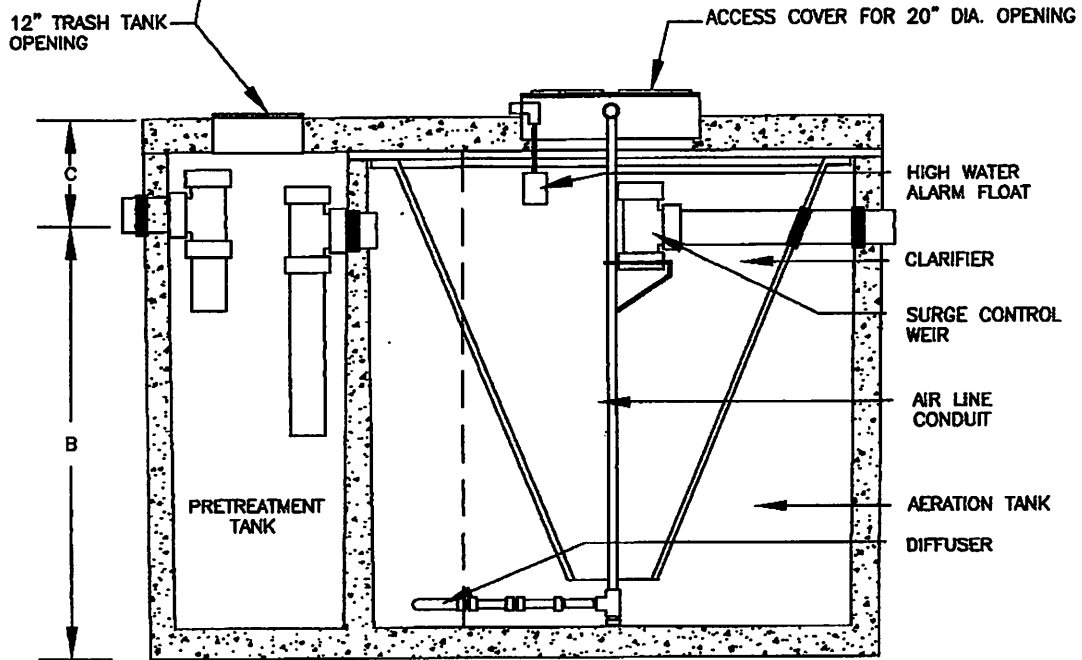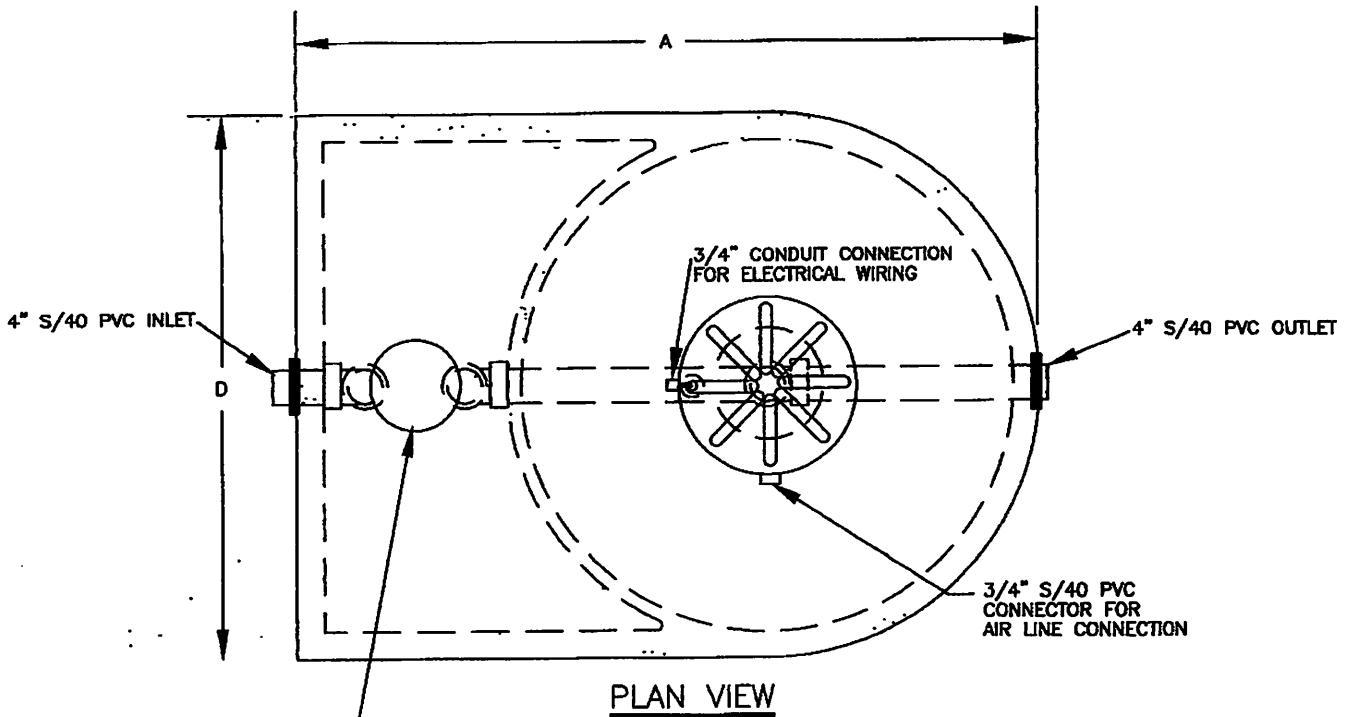

MODEL NC2
SECTION

DIMENSIONAL DATA

MODEL	A	B	C	D
500 NC2	104"	60"	10-1/2"	75"
600 NC2	107"	60"	10-1/2"	82"
750 NC2	107"	70"	10-1/2"	82"
800 NC2	107"	72"	8-1/2"	82"



F2508
02/26/25

TANK NOTES:



Tanks must be set to allow a minimum of 1/8" per foot fall from the residence.

Tightlines to the tank shall be SCH-40 PVC.

A two way sanitary tee is required between residence and tank.

A minimum of 4" of sand, sandy loam, clay loam free of rock shall be placed under and around tanks

ALL WIRING MUST BE IN COMPLIANCE WITH
THE MOST RECENT NATIONAL ELECTRIC CODE

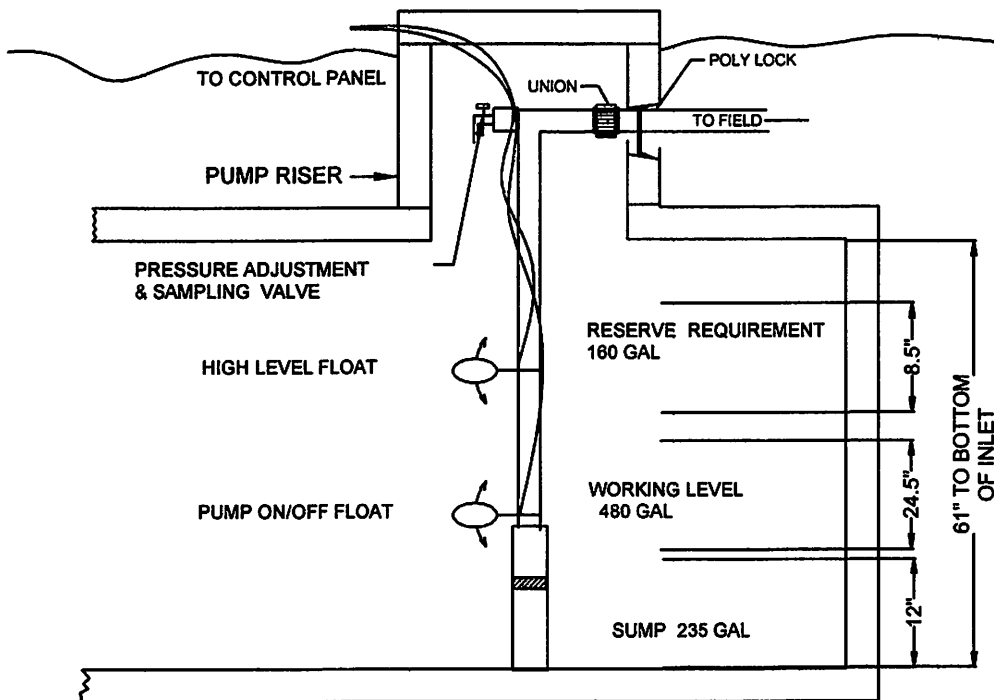

**TYPICAL PUMP TANK CONFIGURATION
CLEARSTREAM 1200 GAL PUMP TANK**

OPERATION

1. The pump must be submerged at all times during normal operation. Do not run pump dry.
2. Make sure that the float switches are set so that the pump stops before the pump runs dry or breaks suction. If necessary, adjust float switches to achieve this.
3. The motor bearings are lubricated internally. No maintenance is required or possible on the pump.

Table 1: Recommended Fusing Data
60 Hz/1 Phase 2-Wire Cable

Model	HP	Voltz/Hz/ Phase	Max Load Amps	Locked Rotor Amps	Fuse Size Standard/ Dual Element
P10D	1/2	115/60/1	11.0	30.0	15
P20D	1/2	115/60/1	9.5	30.0	15
P30D	1/2	115/60/1	9.5	30.0	15




Figure 1: Insert a piece of 3" PVC pipe in the bottom of the motor to raise the pump in the tank.

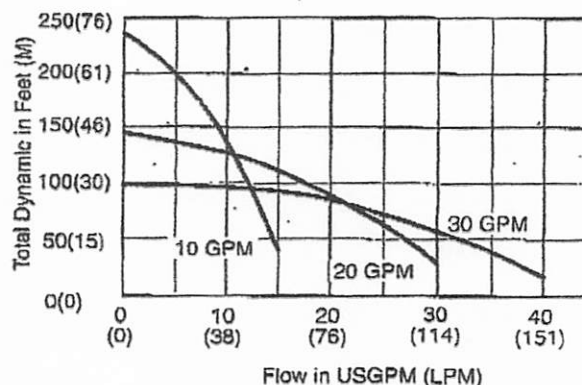



Figure 2: Performance in Feet of Head at Gallons Per Minute (GPM).

LOW ANGLE NOZZLE PERFORMANCE CHART

Nozzle	PSI	Radius	GPM
#1	30	22'	1.5
	40	24'	1.7
	50	26'	1.8
	60	28'	2.0
#3	30	29'	3.0
	40	32'	3.1
	50	35'	3.5
	60	37'	3.8
#4	30	31'	3.4
	40	34'	3.9
	50	37'	4.4
	60	38'	4.7
#6	40	38'	6.5
	50	40'	7.3
	60	42'	8.0
	70	44'	8.6

KRAIN
K-2 PLUS

X

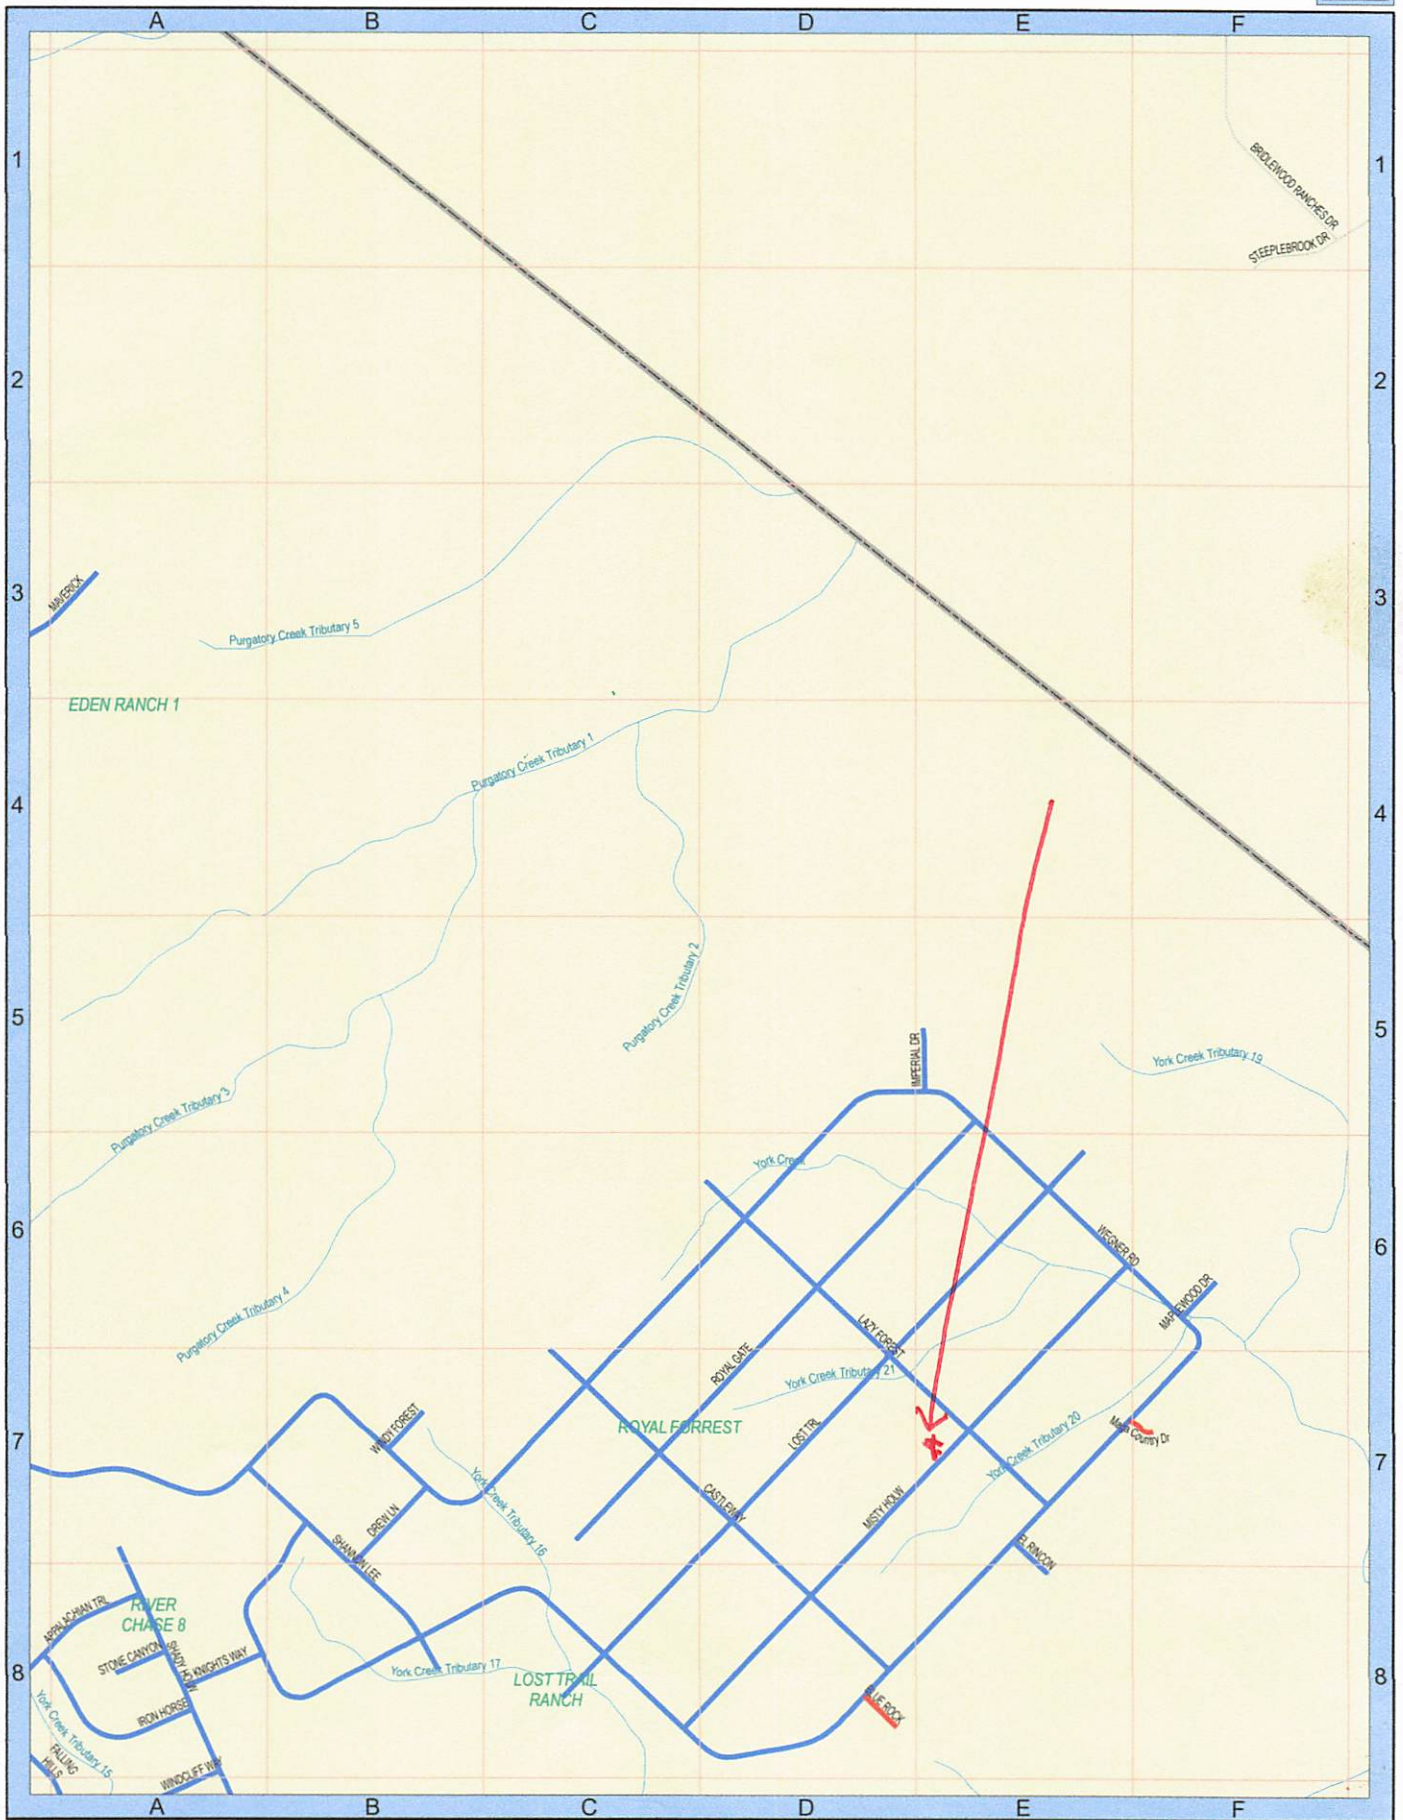

SEE PAGE 34



0 1,250 2,500
Feet

0 0.25 0.5
Miles

CAPITAL TITLE
GF # _____

25-843079-AS

Warranty Deed with Vendor's Lien

Notice of confidentiality rights: If you are a natural person, you may remove or strike any or all of the following information from any instrument that transfers an interest in real property before it is filed for record in the public records: your Social Security number or your driver's license number.

Date: February 19, 2025

Grantor: Chris Terry and Kevyn Terry a/k/a Kevin Terry

Grantee: Tjitse miller and Kaitlin Miller, husband and wife, owning, occupying, and claiming other property as homestead

Grantee's Mailing Address: 3013 Sandstone Way, New Braunfels, TX 78130

Consideration:

Cash and other good and valuable consideration along with a note of even date executed by Grantee and payable to the order of Randolph-Brooks Federal Credit Union in the principal amount of \$155,000.00 (One Hundred Fifty Five Thousand and 00/100 Dollars). The note is secured by a first and superior vendor's lien and superior title retained in this deed in favor of Randolph-Brooks Federal Credit Union and by a first-lien deed of trust of even date from Grantee to Morton W. Baird, II, trustee.

Property (including any improvements):

Lot 339, ROYAL FOREST SUBDIVISION, Comal County, Texas, according to plat thereof recorded in Volume 4, Page 4, Map and Plat Records of Comal County, Texas.

Reservations from Conveyance: None

Exceptions to Conveyance and Warranty:

This Deed is executed, delivered and accepted subject to all and singular any liens securing the payment of any debt created or assumed in connection herewith if such liens are described herein, standby fees, ad valorem taxes for the current and all subsequent years, subsequent assessments for prior years due to changes in land usage or ownership, zoning ordinances, utility district assessments and standby fees, if any, applicable to and enforceable against the above described property, and all valid utility easements created by the dedication deed or plat of the subdivision in which said real property is located, covenants, restrictions common to the platted subdivision in which said real property is located, mineral reservations, maintenance fund liens, and any title or rights asserted by anyone, including, but not limited to, persons, corporations, governments or other entities to tidelands, or lands comprising the shores or beds of navigable or perennial rivers and streams, lakes, bays, gulfs or oceans, or to any land extending from the line of the harbor or bulkhead lines as established or changed by any government or to filled-in lands, or artificial islands, or to riparian rights or other statutory water rights, or the rights or interests of

the State of Texas or the public generally in the area extending from the line of mean low tide to the line of vegetation or the right of access thereto, or right of easement along and across the same, if any, applicable to and enforceable against the above described property as shown by the records of the County Clerk of the County in which said real property is located.

Grantor, for the Consideration and subject to the Reservations from Conveyance and the Exceptions to Conveyance and Warranty, grants, sells, and conveys to Grantee the Property, together with all and singular the rights and appurtenances thereto in any way belonging, to have and to hold it to Grantee and Grantee's heirs, successors, and assigns forever. Grantor binds Grantor and Grantor's heirs and successors to warrant and forever defend all and singular the Property to Grantee and Grantee's heirs, successors, and assigns against every person whomsoever lawfully claiming or to claim the same or any part thereof, except as to the Reservations from Conveyance and the Exceptions to Conveyance and Warranty.

The Vendor's Lien against and Superior Title to the Property are retained until the Note described is fully paid according to its terms, at which time this Deed will become absolute. The Vendor's Lien and Superior Title herein retained are hereby transferred, assigned, sold, and conveyed to the payee of the Note, and the successors and assigns of the payee.

When the context requires, singular nouns and pronouns include the plural.

EXECUTED this 19th day of February, 2025.

Chris Terry

Chris Terry


State of Texas County of Harris **NOTARY ACKNOWLEDGMENT**

Before me, Sabriyah Callis, on this day personally appeared by means of an interactive two-way audio and video communication Chris Terry, who is known to me, or has provided satisfactory evidence of identity in accordance with Chapter 406, Texas Government Code, to be the person whose name is subscribed to the foregoing instrument and acknowledged to me that he/she executed the same for the purposes and consideration therein expressed. This notarial act was an online notarization.

Given under my hand and seal of office this 19th day of February, 2025.

**Notary
Digital Certificate**

Sabriyah Callis



Seal

Electronically signed and notarized online using the Proof platform.

Kevyn Terry

Kevyn Terry a/k/a Kevin Terry

NOTARY ACKNOWLEDGMENT

State of Texas / County of Brazoria


Before me, Marie Ward, on this day personally appeared by means of an interactive two-way audio and video communication Kevyn Terry, who is known to me, or has provided satisfactory evidence of identity in accordance with Chapter 406, Texas Government Code, to be the person whose name is subscribed to the foregoing instrument and acknowledged to me that he/she executed the same for the purposes and consideration therein expressed. This notarial act was an online notarization.

Given under my hand and seal of office this 19th day of February 2025.

**Notary
Digital Certificate**

Marie Ward

Notary Public, State of Texas



Seal

Electronically signed and notarized online using the Proof platform.

**Filed and Recorded
Official Public Records
Bobbie Koepp, County Clerk
Comal County, Texas
02/24/2025 01:04:56 PM
MARY 3 Pages(s)
202506005159**



Bobbie Koepp



COMAL COUNTY

ENGINEER'S OFFICE

OSSF DEVELOPMENT APPLICATION CHECKLIST

Staff will complete shaded items

--	--

Date Received

Initials

118467

Permit Number

Instructions:

Place a check mark next to all items that apply. For items that do not apply, place "N/A". This OSSF Development Application Checklist **must** accompany the completed application.

OSSF Permit

- ☒ Completed Application for Permit for Authorization to Construct an On-Site Sewage Facility and License to Operate
- ☒ Site/Soil Evaluation Completed by a Certified Site Evaluator or a Professional Engineer
- ☒ Planning Materials of the OSSF as Required by the TCEQ Rules for OSSF Chapter 285. Planning Materials shall consist of a scaled design and all system specifications.
- ☒ Required Permit Fee - See Attached Fee Schedule
- ☒ Copy of Recorded Deed
- ☒ Surface Application/Aerobic Treatment System
 - ☒ Recorded Certification of OSSF Requiring Maintenance/Affidavit to the Public
 - ☒ Signed Maintenance Contract with Effective Date as Issuance of License to Operate

I affirm that I have provided all information required for my OSSF Development Application and that this application constitutes a completed OSSF Development Application.

Signature of Applicant

03/12/2025

Date

___ COMPLETE APPLICATION

Check No. _____ Receipt No. _____

INCOMPLETE APPLICATION

___ (Missing Items Circled, Application Refused)
