



# COMAL COUNTY

## ENGINEER'S OFFICE

### License to Operate On-Site Sewage Treatment and Disposal Facility

Issued This Date: 09/23/2019 Permit Number: 109439

Location Description: 80 SUN VALLEY DR  
SPRING BRANCH, TX 78070

Subdivision: Sun Valley Village  
Unit: 2  
Lot: 80  
Block:  
Acreage:

Type of System: Aerobic  
Surface Irrigation

Issued to: Bret S. Johnson & Virginia L. Johnson

This license is authorization for the owner to operate and maintain a private facility at the location described in accordance to the rules and regulations for on-site sewerage facilities of Comal County, Texas, and the Texas Commission on Environmental Quality.

The license grants permission to operate the facility. It does not guarantee successful operation. It is the responsibility of the owner to maintain and operate the facility in a satisfactory manner.

Alterations to this permit including, but not limited to:


- Increase in the square feet of living area
- Increase in the number of bedrooms
- A change of use (i.e. residential to commercial)
- Relocation of system components (including the relocation of spray heads)
- Installation of landscaping
- Adding new structures to the system

may require a new permit. **It is the responsibility of the owner to apply for a new permit, if applicable.**

Inspection and licensing of a facility indicates only that the facility meets certain minimum requirements. It does not impede any governmental entity in taking the proper steps to prevent or control pollution, to abate nuisance, or to protect the public health.

This license to operate is valid for an indefinite period. The holder may transfer it to a succeeding owner, provided the facility has not been remodeled and is functioning properly.

Licensing Authority  
Comal County Environmental Health

  
OS0034792  
ENVIRONMENTAL HEALTH INSPECTOR

  
ENVIRONMENTAL HEALTH COORDINATOR  
OS 0025599

Final

**Comal County Environmental Health  
OSSF Inspection Sheet**

Installer Name: Swoyer OSSF Installer #: \_\_\_\_\_  
 1st Inspection Date: 8/13/19 2nd Inspection Date: \_\_\_\_\_ 3rd Inspection Date: 8-22-19 09-23-19  
 Inspector Name: Mike T. Inspector Name: \_\_\_\_\_ Inspector Name: Mike T. B. Over  
 Permit #: 109439 Address: Sun Valley Village / 80 Sun Valley Dr.

Req.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials	/	285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)		8/13/19		8-22-19
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards	/	285.31(d) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)	/	285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot	/	285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)	/	285.32(a)(5)				
6	PRETREATMENT installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

MT- 8/13/19  
 Tank set, leveled  
 operational ✓  
 Ready for Cover.  
 Replace tight line w/ sch. 40 or SDR 26

8-22-19 BMO  
 Tight line changed  
 covered  
 NO Final NO house

09-23-19 BMO  
 connected

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(E) 285.91(2) 285.32(b)(1)(F) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(ii)(ii) 285.32(b)(1)(E)(ii)(i) 285.32(b)(1)(D) 285.32(b)(1)(C)(ii) 285.32(b)(1)(C)(i) 285.32(b)(1)(B) 285.32(b)(1)(A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed	✓		600	8/13/19		8-20 10
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number	✓		Max Aire	1		1
16	DISPOSAL SYSTEM Absorptive		285.33(a)(1) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(1) 285.33(a)(1) 285.33(a)(2)				

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(b)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(V)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/ Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
	EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling EFFLUENT DISPOSAL SYSTEM Topographic Slopes < 2.0% EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field ( 1000 Linear ft. for 2 bedrooms or Less & an additional 400 ft. for each additional bedroom ) EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. & Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) & Pipe Holes ( 3/16 - 1/4" dia. Hole Size ) 5 ft. Apart		285.33(b)(3)(A) 285.33(b)(3)(A) 285.33(b)(3)(B) 285.91(13) 285.33(b)(3)(D) 285.33(b)(3)(F)				
32	AEROBIC TREATMENT UNIT Is Aerobic Unit Installed According to Approved Guidelines.	✓	285.32(c)(1)		8/13/19		8-29 19
33	AEROBIC TREATMENT UNIT Inspection/Clean Out Port & Risers Provided AEROBIC TREATMENT UNIT Secondary restraint system provided AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions	✓					
34	AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.	✓					
35	PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials & construction PUMP TANK Sampling Port Provided in the Treated Effluent Line PUMP TANK Check Valve and/or Anti-Siphon Device Present When Required PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump						
36	PUMP TANK Inspection/Clean Out Port & Risers Provided PUMP TANK Secondary restraint system provided PUMP TANK Riser permanently fastened to lid or cast into tank PUMP TANK Riser cap protected against unauthorized intrusions						
37	PUMP TANK Secondary restraint system provided						
38	PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried						1
39							

**Comal County Environmental Health  
OSSF Inspection Sheet**

*Final 4/23/19*

No.	Description	Amesas	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?	✓	285.33(d)(2)(G)(iii)(II)285.33(d)(2)(G)(iii)(III)285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)		8/13/18		8-20 19
41	APPLICATION AREA Low Angle Nozzles Used / Pressure is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed	✓	285.33(d)(2)(G)(i) 285.33(d)(2)(A) 285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						

## Comal County Environmental Health OSSF Inspection Sheet

Installer Name: Swoyer OSSF Installer #: \_\_\_\_\_

1st Inspection Date: 8/13/19 2nd Inspection Date: \_\_\_\_\_ 3rd Inspection Date: 8-22-19

Inspector Name: Mike T. Inspector Name: \_\_\_\_\_ Inspector Name: Mike T.

Permit#: 109439 Address: Sun Valley Village / 80 Sun Valley Dr.

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials	✓	285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)		8/13/19		8-22-19
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards	✓	285.31(10) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)	✓	285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot	✓	285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)	✓	285.32(a)(5)				
6	PRETREATMENT installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

MT- 8/13/19  
 Tank set, leveled  
 operational ✓  
 ready for cover.  
 Replace tight line w/ sch. 40 or SDR 26

8-22-19. P.M.O  
 Tight line changed  
 covered  
No Final No house

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(E) 285.91(2) 285.32(b)(1)(F) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(ii)(I) 285.32(b)(1)(E)(f) 285.32(b)(1)(D) 285.32(b)(1)(C)(ii) 285.32(b)(1)(C)(f) 285.32(b)(1)(B) 285.32(b)(1)(A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed	✓		600	8/13/19		8-20 10
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number	✓		Maxxair	/		/
16	DISPOSAL SYSTEM Absorptive		285.33(a)(4) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(3) 285.33(a)(4) 285.33(a)(1) 285.33(a)(2)				



**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(a)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(v)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
	<p>EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling</p> <p>EFFLUENT DISPOSAL SYSTEM Topographic Slopes &lt; 2.0%</p> <p>EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field ( 1000 Linear ft. for 2 bedrooms or Less &amp; an additional 400 ft. for each additional bedroom )</p> <p>EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. &amp; Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully</p> <p>EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) &amp; Pipe Holes ( 3/16 - 1/4" dia. Hole Size ) 5 ft. Apart</p>		<p>285.33(b)(3)(A)</p> <p>285.33(b)(3)(A)</p> <p>285.33(b)(3)(B)</p> <p>285.91(13)</p> <p>285.33(b)(3)(D)</p> <p>285.33(b)(3)(F)</p>				
32	AEROBIC TREATMENT UNIT Is Aerobic Unit installed According to Approved Guidelines.	✓	285.32(c)(1)		8/13/19		8-20 15
33	AEROBIC TREATMENT UNIT Inspection/Clean Out Port & Risers Provided	✓					
	AEROBIC TREATMENT UNIT Secondary restraint system provided	✓					
	AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank	✓					
34	AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions	✓					
35	AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.	✓					
36	PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials & construction						
	PUMP TANK Sampling Port Provided in the Treated Effluent Line						
	PUMP TANK Check Valve and/or Anti-Siphon Device Present When Required						
	PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump						
37	PUMP TANK Inspection/Clean Out Port & Risers Provided						
	PUMP TANK Secondary restraint system provided						
	PUMP TANK Riser permanently fastened to lid or cast into tank						
	PUMP TANK Riser cap protected against unauthorized intrusions						
38	PUMP TANK Secondary restraint system provided						
39	PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried						1

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Address	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?	✓	285.33(d)(2)(G)(iii)(I) 285.33(d)(2)(G)(iii)(II) 285.33(d)(2)(G)(v) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)		8/13/19		8-20 19
41	APPLICATION AREA Low Angle Nozzles Used / Pressure Is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed	✓	285.33(d)(2)(G)(i) 285.33(d)(2)(A) 285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						

## Comal County Environmental Health OSSF Inspection Sheet

Installer Name: Swoyer OSSF Installer #: \_\_\_\_\_

1st Inspection Date: 8/13/19 2nd Inspection Date: \_\_\_\_\_ 3rd Inspection Date: \_\_\_\_\_

Inspector Name: Mike T. Inspector Name: \_\_\_\_\_ Inspector Name: \_\_\_\_\_

Permit#: 109439 Address: Sun Valley Village / 80 Sun Valley Dr.

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials	/	285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)		8/13/19 		
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards	/	285.91(10) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)	/	285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot	/	285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)	/	285.32(a)(5)				
6	PRETREATMENT Installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G)285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

MT- 8/13/19

Tank set, checked  
operational ✓

Ready for Cover.

Replace tight line w/ Sch. 40 or SDR 26

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(E) 285.91(2) 285.32(b)(1)(F) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(ii)(I) 285.32(b)(1)(E)(i) 285.32(b)(1)(D) 285.32(b)(1)(C)(ii) 285.32(b)(1)(C)(i) 285.32(b)(1)(B) 285.32(b)(1)(A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed	✓		600	8/13/19		
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number	✓		Maxxair			
16	DISPOSAL SYSTEM Absorptive		285.33(a)(4) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(3) 285.33(a)(4) 285.33(a)(1) 285.33(a)(2)				

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(a)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(v)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				


**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
32	<p>EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling</p> <p>EFFLUENT DISPOSAL SYSTEM Topographic Slopes &lt; 2.0%</p> <p>EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field ( 1000 Linear ft. for 2 bedrooms or Less &amp; an additional 400 ft. for each additional bedroom )</p> <p>EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. &amp; Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully</p> <p>EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) &amp; Pipe Holes ( 3/16 - 1/4" dia. Hole Size ) 5 ft. Apart</p>		<p>285.33(b)(3)(A)</p> <p>285.33(b)(3)(A)</p> <p>285.33(b)(3)(B)</p> <p>285.91(13)</p> <p>285.33(b)(3)(D)</p> <p>285.33(b)(3)(F)</p>				
33	<p>AEROBIC TREATMENT UNIT Is Aerobic Unit Installed According to Approved Guidelines.</p>	/	285.32(c)(1)		8/13/19		
34	<p>AEROBIC TREATMENT UNIT Inspection/Clean Out Port &amp; Risers Provided</p> <p>AEROBIC TREATMENT UNIT Secondary restraint system provided</p> <p>AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank</p> <p>AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions</p>	/					
35	<p>AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.</p>	/					
36	<p>PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials &amp; construction</p> <p>PUMP TANK Sampling Port Provided in the Treated Effluent Line</p> <p>PUMP TANK Check Valve and/or Anti- Siphon Device Present When Required</p> <p>PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump</p>						
37	<p>PUMP TANK Inspection/Clean Out Port &amp; Risers Provided</p> <p>PUMP TANK Secondary restraint system provided</p> <p>PUMP TANK Riser permanently fastened to lid or cast into tank</p> <p>PUMP TANK Riser cap protected against unauthorized intrusions</p>						
38	<p>PUMP TANK Secondary restraint system provided</p>						
39	<p>PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried</p>						

**Comal County Environmental Health  
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?	✓	285.33(d)(2)(G)(iii)(II)285.33(d)(2)(G)(iii)(III)285.33(d)(2)(G)(v) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)		8/13/18 		
41	APPLICATION AREA Low Angle Nozzles Used / Pressure is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed	✓	285.33(d)(2)(G)(i) 285.33(d)(2)(A) 285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						





# Comal County

OFFICE OF COMAL COUNTY ENGINEER

## **Permit of Authorization to Construct an On-Site Sewage Facility Permit Valid For One Year From Date Issued**

Permit Number: 109439  
Issued This Date: 07/30/2019  
This permit is hereby given to: Bret S. Johnson & Virginia L. Johnson

To start construction of a private, on-site sewage facility located at:

80 SUN VALLEY DR  
SPRING BRANCH, TX 78070

Subdivision: Sun Valley Village  
Unit: 2  
Lot: 80  
Block:  
Acreage:

APPROVED MINIMUM SIZES AS PER ATTACHED DESIGN

Type of System: Aerobic  
Surface Irrigation

This permit gives permission for the construction of the above referenced on-site facility to commence. Installation must be completed by an installer holding a valid registration card from the Texas Commission on Environmental Quality (TCEQ). Installation and inspection must comply with current TCEQ and Comal County requirements.

Call (830) 608-2090 to schedule inspections.

OSSF DEVELOPMENT APPLICATION CHECKLIST

Staff will complete shaded

Items	Date Received
	Initials

Permit Number

Instructions:


Place a check mark next to all items that apply. For items that do not apply, place "N/A". This OSSF Development Application Checklist **must** accompany the completed application.

OSSF Permit

- Completed Application for Permit for Authorization to Construct an On-Site Sewage Facility and License to Operate
- Site/Soil Evaluation Completed by a Certified Site Evaluator or a Professional Engineer
- Planning Materials of the OSSF as Required by the TCEQ Rules for OSSF Chapter 285. Planning Materials shall consist of a scaled design and all system specifications.
- Required Permit Fee
- Copy of Recorded Deed
- Surface Application/Aerobic Treatment System
  - Recorded Certification of OSSF Requiring Maintenance/Affidavit to the Public
  - Signed Maintenance Contract with Effective Date as Issuance of License to Operate

I affirm that I have provided all information required for my OSSF Development Application and that this application constitutes a completed OSSF Development Application.

  
 \_\_\_\_\_  
 Signature of Applicant

  
 \_\_\_\_\_  
 Date

___ COMPLETE APPLICATION	
Check No. _____	Receipt No. _____

___ INCOMPLETE APPLICATION
(Missing Items Circled, Application Refused)

\* \* \* COMAL COUNTY OFFICE OF ENVIRONMENTAL HEALTH \* \* \*  
APPLICATION FOR PERMIT FOR AUTHORIZATION TO CONSTRUCT AN  
ON-SITE SEWAGE FACILITY AND LICENSE TO OPERATE

Date \_\_\_\_\_

Permit # 109439

Owner Name	<u>BRET S. JOHNSON &amp; VIRGINIA L. JOHNSON</u>	Agent Name	<u>FRANK AGUIRRE</u>
Mailing Address	<u>c/o 23011 FM 306</u>	Agent Address	<u>16159 OLD STABLE ROAD</u>
City, State, Zip	<u>CANYON LAKE, TX 78133</u>	City, State, Zip	<u>SAN ANTONIO, TX 78247</u>
Phone #	<u>830-935-4936</u>	Phone #	<u>210-275-7866</u>
Email	<u>katelyn@paulswoyerseptics.com</u>	Email	<u>frankseptic45@gmail.com</u>

All correspondence should be sent to:  Owner  Agent  Both      Method:  Mail  Email

Subdivision Name SUN VALLEY VILLAGE      Unit 2      Lot 80      Block \_\_\_\_\_

Acreage/Legal \_\_\_\_\_

Street Name/Address 80 SUN VALLEY DRIVE      City SPRING BRANCH      Zip 78070

**Type of Development:**

Single Family Residential

Type of Construction (House, Mobile, RV, Etc.) MOBILE

Number of Bedrooms 4

Indicate Sq Ft of Living Area 1972

RECEIVED

JUL 19 2019

COUNTY ENGINEER

Non-Single Family Residential

(Planning materials must show adequate land area for doubling the required land needed for treatment units and disposal area)

Type of Facility \_\_\_\_\_

Offices, Factories, Churches, Schools, Parks, Etc. - Indicate Number Of Occupants \_\_\_\_\_

Restaurants, Lounges, Theaters - Indicate Number of Seats \_\_\_\_\_

Hotel, Motel, Hospital, Nursing Home - Indicate Number of Beds \_\_\_\_\_

Travel Trailer/RV Parks - Indicate Number of Spaces \_\_\_\_\_

Miscellaneous \_\_\_\_\_

Estimated Cost of Construction: \$ 170,000 (Structure Only)

Is any portion of the proposed OSSF located in the United States Army Corps of Engineers (USACE) flowage easement?

Yes  No (If yes, owner must provide approval from USACE for proposed OSSF improvements within the USACE flowage easement)

Source of Water  Public  Private Well

Are Water Saving Devices Being Utilized Within the Residence?  Yes  No

By signing this application, I certify that:

- The completed application and all additional information submitted does not contain any false information and does not conceal any material facts.

- Authorization is hereby given to the permitting authority and designated agents to enter upon the above described property for the purpose of site/soil evaluation and inspection of private sewage facilities..

- I understand that a permit of authorization to construct will not be issued until the Floodplain Administrator has performed the reviews required by the Comal County Flood Damage Prevention Order.

- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

Signature of Owner

Date

Page 1 of 2

\*\*\* COMAL COUNTY OFFICE OF ENVIRONMENTAL HEALTH \*\*\*  
APPLICATION FOR PERMIT FOR AUTHORIZATION TO CONSTRUCT AN  
ON-SITE SEWAGE FACILITY AND LICENSE TO OPERATE

Planning Materials & Site Evaluation as Required Completed By FRANK A. BUJORE

System Description ATU w/ SPENY

Size of Septic System Required Based on Planning Materials & Soil Evaluation

Tank Size(s) (Gallons) 1000 Absorption/Application Area (Sq Ft) 4985

Gallons Per Day (As Per TCEQ Table III) 300

(Sites generating more than 5000 gallons per day are required to obtain a permit through TCEQ.)

Is the property located over the Edwards Recharge Zone?  Yes  No  
(If yes, the planning materials must be completed by a Registered Sanitarian (R.S.) or Professional Engineer (P.E.))

Is there an existing TCEQ approved WPAP for the property?  Yes  No  
(If yes, the R.S. or P.E. shall certify that the OSSF design complies with all provisions of the existing WPAP.)

If there is no existing WPAP, does the proposed development activity require a TCEQ approved WPAP?  Yes  No  
(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed WPAP. A Permit to Construct will not be issued for the proposed OSSF until the proposed WPAP has been approved by the appropriate regional office.)

Is the property located over the Edwards Contributing Zone?  Yes  No

Is there an existing TCEQ approval CZP for the property?  Yes  No  
(If yes, the P.E. or R.S. shall certify that the OSSF design complies with all provisions of the existing CZP.)

If there is no existing CZP, does the proposed development activity require a TCEQ approved CZP?  Yes  No  
(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed CZP. A Permit to Construct will not be issued for the proposed OSSF until the CZP has been approved by the appropriate regional office.)

Is this property within an incorporated city?  Yes  No

If yes, indicate the city: \_\_\_\_\_

By signing this application, I certify that:

- The information provided above is true and correct to the best of my knowledge.
- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

Frank A. Bujore  
Signature of Designer

19 JULY 12  
Date

Yes

**AFFIDAVIT**



201906023837 07/11/2019 01:20:39 PM 1/1

**THE COUNTY OF COMAL  
STATE OF TEXAS**

**CERTIFICATION OF OSSF REQUIRING MAINTENANCE**

According to Texas Commission on Environmental Quality Rules for On-Site Sewage Facilities (OSSF's), this document is filed in the Deed Records of Comal County, Texas.

**I**

The Texas Health and Safety Code, Chapter 366 authorizes the Texas Commission on Environmental Quality (TCEQ) to regulate on-site sewage facilities (OSSFs). Additionally, the Texas Water Code (TWC), § 5.012 and § 5.013, gives the commission primary responsibility for implementing the laws of the State of Texas relating to water and adopting rules necessary to carry out its powers and duties under the TWC. The commission, under the authority of the TWC and the Texas Health and Safety code, requires owner's to provide notice to the public that certain types of OSSFs are located on specific pieces of property. To achieve this notice, the commission requires a recorded affidavit. Additionally, the owner must provide proof of the recording to the OSSF permitting authority. This recorded affidavit is not a representation or warranty by the commission of the suitability of this OSSF, nor does it constitute any guarantee by the commission that the appropriate OSSF was installed.

**II**

An OSSF requiring a maintenance contract, according to 30 Texas Administrative Code §285.91(12) will be installed on the property described as **(insert legal description):**

2 UNIT/PHASE/SECTION \_\_\_\_\_ BLOCK 80 LOT \_\_\_\_\_ SUN VALLEY VILLAGE \_\_\_\_\_ SUBDIVISION

IF NOT IN SUBDIVISION: \_\_\_\_\_ ACREAGE \_\_\_\_\_ SURVEY

The property is owned by **(insert owner's full name):** BRET S. JOHNSON & VIRGINIA L. JOHNSON

This OSSF must be covered by a continuous maintenance contract for the first two years. After the initial two-year service policy, the owner of an aerobic treatment system for a single family residence shall either obtain a maintenance contract within 30 days or maintain the system personally.

Upon sale or transfer of the above-described property, the permit for the OSSF shall be transferred to the buyer or new owner. A copy of the planning materials for the OSSF can be obtained from the Comal County Engineer's Office.

RECEIVED  
JUL 19 2019  
COUNTY ENGINEER

WITNESS BY HAND(S) ON THIS 9 DAY OF June, 2019

X [Signature]

BRET S. JOHNSON

X [Signature]

VIRGINIA L. JOHNSON


Owner(s) signature(s)

Owner (s) Printed name (s)

Bret & Virginia  
June, 2019

SWORN TO AND SUBSCRIBED BEFORE ME ON THIS 9 DAY OF

[Signature]  
Notary Public Signature



(Notary Seal Here)

THIS AREA FOR COMAL COUNTY CLERK RECORDING PURPOSES ONLY

Filed and Recorded  
Official Public Records  
Bobbie Koepf, County Clerk  
Comal County, Texas  
07/11/2019 01:20:39 PM  
TERRI 1 Page(s)  
201906023837



Bobbie Koepf



PAUL SWOYER SEPTIC SUPPLY & SERVICE

23011 FM 306  
CANYON LAKE, TX 78133

RECEIVED  
JUL 19 2019

COUNTY ENGINEER

MP#0001708

CHRISTOPHER RYAN SEIDENSTICKER

**PROPERTY LEGAL DESCRIPTION:**

SUN VALLEY VILLAGE, UNIT 2, LOT 80

**Customer:** BRET S. JOHNSON & VIRGINIA L. JOHNSON

**Site Address:** 80 SUN VALLEY DRIVE

**City/State:** SPRING BRANCH, TX

**Zip:** 78070

**County:** COMAL

**Permit#:** \_\_\_\_\_

**Phone Number:** \_\_\_\_\_

**E-mail:** \_\_\_\_\_

**I. General:** This On-Site Sewage Facility Service Agreement (hereinafter referred to as "Agreement") is entered into by and between BRET S. JOHNSON & VIRGINIA L. JOHNSON, (hereinafter referred to as "Client") and PS Supply & Service LLC. (hereinafter referred to as "Contractor"). By this agreement, Contractor agrees to render services, as described herein (the "Services"), and the client agrees to fulfill his/her/their responsibilities under this agreement herein.

**II. Effective Dates:** This agreement commences on the date of License to Operate is issued for Three (3) years.

Date of License to Operate: LTO Last Date of Service: 3 yrs from LTO

**III. Services by Contractor:** Contractor will provide the following Services:

1. Inspect and perform routine maintenance on the On-Site Sewage Facility ("OSSF") in compliance with the code, regulations, and/or rules of the Texas Commission on Environmental Quality ("TCEQ") and county in which the OSSF is located (the "County") and the manufacturer's requirements, at a frequency of approximately once every four (4) months.
2. Report to the appropriate regulatory authority and to Client, as required by the State of Texas' on-site rules and, if required, TCEQ or County rules. All findings must be reported to the appropriate regulatory authority within 14 days.
3. Notify Client and repair any components of the OSSF that are found to be in need of repair during the inspection. If warranty, you just do it. If not, Client will be responsible. Repairs will be made so brought up to compliance and bill forward.
4. Visit site in response to Client's request for unscheduled service within two business days from the date of Contractor's actual receipt of Client's request. Unscheduled service visits are not included in the fee agreement herein and will be billed to the client in addition to fees under this Agreement.
5. Provide notification of arrival to site to the Client or to site personnel. Additionally, Contractor will leave written notification of the visit at the site or with site personnel upon completion of inspection, and forward such notice to the appropriate regulatory authority within fourteen (14) days.

**IV. Payment(s):** Client shall pay to Contractor included w/ septic, for the Services describe herein (the "Inspection and Routine Maintenance Fee"), excepting those described in Section III (4), or Section IX, herein. The Fee does not include equipment, parts or labor supplied for anything beyond routine inspection and routine maintenance. Payments for such additional services are due at the time services are provided or rendered. Payments not received within thirty (30) days from the due date will be subject the greater of a \$20.00 late penalty or 1.5% carrying charge on the original balance for each month or portion thereof a balance in past due. If for any reason such charges are found to be usurious by a court of competent jurisdiction, such charges shall be reduced to the maximum allowable by law. By signing this contract, Client authorizes Contractor to remove any parts installed, but not paid in full at the end of the thirty (30) days. Client agrees to pay for any labor cost associated with the installation and the reasonable cost of removal of said parts.

Client: [Signature]

Contractor: [Signature]

RECEIVED

JUL 19 2019

**V. Client's Responsibilities:** Client is responsible for each and all of the following:

1. To maintain chlorinator and provide proper chlorine supply, if OSSF is so equipped.
2. To provide all necessary yard or lawn maintenance and removal of obstacles as needed to allow the OSSF to function properly, and to allow Contractor ready access to all parts of the OSSF.
3. To maintain a current license to operate, and abide by the conditions and limitations of that license and all requirements for on-site sewage facilities from the State and local regulatory agency.
4. To maintain the OSSF in accordance with manufacturer's recommendations.
5. To immediately notify Contractor and Agency of any and all problems with, the OSSF, including failure thereof.
6. Upon receipt of any written notification of required services from Contractor, to contact Contractor and authorize the required service. If Client elects a different contractor to perform the required service, Client is responsible for ensuring the substitute contractor holds the proper license (Installer II) and is certified by the manufacturer. Additionally, Client shall be responsible for ensuring proper notification is given to the appropriate regulatory authority, as required by the State and/or local regulatory authority rules.
7. To provide Contractor with water usage records, upon request, for evaluation by Contractor of the OSSF performance.
8. To pay required sampling charges for samples collected for testing (e.g. Biological Oxygen Demand/Total Suspended Solids ("BOD/TSS") that may be required on the OSSF.
9. To prevent backwash from water treatment or water conditioning equipment to enter the OSSF.
10. To provide, at Client's expense, for pumping of tanks as needed.
11. To maintain site drainage sufficient to prevent adverse effects on the OSSF.
12. To promptly and fully pay Contractor's bills, fees, or invoices as described herein.

**VI. Access by Contractor:** Client agrees to allow Contractor, or personnel authorized by the Contractor, to enter the property at reasonable times without prior notice for the purpose of performing the Services described herein. Such entry shall include access to the OSSF electrical and physical components, including tanks, by means of manways or risers for the purpose of evaluations required by the manufacturer, and/or regulatory authority rules. If such manways or risers are not in place, Client shall allow and be responsible for payment of required excavation, including labor and materials, necessary to allow access to the OSSF or any required components. Such excavation shall be billed at the rate of \$75.00 per hour for labor, plus materials billed at list price. Contractor shall make only those efforts reasonable under the circumstances to replace excavated soil.

**VII. Application or Transfer of Payment:** The fees paid for this agreement may transfer to any subsequent owner(s) of the property on which the OSSF is located. The subsequent owner(s) must sign a similar agreement authorizing Contractor to perform the above-described Services, and accepting Client's responsibilities. The replacement Agreement must be signed and received within 30 days of transfer of ownership. Contractor will apply all funds received from Client first to any past due obligations arising from this Agreement including late charges, return check charges, and charges for repairs or services not paid within 30 days of invoicing. The consumption of the payment in this manner may lead to termination of the agreement by Contractor

**VIII. Termination of Agreement:** This agreement may be terminated by either party with 30 days written notice. If this agreement is so terminated by Client, Contractor shall be paid at the rate of \$75.00 per hour for any worked performed or required, but not yet paid. If terminated by Contractor, all amounts outstanding shall be due within thirty days of termination. The party terminating will immediately notify the other party, the equipment manufacturer, and the regulatory agency of the termination.

**IX. Limitation of Liability:** In no event shall Contractor be liable for indirect, consequential, incidental or punitive damages, whether in contract, tort, or any other theory of liability. In no event shall the Contractor's liability for direct damages exceed payments by the Client under this Agreement.

**X. Severability and Reformation:** If any provision in this Agreement shall be held to be invalid or unenforceable for any reason, it shall be reformed to the minimum extent necessary to effect the intent of the Parties. If any provision is such that it cannot reasonably be reformed, it shall be struck from this Agreement and the remaining provisions shall continue to be valid and enforceable.

**XI. Performance of Agreement:** Commencement of performance by Contractor under this agreement is contingent on the following conditions: (1) Contractor receiving a fully executed original copy of this agreement. (2) Contractor receiving payment in full of the fee(s) described herein. If the above conditions are not met, then Contractor is from any obligation to perform any portion of this agreement.

**XII. Modification.** This Agreement may not be changed or modified except by an instrument in writing, signed by both Contractor and Client.

**XIII. Waiver.** Except as otherwise noted in this Agreement, the waiver by other party of a breach of any provision of this Agreement shall not operate or be construed as a continuing waiver or as a consent to or waiver of any subsequent breach hereof.

Client: 

Contractor: 

RECEIVED

JUL 19 2019

XIV. **Headings.** The Article and Section headings in this Agreement are for the convenience of reference only and do not constitute a part of this Agreement and shall not be deemed to limit or affect any of the provisions hereof.

XV. **GOVERNING LAW AND CHOICE OF VENUE.** EACH OF THE PARTIES HERETO HEREBY CONSENTS TO THE EXCLUSIVE JURISDICTION OF THE COURTS OF THE STATE OF TEXAS, COUNTY OF COMAL, AND TO THE UNITED STATES DISTRICT COURT FOR THE WESTERN DISTRICT OF TEXAS - SAN ANTONIO DIVISION, AS WELL AS TO THE JURISDICTION OF ALL COURTS TO WHICH AN APPEAL MAY BE TAKEN FROM SUCH COURTS, FOR THE PURPOSE OF ANY SUIT, ACTION, OR OTHER PROCEEDING ARISING OUT OF, OR IN CONNECTION WITH, THIS AGREEMENT OR ANY OF THE TRANSACTIONS CONTEMPLATED HEREBY, INCLUDING, WITHOUT LIMITATION, ANY PROCEEDING RELATING TO ANCILLARY MEASURES IN AID OF ARBITRATION, PROVISIONAL REMEDIES AND INTERIM RELIEF, OR ANY PROCEEDING TO ENFORCE ANY ARBITRAL DECISION OR AWARD. EACH PARTY HERETO EXPRESSLY WAIVES ANY AND ALL RIGHTS TO BRING ANY SUIT, ACTION, OR OTHER PROCEEDING IN OR BEFORE ANY COURT OR TRIBUNAL OTHER THAN COURTS OF THE STATE OF TEXAS, COUNTY OF COMAL, AND COVENANTS THAT IT SHALL NOT SEEK IN ANY MANNER TO PROSECUTE OR DEFEND ANY DISPUTE OTHER THAN AS SET FORTH IN THIS ARTICLE XVI OR TO CHALLENGE OR SET ASIDE ANY DECISION, AWARD, OR JUDGMENT OBTAINED IN ACCORDANCE WITH THE PROVISIONS HEREOF. EACH OF THE PARTIES HERETO HEREBY EXPRESSLY WAIVES ANY AND ALL OBJECTIONS IT MAY HAVE TO VENUE, INCLUDING, WITHOUT LIMITATION, THE INCONVENIENCE OF SUCH FORUM, IN ANY OF SUCH COURTS.

ENGINEER

XVI. **JURY TRIAL WAIVER.** THE PARTIES HEREBY UNCONDITIONALLY WAIVE THEIR RIGHT TO A JURY TRIAL OF ANY AND ALL CLAIMS OR CAUSES OF ACTION ARISING FROM OR RELATING TO THEIR RELATIONSHIP. THE PARTIES ACKNOWLEDGE THAT A RIGHT TO A JURY IS A CONSTITUTIONAL RIGHT, THAT THEY HAVE HAD AN OPPORTUNITY TO CONSULT WITH INDEPENDENT COUNSEL, AND THAT THIS JURY WAIVER HAS BEEN ENTERED INTO KNOWINGLY AND VOLUNTARILY BY ALL PARTIES TO THIS AGREEMENT. IN THE EVENT OF LITIGATION, THIS AGREEMENT MAY BE FILED AS A WRITTEN CONSENT TO A TRIAL BY THE COURT.

MP#0001708

CHRISTOPHER RYAN SEIDENSTICKER

Approved by Contractor:

Approved by Client:

XVII. **Reservation of Rights.** Contractor reserves all rights not specifically granted herein.

XVIII. **Counterparts.** This Agreement may be executed in one or more counterparts, each of which shall be deemed to be an original but all of which together will constitute one and the same instrument.

XIX. **Counsel.** Contractor has previously recommended that Client engage counsel to assist him/her/it in reviewing this Agreement and all other matters relating to it. Contractor and Client shall each bear his/her/its own costs and expenses in connection with the negotiation and documentation of this Agreement.

XX. **Entire Agreement:** This agreement contains the entire agreement of the parties, and there are no promises or conditions in any other agreement, oral or written. The Parties expressly disclaim reliance on any prior statements, oral or written, by either party not expressly provided for herein.

Client:

Contractor:







Property deed: See attached  
Maintenance agreement: See attached  
ATU affidavit: See attached

Site evaluation:

Applicant/site:

Name: Bret and Virginia Johnson

Location: 80 Sun Valley Dr.

Date: 12 July 2019

Site Evaluator:

Frank Aguirre, 16159 Old Stable Rd., San Antonio, Texas 78247; Lic # 30400, 2/20

SOIL BORING NUMBER 1

Depth (Feet)	Texture Class	Soil Texture	Structure (For Class III-Blocky, platy or massive)	Drainage (Medium/ Water Table)	Restrictive Horizon	Observations
0		Limestone			Restrictive Class <u>IV</u>	
1						
2						
3						
4						
5						

RECEIVED

JUL 19 2019

6034

SOIL BORING NUMBER 2

Depth (Feet)	Texture Class	Soil Texture	Structure (For Class III-Blocky, platy or massive)	Drainage (Medium/ Water Table)	Restrictive Horizon	Observations
0			Restrictive Class <u>IV</u>			
1						
2						
3						
4						
5						



16159 Old Stable Rd.  
Frank Aguirre, R.S.

San Antonio, Texas 78247-4490  
210.275.7866

[frankseptic45@gmail.com](mailto:frankseptic45@gmail.com)

REPAIR OF PERMIT #34355, issued in 1975

PLANNING MATERIALS FOR A SEPTIC SYSTEM IN COMAL COUNTY *Frank Aguirre*

DATE, FIELD WORK: 12 July 2019

THE PLAYERS:

Property owner: Bret S. & Virginia L. Johnson, c/o Paul Swoyer, 18382 FM 306, Suite #101, Canyon Lake TX 78133; 830-935-4936; [katelin@paulswoyerseptics.com](mailto:katelin@paulswoyerseptics.com)

Site Evaluator: Frank Aguirre, SE, #10807

Designer: Frank Aguirre, R.S., Lic. 994

Installer: Paul Swoyer, 830-935-4936

Septic system design review & inspections: Comal County: Brenda Ritzen or Sandra Hernandez, 830.608.2090

THE PROPERTY:

Street numerical address: 80 Sun Valley

Legal description: Lot 80, Unit 2, Sun Valley Village

Contributing zone: The property is on the Contributing zone and the septic system design complies with all the provisions of the existing CZP.

THE PROPOSED PROJECT:

A single family residence, 4 BR, 1972 SF

THE ESTIMATED SEWAGE PRODUCTION CHARACTERISTICS:

Hydraulic loading estimated at 300 gpd, sized, by regulations, to a 4 BR home.

Organic loading estimated at 140 to 300 mg/l BOD with traces of FOG and TSS (residential strength)

DESCRIPTION OF PROPOSED MONITORING OF SEWAGE CHARACTERISTICS:

Hydraulic loading as the major portion of the water meter reading.

TARGET FINAL EFFLUENT PARAMETERS:

Hydraulic loading less than the estimated loading on ANY GIVEN DAY.

Organic loading: BOD and TSS of less than 65 mg/l

WATER SOURCE: CLWS

SITE EVALUATION DATA:

A. This certifies that proper soil analysis procedures were followed.

RECEIVED

JUL 19 2019

COUNTY ENGINEER

- B. Soils at this site are Class IV and are not suitable with respect to texture.  
 C. The overall site suitability is not appropriate for a Standard on-site wastewater system.

**OVERALL SEPTIC SYSTEM COMPONENTS:**

**Collection:** (It is crucial that all sewer drops exiting this home/building be as shallow as possible, still meeting elevation plumbing requirements in the slab. This design assumes a shallow sewer drop exit.) About 10' of tightline from the house to the ATU with a cleanout within 3' of the house. *Sink Again*

**Pre-treatment:** Single compartment (trash) tank in front of the ATU

**Treatment:** 600 gpd MAXX AIR ATU (aerobic treatment unit) with disinfection

The system to be installed must be done so in **STRICT ACCORDANCE WITH ALL MANUFACTURER'S RECOMMENDATIONS** by a Class II septic system installer.

**Water pump requirements:** Must overcome an elevation head of 6', a friction head of 8' and a maximum head at the spray head of 45' for a total head of 59'. It shall operate the spray heads at two application times (operated by a control box using a timer) - 12 midnight and 4 am cycles of 150 gal. each cycle. At 12 gpm, each cycle shall run for 13 minutes.

RECEIVED

**Supply line size:** 1"

**Sprayheads:** K-rain 1303 RCW or equal

JUL 19 2019

**Recycling:** The required spray area for this size of residence is 4688 SF.

The actual spray shall be 4983 SF and shall consist of three 23' full circle sprays at 4 gpm for a total of 12 gpm.

The spray area shall be covered with grasses, evergreen shrubs, bushes, trees or landscaped beds containing mixed vegetation.

**Float Switch Placements**

Actual liquid measurements:

60" depth, 60" length, 60" width, dividing by 12 to go to "feet":

5' depth, 5' length, 5' width

Capacity, in CF, = 5' x 5' x 5' = 125 CF X 7.48 gal/CF = 935 gal (Actual tank capacity)

935 gal = 15.58 gal/inch

60" depth *Sink Again*

Volume needed for a single dose = 300 gal/2 = 150 gal.

150 gal = 10" needed between the "Off" and "On" switches

15.58 gal/in

Volume needed between the "On" and "Alarm" switches = 1 day's volume = 300 gal

$\frac{300 \text{ gal}}{15.58 \text{ gal/in}} = 20''$  needed between the "On" and "Alarm" switches

Volume required above the "alarm" switch = 1/3 day's volume = 100 gal.

$\frac{100 \text{ gal.}}{15.58 \text{ gal/in}} = 7''$  needed above the "alarm" switch

Locations of float switches:

Distance between the OFF and ON switches = 10"  
 + Distance between the ON and Alarm switches = 20"  
 + Distance between the Alarm switch and Inlet = 7"

Minimum working depth required = 37"

Actual working depth available = 60"

+Min. height needed above floor of tank for the OFF switch = 8"

Minimum tank depth from Inlet to bottom of tank = 45"

RECEIVED

JUL 19 2019

COUNTY ENGINEER

#### CODE COMPLIANCE

*Everyone realizes that the QUALITY of sewage from a restaurant is more to treat than that from a residence, because of the presence of FOG - fats, oils and greases. But not enough attention is given to the fact that HOME sewage can also include high FOG contents from cosmetics, bath oils, suntan lotion, etc. in addition to cooking greases and food scraps. Medications taken by persons living in the home, bleaches and non-eaten plastics and paper can also play havoc with the septic system.*

*Technical note: Home sewage should have no higher than 60 mg/l in Total Suspended Solids, 20 mg/l in FOG and 300 mg/l in BOD. Exceeding any of these limits can cause serious damage and malfunction to the septic system, in addition to that causes my more VOLUME of sewage than that for which the system was designed.* *Jim Regin*

*Aerobic Treatment Units (ATU's) must be approved by the TCEQ and installed, managed, monitored and maintained in accordance with manufacturer's recommendations. All wiring and piping must be in accordance with Ch. 285, septic system regulations, as a MINIMUM.*

*It is not within the scope of this document to cite all the engineering and construction standards that apply to this project. This is a PERFORMANCE design that is modeled to meet...*

1. *All septic regulations of the Texas Commission On Environment Quality, Chap. 285, version of 28 Dec 2012, and*
2. *All construction standards that are generally accepted with the septic system industry, and*
3. *All requirements as stated by the local inspection jurisdiction in which the property sits.*

**BEST PRACTICES**


It is the opinion of this designer that both state and local jurisdiction requirements represent **MINIMUM** government regulations that may or may not result in a septic system that meets the property owner's **EXPECTATIONS** of it providing dependable, long-lasting service. Therefore, the property owner should consider some of the many **UPGRADES** that are available from the **INDUSTRY** and the **MANUFACTURER'S** side of the project.

As part of the "best practices" thrust, **ALL** septic systems of all types can deliver long-lasting, dependable service **IF and ONLY IF** the owner of the system includes these three items:

- Management** - The sewage that is sent to the system must be within both its quantitative and qualitative design limits.
- Monitoring** - Every system must be closely watched for any signs of failure. The best monitoring includes specific measurements of its various characteristics.
- Maintenance** - The system must be properly maintained on a regularly scheduled basis by a qualified and licensed person.

**Chemical characteristics:** The parameters of typical residential-strength sewage are: BOD-140, TSS - 75, FOG - 15, DO - .5, pH - 7 and temp 59.

**Cross-section of a Maxx Air ATU:** *Sink Again*

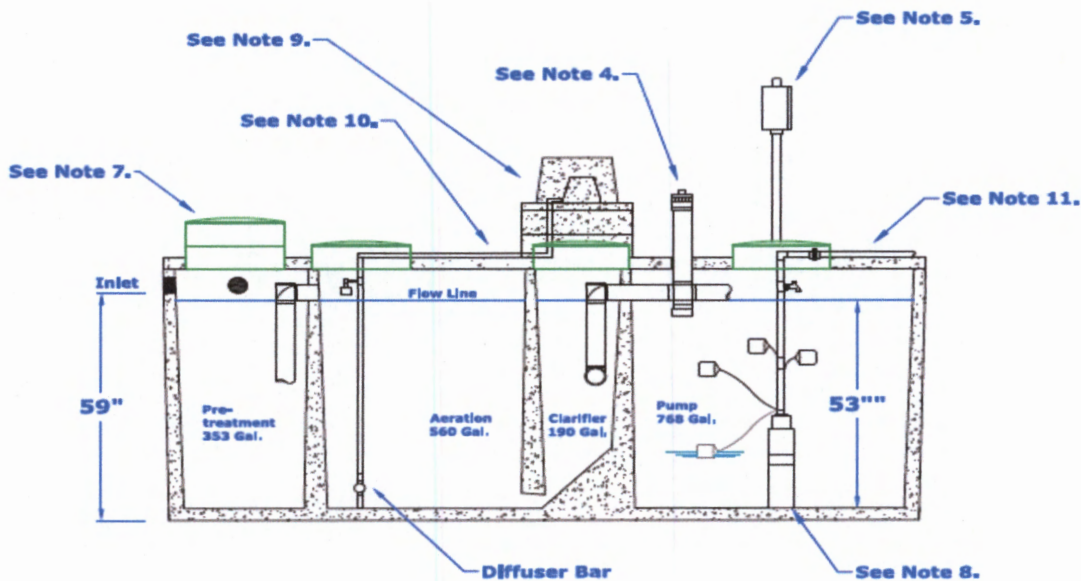

**Maxx Air M-600 (600 GPD)  
Aerobic Treatment Plant (Assembled)**

Dec. 2013  
By: A.S.

**Scale:**


\* All dimensions subject to alternate specification tolerances.

Dwg. #: ADV-B550-3

It is the owner's responsibility to ensure that the aerobic treatment unit is under a PAID contract with a licensed "maintenance provider. The unit must be checked and tested ONCE EVERY 4 MONTHS [Regulation #285.91 (4)] for the life of the unit and test results shall be submitted to the local septic inspector.

I hereby certify that this design conforms to both TCEQ and local regulations for On-Site Sewage Facilities and, with proper use, maintenance, and under normal climatic conditions, can be expected to function without creating a nuisance.

Sincerely,




Frank Aguirre, Registered Sanitarian, Lic. 994, Site Evaluator, Lic. 10807, TCEQ Designated Representative Lic.30400, NAWT Certified Inspector, Lic. 13671TC  
Location:

RECEIVED

JUL 19 2019

COUNTY ENGINEER

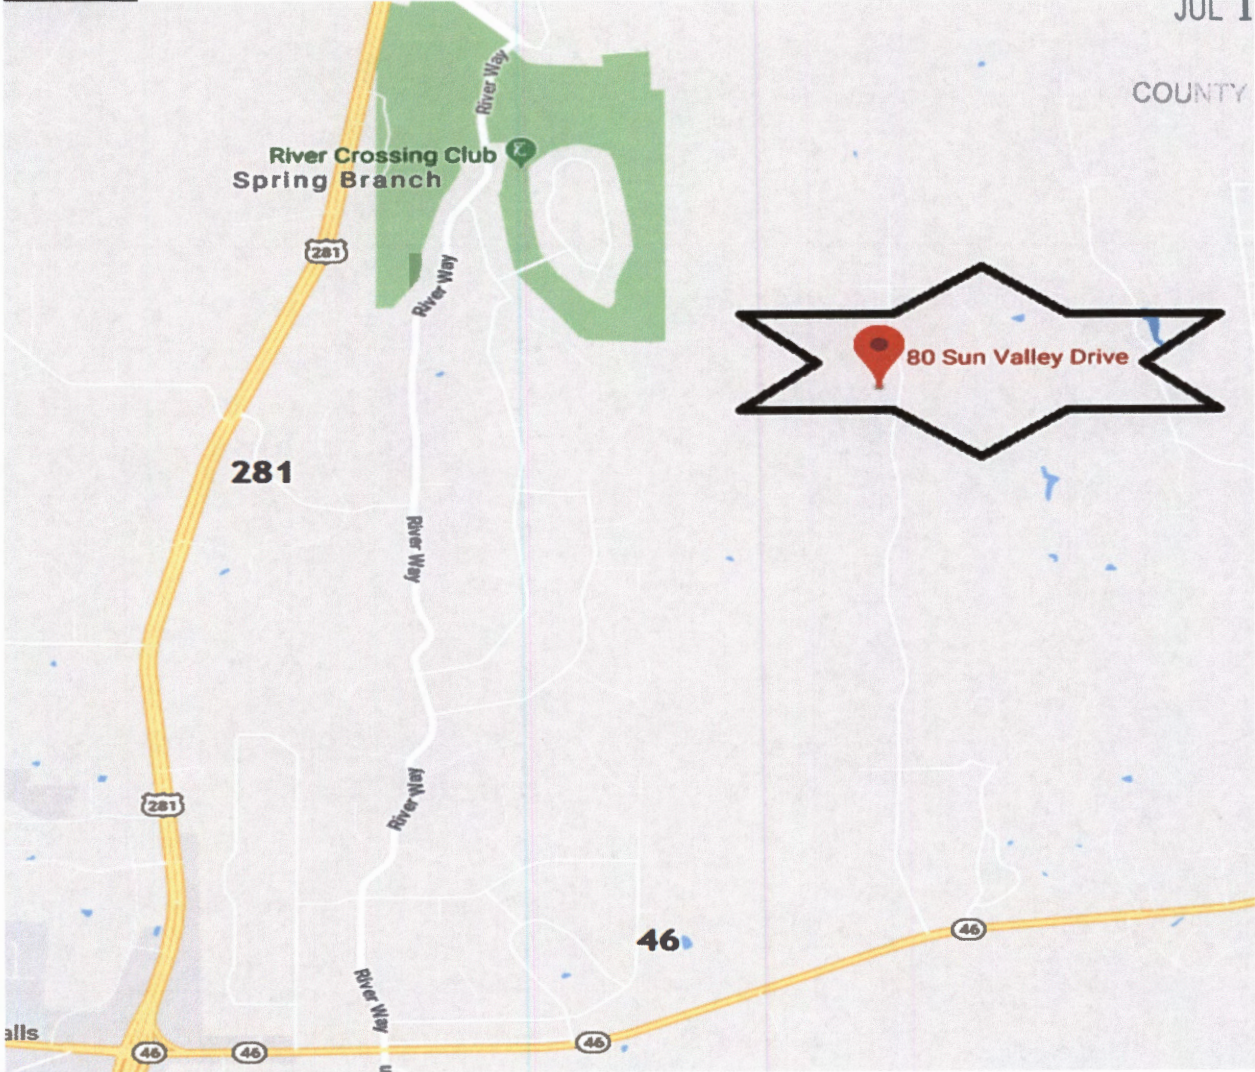

## Ritzen, Brenda

---

**From:** Frank Aguirre <frankseptic45@gmail.com>  
**Sent:** Tuesday, July 30, 2019 10:30 AM  
**To:** Ritzen, Brenda  
**Subject:** Re: Permit 109439

The current (old) pvc pipe will be removed and replaced with a new, Sch. 40 pipe.

No sleeving is required in 285 that I know of.

The existing home will be removed and replaced with a new one. The sizes shown reflect the new one.

Let me know if if you need anything else.

thanx,

f

On Tue, Jul 30, 2019 at 10:05 AM Ritzen, Brenda <[rabbjr@co.comal.tx.us](mailto:rabbjr@co.comal.tx.us)> wrote:

Frank,

Please indicate if the concrete wall will have any impact on the sewer pipe? Will the sewer pipe be sleeved as per 285? Also, will the other improvements/structures be removed?

Thank you,

Brenda Ritzen, OS0007722

Environmental Health Coordinator

Comal County Engineers Office

195 David Jonas Drive


New Braunfels, Texas 78132

830-608-2090

[www.cceo.org](http://www.cceo.org)




1" = 60'  
3.692 Acres



**Septic Systems Express**  
DBA of Frank Aguirre and Associates, Inc.

Note: No RV is connected to the system; the garage includes no additional plumbing.

JOHNSON PROPERTY  
12 JULY 2019  
(Revision of 30 July 2019)

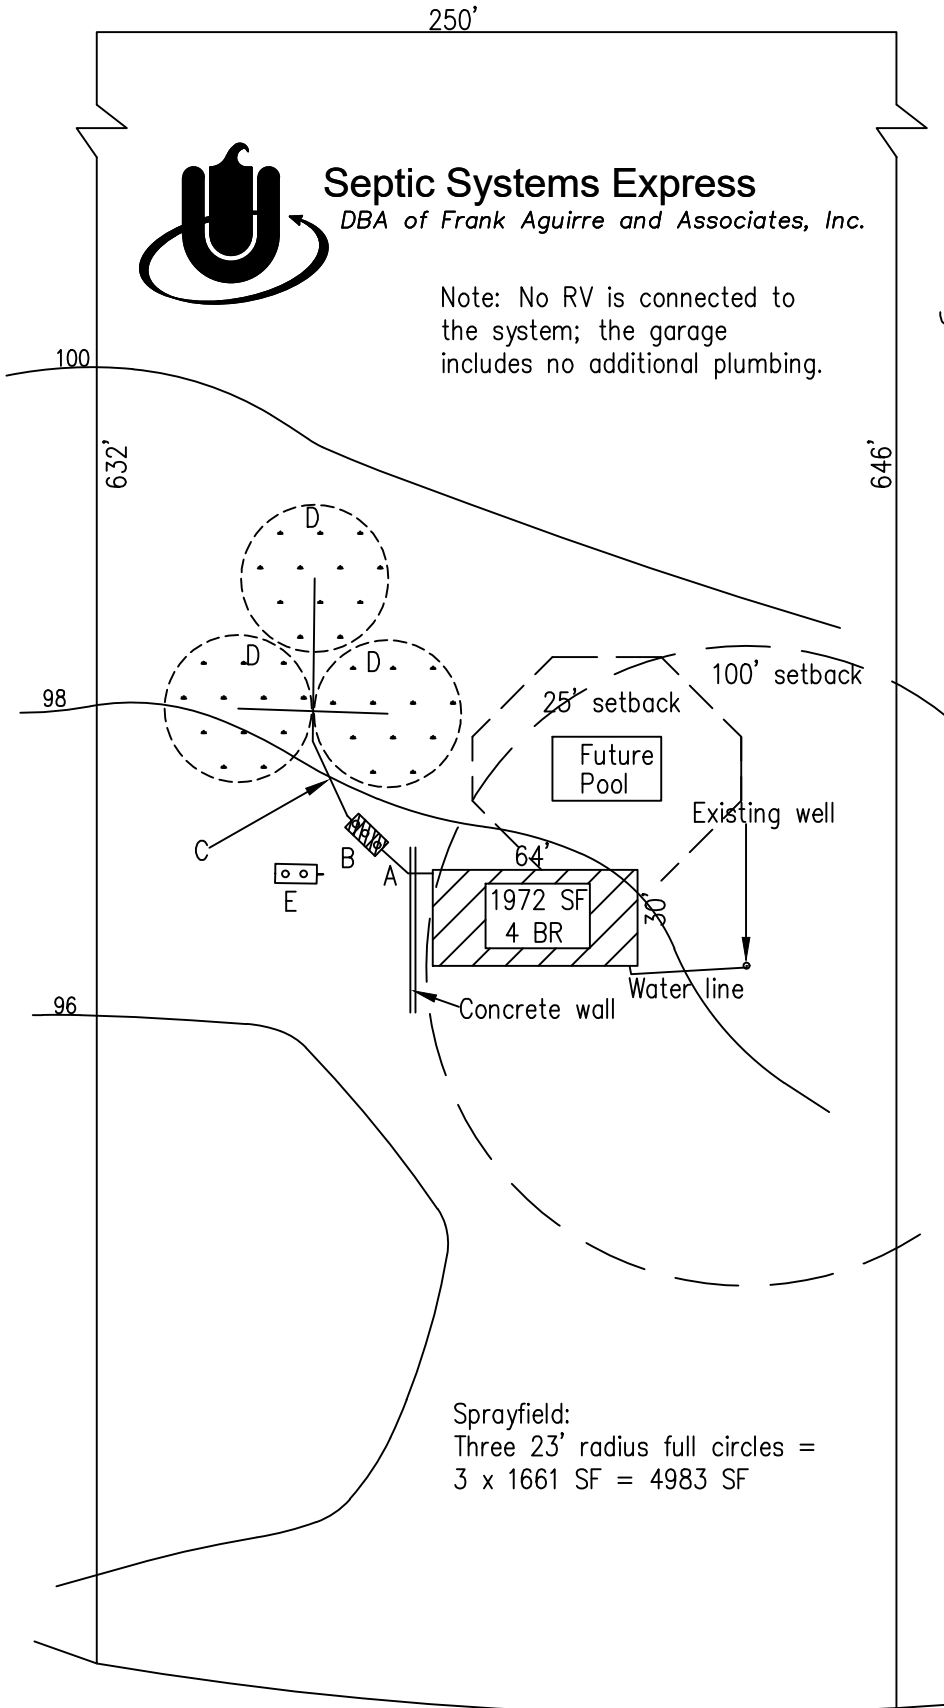

- A = ± 15' of 4" pvc, Sch. 40, tightline from the house to the new tank, with a cleanout within 3' of the house
- B = Pre-treatment tank, 600 gpd MAXX AIR aerobic, chlorinator and pump tank
- C = ± 100' of 1' pvc supply line
- D = 23' radius full circle spray
- E = Old septic tank to be pumped and filled in with soil

Sprayfield:  
Three 23' radius full circles =  
3 x 1661 SF = 4983 SF

*Frank Aguirre*



RS 994  
OS10807  
DR 30400  
L-80,U-2,SunValleyVillage

80 SUN VALLEY DR.

Note: The contractor may make field adjustments to the system so as to better fit specific site conditions. All angles, lengths and locations shown are approximate and are adjustable during the actual system installation.



## Ritzen, Brenda

---

**From:** Ritzen, Brenda  
**Sent:** Tuesday, July 30, 2019 10:05 AM  
**To:** 'Frank Aguirre'  
**Cc:** Katelyn Neumann  
**Subject:** RE: Permit 109439

Frank,

Please indicate if the concrete wall will have any impact on the sewer pipe? Will the sewer pipe be sleeved as per 285? Also, will the other improvements/structures be removed?

Thank you,

Brenda Ritzen, OS0007722  
Environmental Health Coordinator  
Comal County Engineers Office  
195 David Jonas Drive  
New Braunfels, Texas 78132  
830-608-2090  
[www.cceo.org](http://www.cceo.org)

**From:** Frank Aguirre <[frankseptic45@gmail.com](mailto:frankseptic45@gmail.com)>  
**Sent:** Tuesday, July 30, 2019 9:56 AM  
**To:** Ritzen, Brenda <[rabbjr@co.comal.tx.us](mailto:rabbjr@co.comal.tx.us)>  
**Cc:** Katelyn Neumann <[katelyn@paulswoyerseptics.com](mailto:katelyn@paulswoyerseptics.com)>  
**Subject:** Re: Permit 109439

Here you go, Brenda!  
frank

On Tue, Jul 30, 2019 at 9:36 AM Ritzen, Brenda <[rabbjr@co.comal.tx.us](mailto:rabbjr@co.comal.tx.us)> wrote:

Re: Bret S. Johnson & Virginia L. Johnson

Sun Valley Village Unit 2 Lot 80

Application for Permit for Authorization to Construct an On-Site Sewage Facility

Katelyn & Frank,

The following information is needed before I can continue processing the referenced permit submittal:

## Ritzen, Brenda

---

**From:** Ritzen, Brenda  
**Sent:** Tuesday, July 30, 2019 9:36 AM  
**To:** 'Katelyn Neumann'  
**Cc:** 'Frank Aguirre'  
**Subject:** Permit 109439

Re: Bret S. Johnson & Virginia L. Johnson  
Sun Valley Village Unit 2 Lot 80  
Application for Permit for Authorization to Construct an On-Site Sewage Facility

Katelyn & Frank,

The following information is needed before I can continue processing the referenced permit submittal:

1. The aerial view shows a swimming pool, RV, and an addition or garage. If these improvements will remain they must be incorporated into the planning materials. Revise as needed and resubmit.

Thank you,

Brenda Ritzen, OS0007722  
Environmental Health Coordinator  
Comal County Engineers Office  
195 David Jonas Drive  
New Braunfels, Texas 78132  
830-608-2090  
[www.cceo.org](http://www.cceo.org)

250'  
**VOID**



**Septic Systems Express**  
DBA of Frank Aguirre and Associates, Inc.




1" = 60'  
3.692 Acres

RECEIVED  
JUL 19 2019

COUNTY ENGINEER

JOHNSON PROPERTY  
12 JULY 2019

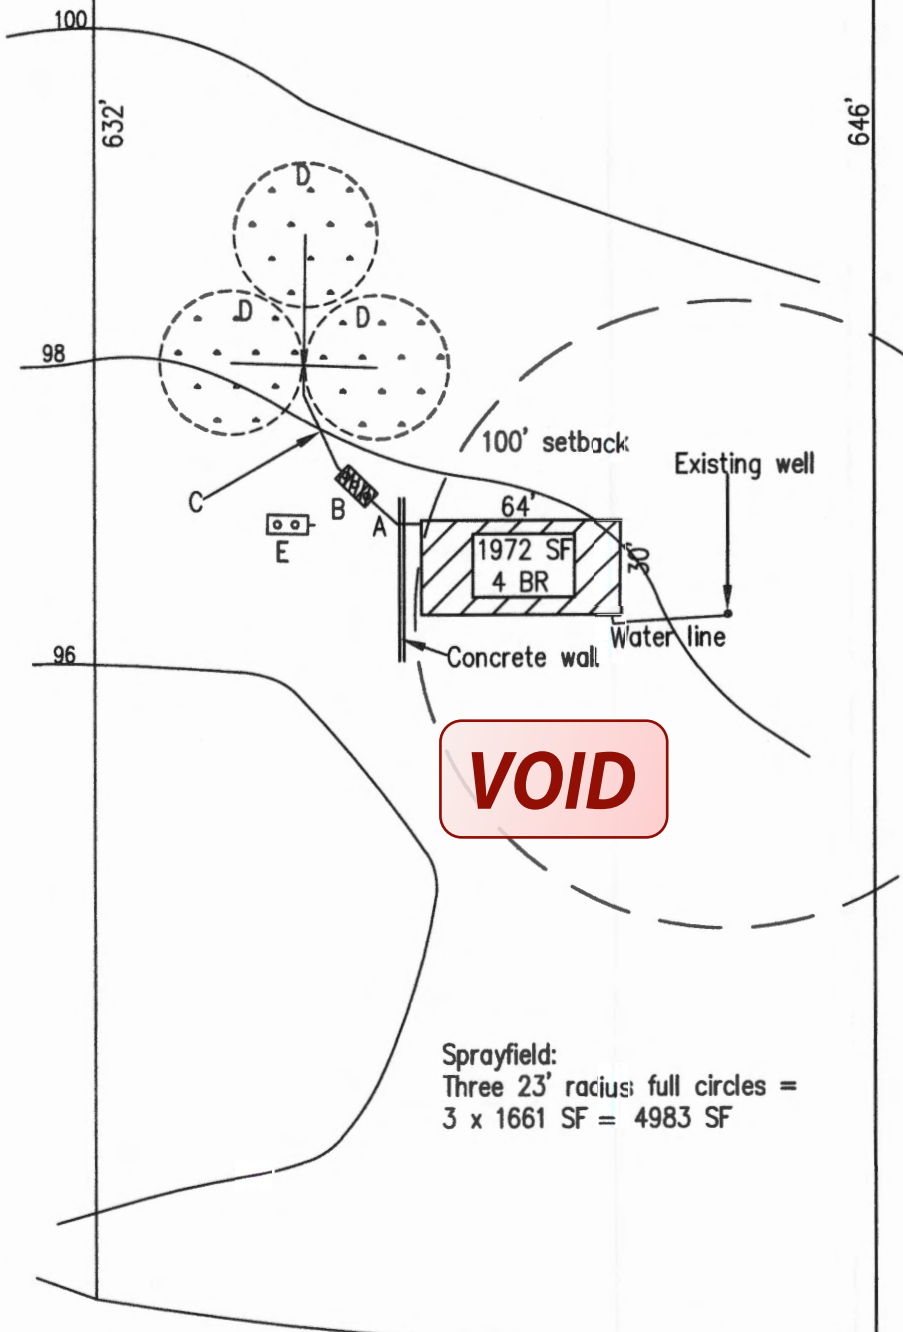

- A = ± 15' of 4" pvc, Sch. 40, tightline from the house to the new tank, with a cleanout within 3' of the house
- B = Pre-treatment tank, 600 gpd MAXX AIR aerobic, chlorinator and pump tank
- C = ± 100' of 1' pvc supply line
- D = 23' radius full circle spray
- E = Old septic tank to be pumped and filled in with soil

**VOID**

Sprayfield:  
Three 23' radius full circles =  
3 x 1661 SF = 4983 SF

*Frank Aguirre*



RS 994  
OS10807  
DR 30400  
L-80,U-2,SunValleyVillage


80 SUN VALLEY DR.

Note: The contractor may make field adjustments to the system so as to better fit specific site conditions. All angles, lengths and locations shown are approximate and are adjustable during the actual system installation.

Flood zone/Aquifer map: *Link Origin*



Property plat:

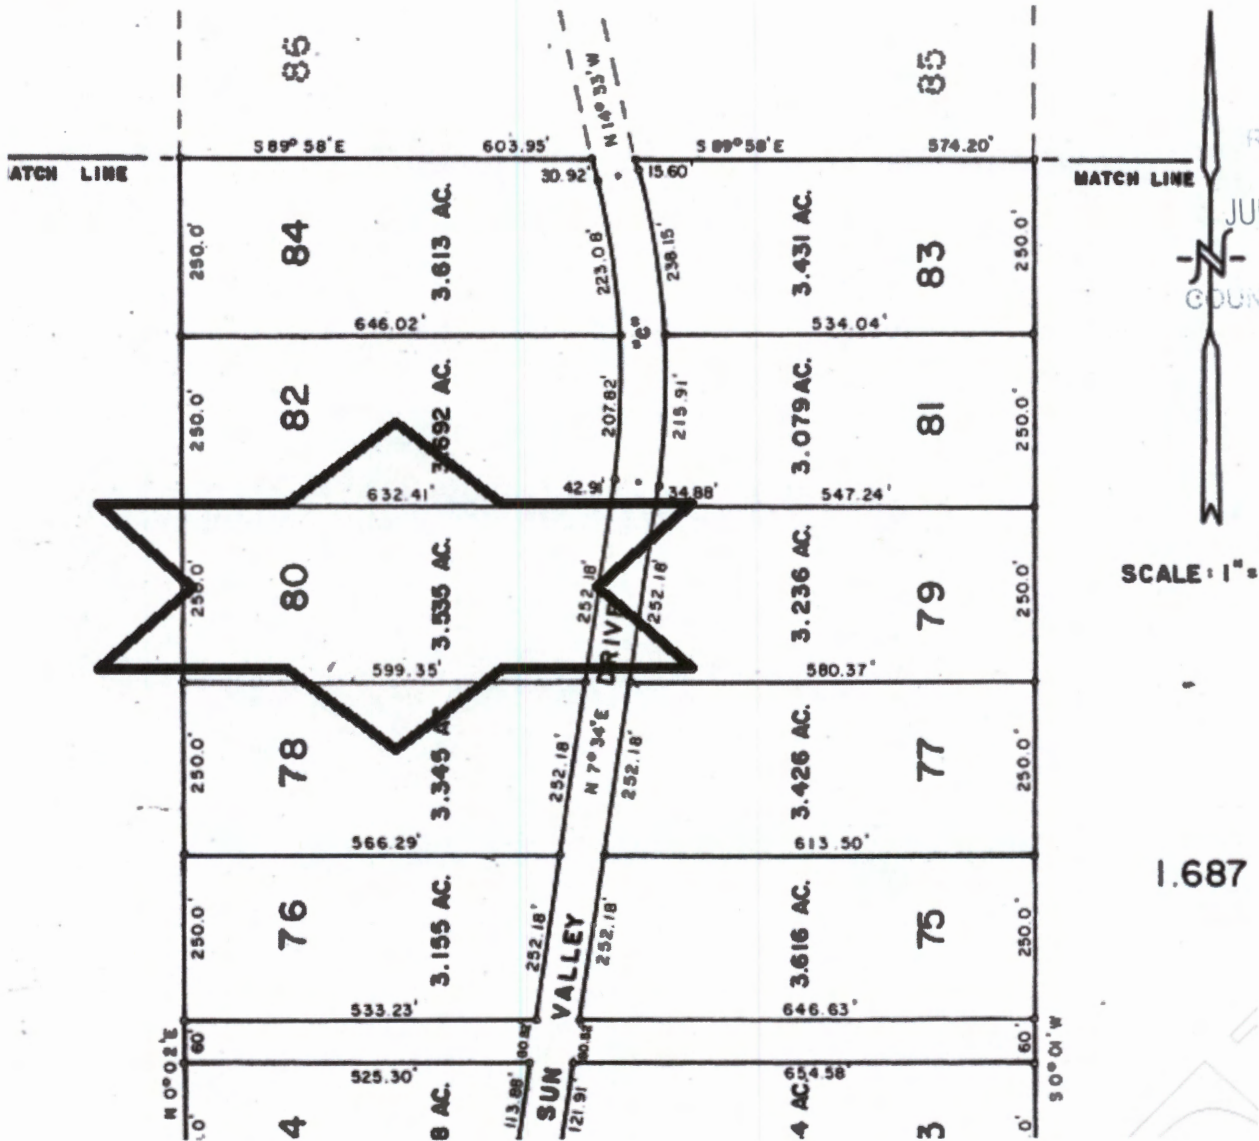

High head pump graph:


RECEIVED

JUL 19 2019


COUNTY ENGINEER

# High Head Filtered Effluent Pumps


½, ¾, 1 and 1½ HP  
8, 12, 20, 25, and 35 GPM  
4" Diameter Submersibles

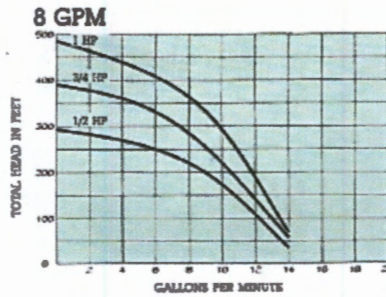


HP	Voltage	Pump Model
½	115	2NFL51-8E
½	230	2NFL52-8E
¾	230	2NFL72-8E
1	230	2NFL102-8E




HP	Voltage	Pump Model
½	115	2NFL51-20E
½	230	2NFL52-20E
¾	230	2NFL72-20E
1	230	2NFL102-20E
1½	230	2NFL152-20E



HP	Voltage	Pump Model
½	115	2NFL51-12E
½	230	2NFL52-12E
¾	230	2NFL72-12E
1	230	2NFL102-12E



HP	Voltage	Pump Model
1	230	J1025BE
1½	230	J1525BE



HP	Voltage	Pump Model
1	230	J1035BE
1½	230	J1535BE

**NOTICE OF CONFIDENTIALITY RIGHTS. IF YOU ARE A NATURAL PERSON, YOU MAY REMOVE OR STRIKE ANY OR ALL OF THE FOLLOWING INFORMATION FROM ANY INSTRUMENT THAT TRANSFERS AN INTEREST IN REAL PROPERTY BEFORE IT IS FILED FOR RECORD IN THE PUBLIC RECORDS: YOUR SOCIAL SECURITY NUMBER OR YOUR DRIVER'S LICENSE NUMBER.**

**GENERAL WARRANTY DEED**

STATE OF TEXAS

§  
§  
§

KNOW ALL MEN BY THESE PRESENTS: 19 2019

COUNTY OF COMAL

RECEIVED

COUNTY ENGINEER

Date: May 2, 2017

Grantor: DAVID L. PARKER and wife, LALONNIE S. PARKER

Grantor's Mailing Address:

P.O. Box 97  
Hot Springs, AR 71902  
COMAL County

Grantee: BRET S. JOHNSON and VIRGINIA L. JOHNSON

Grantee's Mailing Address:

919 Rustic Cactus  
San Antonio, Texas 78260  
Bexar County

Consideration:

TEN AND NO/100 DOLLARS (\$10.00) and other good and valuable consideration.

Property (including any improvements):

Lot 80, Sun Valley Village, Unit Two, according to the map or plat thereof recorded in Volume 4, Pages 38-39 of the Map and Plat Records of Comal County, Texas.

Reservations from Conveyance: None.

Exceptions to Conveyance and Warranty:

This conveyance is made and accepted subject to conditions, restrictions, reservations, declarations, exceptions, easement grants, set-backs, assessments, maintenance and/or association charges and ordinances, affecting the property conveyed, if any, appearing in the public records; and all leases, grants, exceptions or reservations of coal, lignite, oil, gas and other minerals, if any, together with all rights, privileges, and immunities relating thereto, appearing in the Public Records; and standby fees, taxes, and assessments by any taxing authority for the year 2017 and subsequent years, and subsequent taxes and assessments by any taxing authority for prior years due to change in land usage or ownership.

Grantee, by its acceptance hereof, agrees to be solely responsible for payment of all ad valorem taxes pertaining to the Property for the calendar year 2017 and subsequent years.

Grantor, for the Consideration and subject to the Reservations from Conveyance and the Exceptions to Conveyance and Warranty, GRANTS, SELLS, AND CONVEYS to Grantee the Property, together with all and singular the rights and appurtenances thereto in any way belonging, to have and to hold it to Grantee and Grantee's heirs, successors, and assigns forever. Grantor binds Grantor and Grantor's heirs and successors to WARRANT AND FOREVER DEFEND all and singular the Property to Grantee and Grantee's heirs, successors, and assigns against every person whomsoever lawfully claiming or to claim the same or any part thereof, except as to the Reservations from Conveyance and the Exceptions to Conveyance and Warranty.

When the context requires, singular nouns and pronouns include the plural.

[signature(s) on following page(s)]

UNOFFICIAL

Executed effective as of the date first set forth herein.

**GRANTOR:**

David L. Parker  
DAVID L. PARKER

Lalonnie S. Parker  
LALONNIE S. PARKER


RECEIVED  
JUL 19 2019

COUNTY ENGINEER

STATE OF Ark §  
COUNTY OF Garland §

This instrument was acknowledged before me on 1. May 2, 2017, by DAVID L. PARKER, an individual.


Lindsey Henderson  
Notary Public, State of Ark



STATE OF Ark §  
COUNTY OF Garland §

This instrument was acknowledged before me on May 2, 2017, by LALONNIE S. PARKER, an individual.

Lindsey Henderson  
Notary Public, State of Ark



Filed and Recorded  
Official Public Records  
Bobbie Koepf, County Clerk  
Comal County, Texas  
05/05/2017 03:12:49 PM  
LAURA 3 Pages(s)  
201706023761



*Bobbie Koepf*

**AFTER RECORDING RETURN TO:**

BRET S. JOHNSON and VIRGINIA L. JOHNSON  
919 Rustic Cactus  
San Antonio, Texas 78260

After Recording Return to:  
Alamo Title Company  
494 South Seguin St., Ste 100  
New Braunfels, TX 78130



**PS Septic Supply & Service**  
**23011 FM 306**  
**Canyon Lake, TX 78133**

(830) 850-0080  
 Fax: (830) 935-4932

**Permit #: 109439**

**To: Paul Swoyer Septics, LLC**  
**80 Sun Valley Drive**  
**Spring Branch, TX 78070**

Tech: Not Assigned  
 Brand/Mfg.: MAXX AIR -  
 System S/N:  
 Aerator and S/N:

Site: 80 Sun Valley Drive, Spring Branch  
 Agency: Comal County  
 County:  
 Subdivision: Sun Valley Village

Installed:  
 Phone:  
 Cell:  
 Work:

Contract: 9/23/2019 - 9/23/2022  
 Inspections per year: 3  
 Service Due: 1/23/2020  
 Alt Phone:  
 Warranty Ending:

Inspection Type: \_\_\_\_\_ Inspection # \_\_\_\_\_ of \_\_\_\_\_ for the contract year

Item	Operational	Inoperative	N/A
Aerator:	_____	_____	_____
Irrigation pump:	_____	_____	_____
Air compressor:	_____	_____	_____
Disinfection device:	_____	_____	_____
Chlorine supply:	_____	_____	_____
Spray field vegetation:	_____	_____	_____
Sprinkler / Drip backwash:	_____	_____	_____
Photocell Test:	_____	_____	_____
Autodialer:	_____	_____	_____
Water Meter Reading: _____ CFM: _____ PSI: _____			

Test Results and observations: (As Required)

Fecal Coliform: \_\_\_\_\_  
 Chlorine Residual: \_\_\_\_\_  
 Test Method: \_\_\_\_\_  
 BOD: \_\_\_\_\_  
 TSS: \_\_\_\_\_  
 Commercial Lab: \_\_\_\_\_  
 Date Submitted: \_\_\_\_\_

Repairs made: Y / N

Repairs and Comments:

*Gate locked, NO Good Contact #*

Inspector: \_\_\_\_\_ Date: \_\_\_\_\_

*29. 829822*  
*98. 386705*

Area: / 0  
 GPS: 29.8303 -98.3865 ID = 1352

Printed: 1/21/2020

80 Sun Valley Drive, Spring Branch

**PS Septic Supply & Service**  
**23011 FM 306**  
**Canyon Lake, TX 78133**

(830) 850-0080  
 Fax: (830) 935-4932

**Permit #: 109439**

**To: Home Owner**  
**80 Sun Valley Drive**  
**Spring Branch, TX 78070**

Tech: Not Assigned  
 Brand/Mfg: MAXX AIR -  
 System S/N:  
 Aerator and S/N:

Site: 80 Sun Valley Drive, Spring Branch  
 Agency: Comal County  
 County:  
 Subdivision: Sun Valley Village

Installed:  
 Phone:  
 Cell:  
 Work:  
 Contract 9/23/2019 - 9/23/2022  
 Inspections per year: 3  
 Service Due: 5/23/2020  
 Alt Phone:  
 Warranty Ending:

Inspection Type: \_\_\_\_\_ Inspection # \_\_\_\_\_ of \_\_\_\_\_ for the contract year

Item	Operational	Inoperative	N/A
Aerator:	_____	_____	_____
Irrigation pump:	_____	_____	_____
Air compressor:	_____	_____	_____
Disinfection device:	_____	_____	_____
Chlorine supply:	_____	_____	_____
Spray field vegetation:	_____	_____	_____
Sprinkler / Drip backwash:	_____	_____	_____
Photocell Test:	_____	_____	_____
Autodialer:	_____	_____	_____
Water Meter Reading: _____ CFM: _____ PSI: _____			

Test Results and observations: (As Required)  
 Fecal Coliform: \_\_\_\_\_  
 Chlorine Residual: \_\_\_\_\_  
 Test Method: \_\_\_\_\_  
 BOD: \_\_\_\_\_  
 TSS: \_\_\_\_\_  
 Commercial Lab: \_\_\_\_\_  
 Date Submitted: \_\_\_\_\_

Repairs made: Y / N

Repairs and Comments:  
 \_\_\_\_\_  
 \_\_\_\_\_ *Have NO phone number or gate code*  
 \_\_\_\_\_ *NO access*

Inspector: *[Signature]* Date: \_\_\_\_\_

Area: 10 Printed: 5/26/2020  
 GPS: 29.829822 -98.3867 ID = 1352

80 Sun Valley Drive, Spring Branch



PAUL SWOYER SEPTIC SUPPLY &  
SERVICE

23011 FM 306

CANYON LAKE, TX 78133

MP#0001708

CHRISTOPHER RYAN SEIDENSTICKER

PROPERTY LEGAL DESCRIPTION:

Customer: Bret Johnson

Site Address: 80 Sun Valley Dr.

City/State: Spring Branch, TX zip: 78070

County: Comal Permit#: 109439

Phone Number: (210) 834-0320

E-mail: bretj30@gmail.com

I. General: This On-Site Sewage Facility Service Agreement (hereinafter referred to as "Agreement") is entered into by and between \_\_\_\_\_, (hereinafter referred to as "Client") and PS Supply & Service LLC (hereinafter referred to as "Contractor"). By this agreement, Contractor agrees to render services, as described herein (the "Services"), and the client agrees to fulfill his/her their responsibilities under this agreement herein

II. Effective Dates: This agreement commences on the date of License to Operate is issued for Three (3) years

Date of License to Operate: 3.22.21 Last Date of Service 3.22.23

III. Services by Contractor: Contractor will provide the following Services

1. Inspect and perform routine maintenance on the On-Site Sewage Facility ("OSSF") in compliance with the code, regulations, and/or rules of the Texas Commission on Environmental Quality ("TCEQ") and county in which the OSSF is located (the "County") and the manufacturer's requirements, at a frequency of approximately once every four (4) months.
2. Report to the appropriate regulatory authority and to Client, as required by the State of Texas' on-site rules and, if required, TCEQ or County rules. All findings must be reported to the appropriate regulatory authority within 14 days
3. Notify Client and repair any components of the OSSF that are found to be in need of repair during the inspection. If warranty, you just do it. If not, Client will be responsible. Repairs will be made so brought up to compliance and bill forward
4. Visit site in response to Client's request for unscheduled service within two business days from the date of Contractor's actual receipt of Client's request. Unscheduled service visits are not included in the fee agreement herein and will be billed to the client in addition to fees under this Agreement
5. Provide notification of arrival to site to the Client or to site personnel. Additionally, Contractor will leave written notification of the visit at the site or with site personnel upon completion of inspection, and forward such notice to the appropriate regulatory authority within fourteen (14) days.

IV. Payment(s): Client shall pay to Contractor included w/ install for the Services describe herein (the "Inspection and Routine Maintenance Fee"), excepting those described in Section III (4), or Section IX, herein. The Fee does not include equipment, parts or labor supplied for anything beyond routine inspection and routine maintenance. Payments for such additional services are due at the time services are provided or rendered. Payments not received within thirty (30) days from the due date will be subject the greater of a \$20.00 late penalty or 1.5% carrying charge on the original balance for each month or portion thereof a balance in past due. If for any reason such charges are found to be usurious by a court of competent jurisdiction, such charges shall be reduced to the maximum allowable by law. By signing this contract, Client authorizes Contractor to remove any parts installed, but not paid in full at the end of the thirty (30) days. Client agrees to pay for any labor cost associated with the installation and the reasonable cost of removal of said parts.

Client: BJ

Contractor: \_\_\_\_\_

**V. Client's Responsibilities:** Client is responsible for each and all of the following

- 1 To maintain chlorinator and provide proper chlorine supply, if OSSF is so equipped.
- 2 To provide all necessary yard or lawn maintenance and removal of obstacles as needed to allow the OSSF to function properly, and to allow Contractor ready access to all parts of the OSSF
- 3 To maintain a current license to operate, and abide by the conditions and limitations of that license and all requirements for on-site sewage facilities from the State and local regulatory agency
- 4 To maintain the OSSF in accordance with manufacturer's recommendations.
- 5 To immediately notify Contractor and Agency of any and all problems with, the OSSF, including failure thereof.
- 6 Upon receipt of any written notification of required services from Contractor, to contact Contractor and authorize the required service. If Client elects a different contractor to perform the required service, Client is responsible for ensuring the substitute contractor holds the proper license (Installer II) and is certified by the manufacturer. Additionally, Client shall be responsible for ensuring proper notification is given to the appropriate regulatory authority, as required by the State and/or local regulatory authority rules
- 7 To provide Contractor with water usage records, upon request, for evaluation by Contractor of the OSSF performance.
- 8 To pay required sampling charges for samples collected for testing (e.g. Biological Oxygen Demand/Total Suspended Solids ("BOD/TSS")) that may be required on the OSSF.
- 9 To prevent backwash from water treatment or water conditioning equipment to enter the OSSF.
- 10 To provide, at Client's expense, for pumping of tanks as needed
- 11 To maintain site drainage sufficient to prevent adverse effects on the OSSF.
- 12 To promptly and fully pay Contractor's bills, fees, or invoices as described herein.

**VI. Access by Contractor:** Client agrees to allow Contractor, or personnel authorized by the Contractor, to enter the property at reasonable times without prior notice for the purpose of performing the Services described herein. Such entry shall include access to the OSSF electrical and physical components, including tanks, by means of manways or risers for the purpose of evaluations required by the manufacturer, and/or regulatory authority rules. If such manways or risers are not in place, Client shall allow and be responsible for payment of required excavation, including labor and materials, necessary to allow access to the OSSF or any required components. Such excavation shall be billed at the rate of \$75.00 per hour for labor, plus materials billed at list price. Contractor shall make only those efforts reasonable under the circumstances to replace excavated soil.

**VII. Application or Transfer of Payment:** The fees paid for this agreement may transfer to any subsequent owner(s) of the property on which the OSSF is located. The subsequent owner(s) must sign a similar agreement authorizing Contractor to perform the above-described Services, and accepting Client's responsibilities. The replacement Agreement must be signed and received within 30 days of transfer of ownership. Contractor will apply all funds received from Client first to any past due obligations arising from this Agreement including late charges, return check charges, and charges for repairs or services not paid within 30 days of invoicing. The consumption of the payment in this manner may lead to termination of the agreement by Contractor.

**VIII. Termination of Agreement:** This agreement may be terminated by either party with 30 days written notice. If this agreement is so terminated by Client, Contractor shall be paid at the rate of \$75.00 per hour for any worked performed or required, but not yet paid. If terminated by Contractor, all amounts outstanding shall be due within thirty days of termination. The party terminating will immediately notify the other party, the equipment manufacturer, and the regulatory agency of the termination.

**IX. Limitation of Liability:** In no event shall Contractor be liable for indirect, consequential, incidental or punitive damages, whether in contract, tort, or any other theory of liability. In no event shall the Contractor's liability for direct damages exceed payments by the Client under this Agreement.

**X. Severability and Reformation:** If any provision in this Agreement shall be held to be invalid or unenforceable for any reason, it shall be reformed to the minimum extent necessary to effect the intent of the Parties. If any provision is such that it cannot reasonably be reformed, it shall be struck from this Agreement and the remaining provisions shall continue to be valid and enforceable.

**XI. Performance of Agreement:** Commencement of performance by Contractor under this agreement is contingent on the following conditions: (1) Contractor receiving a fully executed original copy of this agreement (2) Contractor receiving payment in full of the fee(s) described herein. If the above conditions are not met, then Contractor is from any obligation to perform any portion of this agreement.

**XII. Modification.** This Agreement may not be changed or modified except by an instrument in writing, signed by both Contractor and Client.

**XIII. Waiver.** Except as otherwise noted in this Agreement, the waiver by other party of a breach of any provision of this Agreement shall not operate or be construed as a continuing waiver or as a consent to or waiver of any subsequent breach hereof.

Client BJ

Contractor KS

**XIV. Headings** The Article and Section headings in this Agreement are for the convenience of reference only and do not constitute a part of this Agreement and shall not be deemed to limit or affect any of the provisions hereof.

**XV. GOVERNING LAW AND CHOICE OF VENUE.** EACH OF THE PARTIES HERETO HEREBY CONSENTS TO THE EXCLUSIVE JURISDICTION OF THE COURTS OF THE STATE OF TEXAS, COUNTY OF COMAL, AND TO THE UNITED STATES DISTRICT COURT FOR THE WESTERN DISTRICT OF TEXAS - SAN ANTONIO DIVISION, AS WELL AS TO THE JURISDICTION OF ALL COURTS TO WHICH AN APPEAL MAY BE TAKEN FROM SUCH COURTS, FOR THE PURPOSE OF ANY SUIT, ACTION, OR OTHER PROCEEDING ARISING OUT OF, OR IN CONNECTION WITH, THIS AGREEMENT OR ANY OF THE TRANSACTIONS CONTEMPLATED HEREBY INCLUDING, WITHOUT LIMITATION, ANY PROCEEDING RELATING TO ANCILLARY MEASURES IN AID OF ARBITRATION, PROVISIONAL REMEDIES AND INTERIM RELIEF, OR ANY PROCEEDING TO ENFORCE ANY ARBITRAL DECISION OR AWARD. EACH PARTY HERETO EXPRESSLY WAIVES ANY AND ALL RIGHTS TO BRING ANY SUIT, ACTION, OR OTHER PROCEEDING IN OR BEFORE ANY COURT OR TRIBUNAL OTHER THAN COURTS OF THE STATE OF TEXAS, COUNTY OF COMAL, AND COVENANTS THAT IT SHALL NOT SEEK IN ANY MANNER TO PROSECUTE OR DEFEND ANY DISPUTE OTHER THAN AS SET FORTH IN THIS ARTICLE XVI OR TO CHALLENGE OR SET ASIDE ANY DECISION, AWARD, OR JUDGMENT OBTAINED IN ACCORDANCE WITH THE PROVISIONS HEREOF. EACH OF THE PARTIES HERETO HEREBY EXPRESSLY WAIVES ANY AND ALL OBJECTIONS IT MAY HAVE TO VENUE, INCLUDING, WITHOUT LIMITATION, THE INCONVENIENCE OF SUCH FORUM, IN ANY OF SUCH COURTS

**XVI. JURY TRIAL WAIVER. THE PARTIES HEREBY UNCONDITIONALLY WAIVE THEIR RIGHT TO A JURY TRIAL OF ANY AND ALL CLAIMS OR CAUSES OF ACTION ARISING FROM OR RELATING TO THEIR RELATIONSHIP. THE PARTIES ACKNOWLEDGE THAT A RIGHT TO A JURY IS A CONSTITUTIONAL RIGHT, THAT THEY HAVE HAD AN OPPORTUNITY TO CONSULT WITH INDEPENDENT COUNSEL, AND THAT THIS JURY WAIVER HAS BEEN ENTERED INTO KNOWINGLY AND VOLUNTARILY BY ALL PARTIES TO THIS AGREEMENT. IN THE EVENT OF LITIGATION, THIS AGREEMENT MAY BE FILED AS A WRITTEN CONSENT TO A TRIAL BY THE COURT.**

MP#0001708

Approved by Contractor \_\_\_\_\_ **CHRISTOPHER RYAN SEIDENSTICKER**

Approved by Client \_\_\_\_\_

**XVII. Reservation of Rights** Contractor reserves all rights not specifically granted herein

**XVIII. Counterparts** This Agreement may be executed in one or more counterparts, each of which shall be deemed to be an original but all of which together will constitute one and the same instrument

**XIX. Counsel.** Contractor has previously recommended that Client engage counsel to assist him/her/it in reviewing this Agreement and all other matters relating to it. Contractor and Client shall each bear his/her its own costs and expenses in connection with the negotiation and documentation of this Agreement.

**XX. Entire Agreement:** This agreement contains the entire agreement of the parties, and there are no promises or conditions in any other agreement, oral or written. The Parties expressly disclaim reliance on any prior statements, oral or written, by either party not expressly provided for herein

Client: BJ

Contractor: \_\_\_\_\_

**PS Septic Supply & Service**  
23011 FM 306  
Canyon Lake, TX 78133

**Phone: (830) 850-0080**  
**Fax: (830) 935-4932**

**To: Bret Johnson**  
80 Sun Valley Drive  
Spring Branch, TX 78070

Printed: 7/13/2021  
Site: 80 Sun Valley Drive  
Spring Branch, TX 78070  
(210) 834-0320

Permit #: **109439**

Agency: Comal County

County:

Mfg / Brand: - MAXX AIR

Treatment Type: Aerobic

Disposal: Surface Application

Sub: Sun Valley Village

Customer ID: 1352

Contract Dates: 3/22/2021 - 3/22/2023

Scheduled Date 7/22/2021

Inspection 1 of 6

GPS Coordinates - Latitude: 29.829822 Longitude: -98.386705

**Service Type: Scheduled Inspection**

This counts as a type of "Scheduled Inspection"

**Visit Date: 7/12/2021**

**Entered By: \_**

**Method: Grab**

**Technician: Chris Zigalo**

**Maint. Provider: Ryan Seidensticker**

**Aerators: Operational**

**Sludge Levels**

**Filters: Operational**

**For Tank 1: 12**

**Irrigation Pumps: Operational**

**For Tank 2: 4**

**Disinfection Device: Operational**

**For Tank 3: 2**

**Chlorine Supply: Operational**

**Chlorine Residual: .13**

**Tank Lid / Riser: Secured**

**Sprinkler Drip Backwash: Good**

**Electric Circuits: Operational**

**Distribution System: Operational**

**Sprayfield Veg: Operational**

**Color: Good**

**Odor: Good**

**Alarm: Operational**

**Comments**

**Service Completed**

-Scum=5 Technician Secured the Tank Lid and/or Riser prior to leaving location.

**Owner signature: \_\_\_\_\_**

Insp ID #: 10818

**Provider: Christopher Ryan Seidensticker**  
**PS Septic Supply & Service**

License Info: MP0001708 Expires:

License Info: MT001878 Expires: 7/31/2023

**PS Septic Supply & Service**  
23011 FM 306  
Canyon Lake, TX 78133

**Phone: (830) 850-0080**  
**Fax: (830) 935-4932**

**To: Bret Johnson**  
**80 Sun Valley Drive**  
**Spring Branch, TX 78070**

Printed: 11/18/2021  
Site: 80 Sun Valley Drive (Main House)  
Spring Branch, TX 78070  
(210) 834-0320

---

Permit #: **109439** Customer ID: 1352  
Agency: Comal County Contract Dates: 3/22/2021 - 3/22/2023  
County: Sub: Sun Valley Village Scheduled Date: 11/22/2021 Inspection 2 of 6  
Mfg / Brand: - MAXX AIR  
Treatment Type: Aerobic  
Disposal: Surface Application GPS Coordinates - Latitude: 29.829822 Longitude: -98.386705

---

**Service Type: Scheduled Inspection**

This counts as a type of "Scheduled Inspection"

**Visit Date: 11/17/2021**

**Entered By: Danielle Jordan**

**Method: Grab**

**Technician: Michale Albers**

**Maint. Provider: Ryan Seidensticker**

---

**Aerators: Operational**  
**Filters: Operational**  
**Irrigation Pumps: Operational**  
**Disinfection Device: Operational**  
**Chlorine Supply: Operational**  
**Chlorine Residual: .1**

**Sludge Levels**  
**For Tank 1: 5**

**Tank Lid / Riser: Secured**

**Sprinkler Drip Backwash: Good**

**Electric Circuits: Operational**  
**Distribution System: Operational**  
**Sprayfield Veg: Operational**

**Color: Good**  
**Odor: Good**

**Alarm: Operational**

**Comments**

Scum - 13" - Technician Secured the Tank Lid and/or Riser prior to leaving location.

**Service Completed**

Insp ID #: 13087

**Provider: *Christopher Ryan Seidensticker***  
***PS Septic Supply & Service***

License Info: MP0001708 Expires:

**PS Septic Supply & Service**  
23011 FM 306  
Canyon Lake, TX 78133

**Phone: (830) 850-0080**  
**Fax: (830) 935-4932**

**To: Bret Johnson**  
**80 Sun Valley Drive**  
**Spring Branch, TX 78070**

Printed:3/1/2022  
Site: 80 Sun Valley Drive (Main House)  
Spring Branch, TX 78070  
(210) 834-0320

---

Permit #: **109439** Customer ID: 1352  
Agency: Comal County Contract Dates: 3/22/2021 - 3/22/2023  
County: Sub: Sun Valley Village Scheduled Date: 3/22/2022 Inspection 3 of 6  
Mfg / Brand: - MAXX AIR  
Treatment Type: Aerobic  
Disposal: Surface Application GPS Coordinates - Latitude: 29.829822 Longitude: -98.386705

---

**Service Type: Scheduled Inspection**

This counts as a type of "Scheduled Inspection"

**Visit Date: 2/28/2022**

**Entered By: Michelle Irvin**

**Method: Grab**

**Technician: Michale Albers**

**Maint. Provider: Ryan Seidensticker**

**Aerators: Operational**

**Sludge Levels**

**Filters: Operational**

**For Tank 1: 9**

**Irrigation Pumps: Operational**

**Disinfection Device: Operational**

**Chlorine Supply: Operational**

**Chlorine Residual: .01**

**Tank Lid / Riser: Secured**

**Sprinkler Drip Backwash: Good**

**Electric Circuits: Operational**

**Distribution System: Operational**

**Sprayfield Veg: Operational**

**Color: Good**

**Odor: Good**

**Alarm: Operational**

**Comments**

**Service Completed**

Scum = 20"

Fixed broken spray line - Technician Secured the Tank Lid and/or Riser prior to leaving location.

Insp ID #:15835

**Provider: *Christopher Ryan Seidensticker***  
***PS Septic Supply & Service***

License Info: MP0001708 Expires:



**PS Septic Supply & Service**  
**23011 FM 306**  
**Canyon Lake, TX 78133**

**Phone: (830) 850-0080**  
**Fax: (830) 935-4932**

**To: Bret Johnson**  
**80 Sun Valley Drive**  
**Spring Branch, TX 78070**

Printed: 7/22/2022  
Site: 80 Sun Valley Drive (Main House)  
Spring Branch, TX 78070  
(210) 834-0320

---

Permit #: **109439** Customer ID: 1352  
Agency: Comal County Contract Dates: 3/22/2021 - 3/22/2023  
County: Sub: Sun Valley Village Scheduled Date: 7/22/2022 Inspection 4 of 6  
Mfg / Brand: - MAXX AIR  
Treatment Type: Aerobic  
Disposal: Surface Application GPS Coordinates - Latitude: 29.829822 Longitude: -98.386705

---

**Service Type: Scheduled Inspection**

This counts as a type of "Scheduled Inspection"

**Visit Date: 7/22/2022**

**Entered By: \_**

**Method: Grab**

Copy emailed to Customer  
Customer Emailed: 7/22/2022

**Technician: Not Assigned**

**Maint. Provider: Ryan Seidensticker**

---

**Aerators:** Operational  
**Filters:** Operational  
**Irrigation Pumps:** Operational  
**Disinfection Device:** Operational  
**Chlorine Supply:** Operational  
**Chlorine Residual:** .17

**Sludge Levels**  
**For Tank 1: 10**  
**For Tank 3: 2**

**Electric Circuits:** Operational  
**Distribution System:** Operational  
**Sprayfield Veg:** Operational

**Tank Lid / Riser:** Secured  
**Insp. Port / Plug:** Secured

**Alarm:** Operational

**Comments**

**Service Completed**

Scum on pretreatment 2" - Technician Secured the Tank Lid and/or Riser prior to leaving location. - Inspection Port Plug was noted as Secured prior to leaving. - Copy emailed to the customer on 7/22/2022.

Insp ID #:19668

**Provider: Christopher Ryan Seidensticker**  
**PS Septic Supply & Service**

License Info: MP0001708 Expires:
