

Comal County Environmental Health

OSSF Inspection Sheet

Installer Name: _____

OSSF Installer #: _____

1st Inspection Date: _____

2nd Inspection Date: _____

3rd Inspection Date: _____

Inspector Name: _____

Inspector Name: _____

Inspector Name: _____

Permit#:

Address:

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials		285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)				
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards		285.91(10) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)		285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot		285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)		285.32(a)(5)				
6	PRETREATMENT Installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

Inspector Notes:

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1) (E) 285.91(2) 285.32(b)(1) (F) 285.32(b)(1)(E) (iii) 285.32(b)(1)(E)(ii) (II) 285.32(b)(1)(E)(ii) (I) 285.32(b)(1)(E) (i) 285.32(b)(1) (D) 285.32(b)(1)(C) (ii) 285.32(b)(1)(C) (i) 285.32(b)(1) (B) 285.32(b)(1) (A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed						
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number						
16	DISPOSAL SYSTEM Absorptive		285.33(a)(4) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(3) 285.33(a)(4) 285.33(a)(1) 285.33(a)(2)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(4) 285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(a)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(v)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
32	EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling EFFLUENT DISPOSAL SYSTEM Topographic Slopes < 2.0% EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field (1000 Linear ft. for 2 bedrooms or Less & an additional 400 ft. for each additional bedroom) EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. & Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) & Pipe Holes (3/16 - 1/4" dia. Hole Size) 5 ft. Apart		285.33(b)(3)(A) 285.33(b)(3)(A) 285.33(b)(3)(B)285.91(13) 285.33(b)(3)(D) 285.33(b)(3)(F)				
33	AEROBIC TREATMENT UNIT Is Aerobic Unit Installed According to Approved Guidelines.		285.32(c)(1)				
34	AEROBIC TREATMENT UNIT Inspection/Clean Out Port & Risers Provided AEROBIC TREATMENT UNIT Secondary restraint system provided AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions						
35	AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.						
36	PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials & construction PUMP TANK Sampling Port Provided in the Treated Effluent Line PUMP TANK Check Valve and/or Anti- Siphon Device Present When Required PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump						
37	PUMP TANK Inspection/Clean Out Port & Risers Provided PUMP TANK Secondary restraint system provided PUMP TANK Riser permanently fastened to lid or cast into tank PUMP TANK Riser cap protected against unauthorized intrusions						
38	PUMP TANK Secondary restraint system provided						
39	PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried						

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?		285.33(d)(2)(G)(iii)(II) 285.33(d)(2)(G)(iii)(III) 285.33(d)(2)(G)(v) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)				
41	APPLICATION AREA Low Angle Nozzles Used / Pressure is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed		285.33(d)(2)(G) (i)285.33(d)(2) (A)285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						



COMAL COUNTY

ENGINEER'S OFFICE

Permit of Authorization to Construct an On-Site Sewage Facility Permit Valid For One Year From Date Issued

Permit Number: 118025
Issued This Date: 11/12/2024
This permit is hereby given to: Brant Shalek

To start construction of a private, on-site sewage facility located at:

1056 KINGS COVE DR
CANYON LAKE, TX 78133

Subdivision: Kings Cove
Unit: 1
Lot: 35
Block: 2
Acreage: 1.1500

APPROVED MINIMUM SIZES AS PER ATTACHED DESIGN

Type of System: Aerobic
Surface Irrigation

This permit gives permission for the construction of the above referenced on-site facility to commence. Installation must be completed by an installer holding a valid registration card from the Texas Commission on Environmental Quality (TCEQ). Installation and inspection must comply with current TCEQ and Comal County requirements.

Call (830) 608-2090 to schedule inspections.



COMAL COUNTY
ENGINEER'S OFFICE

ON-SITE SEWAGE FACILITY APPLICATION

195 DAVID JONAS DR
NEW BRAUNFELS, TX 78132
(830) 608-2090
WWW.CCEO.ORG

Date **RECEIVED**
By Kathy Griffin at 10:26 am, Oct 23, 2024

Permit Number **118025**

1. APPLICANT / AGENT INFORMATION

Owner Name Brant Shalek
Mailing Address 1623 Sunshine Peak
City, State, Zip New Braunfels, TX 78130
Phone # _____
Email _____

Agent Name Doug Dowlearn R.S.
Agent Address 703 Oak Dr.
City, State, Zip Blanco, TX 78606
Phone # 210-878-8100
Email TXSEPTIC@GMAIL.COM

2. LOCATION

Subdivision Name Kings Cove Unit 1 Lot 35 Block 2
Survey Name / Abstract Number _____ Acreage 1.15
Address 1056 Kings Cove City Canyon Lake State TX Zip 78133

3. TYPE OF DEVELOPMENT

☒ Single Family Residential
Type of Construction (House, Mobile, RV, Etc.) House
Number of Bedrooms 4
Indicate Sq Ft of Living Area <3500

☐ Non-Single Family Residential
(Planning materials must show adequate land area for doubling the required land needed for treatment units and disposal area)
Type of Facility _____
Offices, Factories, Churches, Schools, Parks, Etc. - Indicate Number Of Occupants _____
Restaurants, Lounges, Theaters - Indicate Number of Seats _____
Hotel, Motel, Hospital, Nursing Home - Indicate Number of Beds _____
Travel Trailer/RV Parks - Indicate Number of Spaces _____
Miscellaneous _____

Estimated Cost of Construction: \$ 790000.00 (Structure Only)

Is any portion of the proposed OSSF located in the United States Army Corps of Engineers (USACE) flowage easement?

☐ Yes ☒ No (If yes, owner must provide approval from USACE for proposed OSSF improvements within the USACE flowage easement)

Source of Water ☒ Public ☐ Private Well ☐ Rainwater

4. SIGNATURE OF OWNER

By signing this application, I certify that:

- The completed application and all additional information submitted does not contain any false information and does not conceal any material facts. I certify that I am the property owner or I possess the appropriate land rights necessary to make the permitted improvements on said property.
- Authorization is hereby given to the permitting authority and designated agents to enter upon the above described property for the purpose of site/soil evaluation and inspection of private sewage facilities..
- I understand that a permit of authorization to construct will not be issued until the Floodplain Administrator has performed the reviews required by the Comal County Flood Damage Prevention Order.
- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

Brant Shalek

Miranda Shalek

10/4/2024

Signature of Owner

Date

Planning Materials & Site Evaluation as Required Completed By _____

System Description _____

Size of Septic System Required Based on Planning Materials & Soil Evaluation

Tank Size(s) (Gallons) _____ Absorption/Application Area (Sq Ft) _____

Gallons Per Day (As Per TCEQ Table III) _____

(Sites generating more than 5000 gallons per day are required to obtain a permit through TCEQ.)

Is the property located over the Edwards Recharge Zone? ☐ Yes ☐ No

(If yes, the planning materials must be completed by a Registered Sanitarian (R.S.) or Professional Engineer (P.E.))

Is there an existing TCEQ approved WPAP for the property? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design complies with all provisions of the existing WPAP.)

Is there at least one acre per single family dwelling as per 285.40(c)(1)? ☐ Yes ☐ No

If there is no existing WPAP, does the proposed development activity require a TCEQ approved WPAP? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed WPAP. A Permit to Construct will not be issued for the proposed OSSF until the proposed WPAP has been approved by the appropriate regional office.)

Is the property located over the Edwards Contributing Zone? ☐ Yes ☐ No

Is there an existing TCEQ approval CZP for the property? ☐ Yes ☐ No

(If yes, the P.E. or R.S. shall certify that the OSSF design complies with all provisions of the existing CZP.)

If there is no existing CZP, does the proposed development activity require a TCEQ approved CZP? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed CZP. A Permit to Construct will not be issued for the proposed OSSF until the CZP has been approved by the appropriate regional office.)

Is this property within an incorporated city? ☐ Yes ☐ No

If yes, indicate the city: _____

By signing this application, I certify that:

- The information provided above is true and correct to the best of my knowledge.

- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.



Signature of Designer

Date



202406030367 10/07/2024 10:05:00 AM 1/1

COUNTY OF COMAL
STATE OF TEXAS

AFFIDAVIT TO THE PUBLIC

CERTIFICATION OF OSSF REQUIRING MAINTENANCE

According to Texas Commission on Environmental Quality (TCEQ) Rules for On-Site Sewage Facilities (OSSFs), this document is filed in the Deed Records of Comal County, Texas

The Texas Health and Safety Code, Chapter 366 authorizes the Texas Commission on Environmental Quality (TCEQ) to regulate on-site sewage facilities (OSSFs). Additionally, the Texas Water Code (TWC), § 5.012 and § 5.013, give the commission primary responsibility for implementing the laws of the State of Texas relating to water and adopting rules necessary to carry out its powers and duties under the TWC. The commission, under the authority of the TWC and the Texas Health and Safety Code, requires owners to provide notice to the public that certain types of OSSFs are located on specific pieces of property. To achieve this notice, the commission requires a recorded affidavit. Additionally, the owner must provide proof of the recording to the OSSF permitting authority. This recorded affidavit is not a representation or warranty by the commission of the suitability of this OSSF, nor does it constitute any guarantee by the commission that the appropriate OSSF was installed.

An OSSF requiring a maintenance contract, according to 30 Texas Administrative Code § 285.91 (12) will be installed on the property described as (insert legal description):

Kings Cove Unit One, Lot 35, Block 2

The property is owned by (Insert owner's full name):

Brant Shalek

This OSSF must be covered by a continuous maintenance contract for the first two years. After the initial two-year service policy, the owner of an aerobic treatment system for a single family residence shall either obtain a maintenance contract within 30 days or maintain the system personally.

Upon sale or transfer of the above described property, the permit for the OSSF shall be transferred to the buyer or new owner. A copy of the planning materials for OSSF may be obtained from Comal County Engineer's Office.

WITNESS BY HAND(S) ON THIS 4 DAY OF October, 2024

Owner(s) signature(s)

Brant Shalek


(PRINTED NAME) /TITLE

SWORN TO AND SUBSCRIBED BEFORE ME ON THIS 4 DAY OF October, 2024

Notary Public, State of Texas

Notary's Printed Name: Jacob Bruner

My Commission Expires: 10-16-2027



Filed and Recorded
Official Public Records
Bobbie Koepf, County Clerk
Comal County, Texas
10/07/2024 10:05:00 AM
TRACY 1 Page(s)
202406030367



Bobbie Koepf



On-Site Sewage Facility (OSSF) Service Agreement

- I. **General:** This Work for Hire Agreement (hereinafter referred to as "Agreement") is entered into by and between Brant Shalek, (hereinafter referred to as "Client") and SOTX Septic Services (hereinafter to as "Contractor"). By this agreement, Contractor agrees to render services, as described herein, and the Client agrees to fulfill his/her/their responsibilities under this agreement as described herein.
- II. **Effective Dates:** This agreement commences on receipt of full payment and runs for two (2) years. Agreement's... Starting Date: (Date License to Operate is Issued) Ending Date: (2yrs. From Date of LTO)
- III. **Services by Contractor:** Contractor will provide the following services (hereinafter referred to as the "Services"):
 1. In compliance with Agency (TCEQ and/or County) and manufacturer's requirements, inspect and perform routine maintenance on the On-Site Sewage Facility (hereinafter referred to as the "OSSF") three (3) times per year (approximately once every four (4) months).
 2. Report to the appropriate regulatory authority and to the Client, as is required by both the State's on-site rules and the local Agency's rules, if more stringent. All findings must be reported to the local Agency within 14 days.
 3. If any components of the OSSF are found to need repair during the inspection, the Contractor will notify the Client of the repairs needed.
 4. Visit in response to Client's request(s) for unscheduled service(s) within two business days from the date of Contractor's receipt of Client's request. All unscheduled responses are in addition to the fee covered by this Agreement and will be billed to the Client.
 5. Provide notification of arrival to site to the homeowner or to site personnel. Additionally, written notification of the visit will be left at the site or with site personnel upon completion or inspection, as well as, forwarded to agency within 14 days.
- IV. **Site Location:** The Services are to be performed at the property located at:
1056 Kings Cv Dr. Canyon Lake, TX 78133
- V. **Payment(s):** The fee for this Agreement only covers the Services describes herein. This fee does not cover equipment, parts or labor supplied for the repairs or charges for unscheduled Client-request trips to the site. Payments for such additional services are due when service is provided or rendered. Payments not received within 30 days from due date will be subjected to a \$20.00 late penalty and / or a 1.5% carrying charge, whichever is greater, in addition the reasonable attorney's fees and all costs of collection incurred by Contractor in collection of any unpaid debt(s). By signing this contract, the Client is authorizing the Contractor to remove any parts which were installed but not paid for at the end of 30 days. The Client is still responsible for any labor costs associated with the installation and remove of said parts.

Initials...

Customer:

DS Initial
 BS MS

Contractor: CDH

Client's Responsibilities: The Client is responsible for each and all the following:

1. Maintain chlorinator and provide proper chlorine supply, if OSSF is equipped with same.
2. Provide all necessary yard or lawn maintenance and removal of obstacles as needed to allow the OSSF to function properly, and to allow Contractor easy access to all parts of the OSSF.
3. Maintain a current license to operate and abide by the conditions and limitations of that license and all requirements for on-site sewage facilities (OSSF's) from the State and local regulatory agency, as well as manufacturer's recommendations.
4. Immediately notify the Contractor and Agency of all problems with, including the failure of the OSSF.
5. Upon receiving a written notification of services needed from the Contractor, it becomes the Client's responsibility to contact the Contractor to authorize the service. If the Client chooses to use a different contractor to perform the service, the Client's responsible for ensuring the contractor holds the proper license (installer II) and is certified by the manufacturer. Also, the Client is responsible for ensuring proper notification is given to the Agency, as required by the State and local Agency rules.
6. Provide the Contractor with water usage records, upon request, for evaluation by the Contractor of the OSSF performance.
7. Clients residing in Harris County should allow for samples at both the inlet and outlet to the OSSF to be obtained by the Contractor for the purpose of evaluating the OSSF's performance when requested by the Client. If these samples are sent to the lab for testing, the Client will directly pay the lab for the cost of the testing plus pay the Contractor for all man-hours expended in providing this additional service at the rate of \$75.00 per hour measured from office to site, site to lab, and lab to office, otherwise known as portal to portal.
8. Not allow the backwash from water treatment or water conditioning equipment to enter the OSSF.
9. Provide for pumping of tanks, when needed, at Clients expense.
10. Maintain site drainage to prevent adverse effects on OSSF.
11. Promptly and fully pay Contactor's bills, fees, or invoices as described herein.

- VI. Access by Contractor:** Contractor, or personnel authorized by the Contractor, may enter the property at reasonable times without prior notice for the purpose of performing the above-described Services. Contractor will require access to the OSSF electrical and physical components, including tanks, by means of manways or risers for the purpose of evaluations required by manufacturer, and/ or rules. If such manways or risers are not in place, excavation together with other labor and materials will be required and will be billed to Client as additional service at the rate of \$75.00 per hour, plus materials billed at list price. Excavated soil is to be replaced as best as reasonably possible.
- VII. Application or Transfer of Payments:** The fees paid for this agreement may transfer to subsequent owner(s); however, this agreement will not transfer. The subsequent owner(s) must sign a similar agreement authorizing Contractor to perform the above-described Services and accepting Client's responsibilities. This replacement Agreement must be signed and received within 30 days of transfer of ownership. Contractor will apply all funds received from Client first to any past due obligations arising from this Agreement including late charges, return check charges, and charges for repairs or services not paid within 30 days of invoicing. The consumption of the payment in this manner may lead to early termination of the agreement by Contractor.
- VIII. Termination of Agreement:** This Agreement may be terminated by either party within 30 days written notice in the event of substantial failure to perform in accordance with its terms by the other party without fault of the terminating party. If this Agreement is so terminated, Contractor shall be paid at the rate of \$75.00 per hour for any work performed, but not yet paid. The party terminating will immediately notify the other party, the equipment manufacturer, and the regulatory agency of the termination.
- IX. Limits of Liability:** In no event shall the Contractor be liable for indirect, consequential, incidental or punitive damages, whether in contract tort or any other theory. In no event the Contractor's liability for direct damages exceed the price for the Services described in this Agreement.
- X. Severability:** If any provision in the Agreement shall be held to be invalid or unenforceable for any reason, the remaining provisions shall continue to be valid and enforceable. If court finds that any provision of this

Initials...

Customer: DS
BS Initial
MS

Contractor: CDH


Agreement is invalid or unenforceable, but that by limiting such provision it would become valid and enforceable, then such provision shall be written, construed, and enforced as so limited.

XI. Performance of Agreement: Commencement of performance by Contractor under this agreement is contingent on the following conditions (1) Contractor receiving a fully execute original copy of this agreement. (2) Contractor receiving payment in full for the fee as described in Section V. If the above conditions are not met, then Contractor is not obligated to perform any portion of this agreement.

XII. Entire Agreement: This agreement contains the entire agreement parties, and there are no other promises or conditions in any other agreement, oral or written.

Client... (And/or authorized agent)

Printed Name: Brant Shalek Signature:  Date: 10/4/2024

Printed Name: Miranda Shalek Signature:  Date: 10/4/2024

Physical Address: 1056 Kings Cv, Canyon Lake Zip: 78133


Mailing Address: 30 Indian Princess Ln, wimberley, TX Zip: 78676

Phone # 936-661-1038 Cell# _____ County: COMAL

Email: mirandashalek@gmail.com Gate Code: #2202
brant.shalek@me.com

=====Contractor=====Contractor=====

SOTX Septic Services

Clarence D. Hinds Jr 

15656 Cranes Mill Rd.

Lic #: OSSF Installer II #: OS0030965

Canyon Lake, TX 78133

Maintenance Provider #: MP0002439

830-481-3249

sotxservices@gmail.com

Installer Name: Canyon Impact Construction

Phone #: _____

Email: _____

Lic #: _____


Manufacturer: _____

GPD: 600 800 1000 Other: _____

Disposal: Spray Drip Other: _____

Initials...

Customer: 

Contractor: 

OSSF SOIL EVALUATION REPORT INFORMATION

Date: 10/22/2024

Applicant Information:

Name: Brant Shalek

Address: 1623 Sunshine Peak

City, State & Zip Code: New Braunfels, TX 78130

Phone:

Email:

Site Evaluator Information:

Name: Doug Dowlearn

Company: D.A.D. Services, Inc.

Address: 703 Oak Drive

City, State & Zip: Blanco, TX 78606

Phone: (210)240-2101 **Fax:** (866)260-7687

Email: txseptic@gmail.com

Property Location:

Subdivision: Kings Cove **Unit:** 1 **Lot:** 35 **Block:** 2

Street/Road Address: 1056 Kings Cv

City : Canyon Lake **Zip:** 78133

Additional Info: Comal County

Installer Information:

Name:

Company:

Address:

City, State & Zip:

Phone:

Depth	Texture Class	Soil Texture	Structure (For Class III – blocky, platy or massive)	Drainage (Mottles/Water Table)	Restrictive Horizon	Observation
Soil Boring #1 60"	III	0-14" Clay Loam 14"+ Limestone	Blocky	<30% Gravel	14"+ Limestone	N/A
Soil Boring #2 60"		Same as above				

DESIGN SPECIFICATIONS

Application Rate (RA): 0.064

OSSF is designed for: 4 bedroom <3500 Sq. Ft Residence

300 gallons per day

An aerobic with spray disposal system is to be utilized based on the site evaluation.

4688 sq. ft. disposal area required

600 GPD Aerobic Treatment Unit

Calculations: Absorption Area: $Q/RA=300/0.064=4688$ Sq. Ft.

FEATURES OF SITE AREA

Presence of 100-year flood zone: NO

Existing or proposed water well in nearby area: NO

Presence of adjacent ponds, streams, water impoundments: NO

Presence of upper water shed: NO

Organized sewage service available to lot: NO

I certify that the findings of this report are based on my field observations and are accurate to the best of my ability. The site evaluation and OSSF design are subject to approval by the TCEQ or the local authorized agent. The planning materials and the OSSF design should not be considered final until a permit to construct has been issued.

Site Evaluator:

NAME: Douglas Dowlearn

Signature:



License No. OS9902 **Exp.** 6/30/2026

TDH: #2432 **Exp.** 2/28/2025


The installation site is at block 2, lot 35 of the Kings Cove Unit 1 subdivision in Comal County, TX. The proposed OSSF will treat the wastewater from a 4 bedroom(< 3500 sf) residence. The proposed method of wastewater treatment is aerobic treatment with spray irrigation. This method was chosen because of unsuitable soil conditions.

PROPOSED SYSTEM:

A 3" or 4" PVC pipe will discharge from the residence to a pre-treatment tank, which flows into a 600 gpd aerobic treatment plant. The aerobic tank effluent flows to a 768 gallon storage/pump tank containing a liquid chlorinator and a single 20 gpm submersible pump. Distribution is through 2 K-Rain Gear Driven pop-up sprinklers, with low angle (13 degrees) spray nozzles spraying a radius of 32 feet at 40 psi. One sprinkler will spray 180 degrees of arc; One sprinkler will spray 360 degrees of arc. An audio and visual alarm monitoring both high water and aerator failure will be placed in a noticeable location.

DESIGN SPECIFICATIONS:

Daily Waste Flow: 300 gpd
Application rate: 0.064
Application area required: $300/.064 = 4688$ sq. ft.
Application area utilized: 4824 sq. ft.
Pump tank reserve capacity: 100 gal minimum



SYSTEM COMPONENTS:

SCH 40 PVC sewer line
Solar Aerobic, Model SA600-768PT
374-gallon Pretreatment tank
600 GPD Aerobic Treatment Unit
768-gallon Pump tank with timed controls set to spray in the pre-dawn hours of midnight to 5:00 am
C-1 20X, Model no. 20XC1-05P4-2W115 (or equivalent) submersible pump
Liquid chlorinator
1" purple PVC supply line
2 K-Rain Gear Driven pop-up sprinklers

LANDSCAPING:

The entire surface application area must consist of an area with vegetation capable of growth, before system start up. In the event the surface application area does not have vegetation capable of growth, the bare area shall be seeded or sodded. If the non-vegetative area consists of rock or caliche, 3" of class II or III soil, capable of growing and sustaining vegetative growth, will be added before it is seeded or sodded.

VOID

D.A.D SERVICES, INC.

DOUG DOWLEARN

PO BOX 212, BULVERDE, TX 78163

Designed for:

Brant Shalek

The installation site is at block 2, lot 35 of the Kings Cove Unit 1 subdivision in Comal County, TX. The proposed OSSF will treat the wastewater from a 4 bedroom (< 3500 sf) residence. The proposed method of wastewater treatment is aerobic treatment with spray irrigation. This method was chosen because of unsuitable soil conditions.

PROPOSED SYSTEM:

A 3" or 4" PVC pipe will discharge from the residence to a pre-treatment tank, which flows into a 600 gpd aerobic treatment plant. The aerobic tank effluent flows to a 796 gallon storage/pump tank containing a liquid chlorinator and a single 20 gpm submersible pump. Distribution is through 3 K-Rain Gear Driven pop-up sprinklers, with low angle (13 degrees) spray nozzles spraying a radius of 32 feet at 40 psi. Each sprinkler will spray 180 degrees of arc. An audio and visual alarm monitoring both high water and aerator failure will be placed in a noticeable location.

DESIGN SPECIFICATIONS:

Daily Waste Flow: 300 gpd

Application rate: 0.064

Application area required: $300 / .064 = 4688$ sq. ft.

Application area utilized: 4824 sq. ft.

Pump tank reserve capacity: 100 gal minimum

SYSTEM COMPONENTS:

SCH 40 PVC sewer line

Pro Flo 600 SLPT

447-gallon Pretreatment tank

600 GPD Aerobic Treatment Unit


796-gallon Pump tank with timed controls set to spray in the pre-dawn hours of midnight to 5:00 am

C-1 20X, Model no. 20XC1-05P4-2W115 (or equivalent) submersible pump

Liquid chlorinator

1" purple PVC supply line

3 K-Rain Gear Driven pop-up sprinklers



LANDSCAPING:

The entire surface application area must consist of an area with vegetation capable of growth, before system start up. In the event the surface application area does not have vegetation capable of growth, the bare area shall be seeded or sodded. If the non-vegetative area consists of rock or caliche, 3" of class II or III soil, capable of growing and sustaining vegetative growth, will be added before it is seeded or sodded.

RECEIVED

By Brenda Ritzen at 8:53 am, Nov 12, 2024

Douglas R. Dowlearn
D.A.D. Services, Inc.
703 Oak Drive
Blanco, TX 78606
(210)240-2101
txseptic@gmail.com

October 21, 2024

RE: 1056 Kings Cv

To Whom It May Concern:


I am requesting a variance for the placement of a spray disposal area 10 feet from the property line, but less than 20 feet from the property line as Comal County regulations require. This variance is requested due to limited space. This setback complies with TCEQ CHAPTER 285 rules Table X. requirements. Equivalent protection will be maintained by including a battery backup to the timer clock to assure sprayers only spray during the predawn hours. In my professional opinion this variance will not pose a threat to the environment or public health.


If there are any questions or concerns, please contact me at 210.240.2101 or by email at txseptic@gmail.com.

Sincerely,



Douglas R. Dowlearn, R.S.






BRANT SHALEK
1056 KINGS COVE
CANYON LAKE, TX 78133
KINGS COVE UNIT 1
LOT 35, BLOCK 2
COMAL COUNTY

SCALE 1" = 30'
PRINT SIZE 11" X 17"



Douglas R. Dowlearn

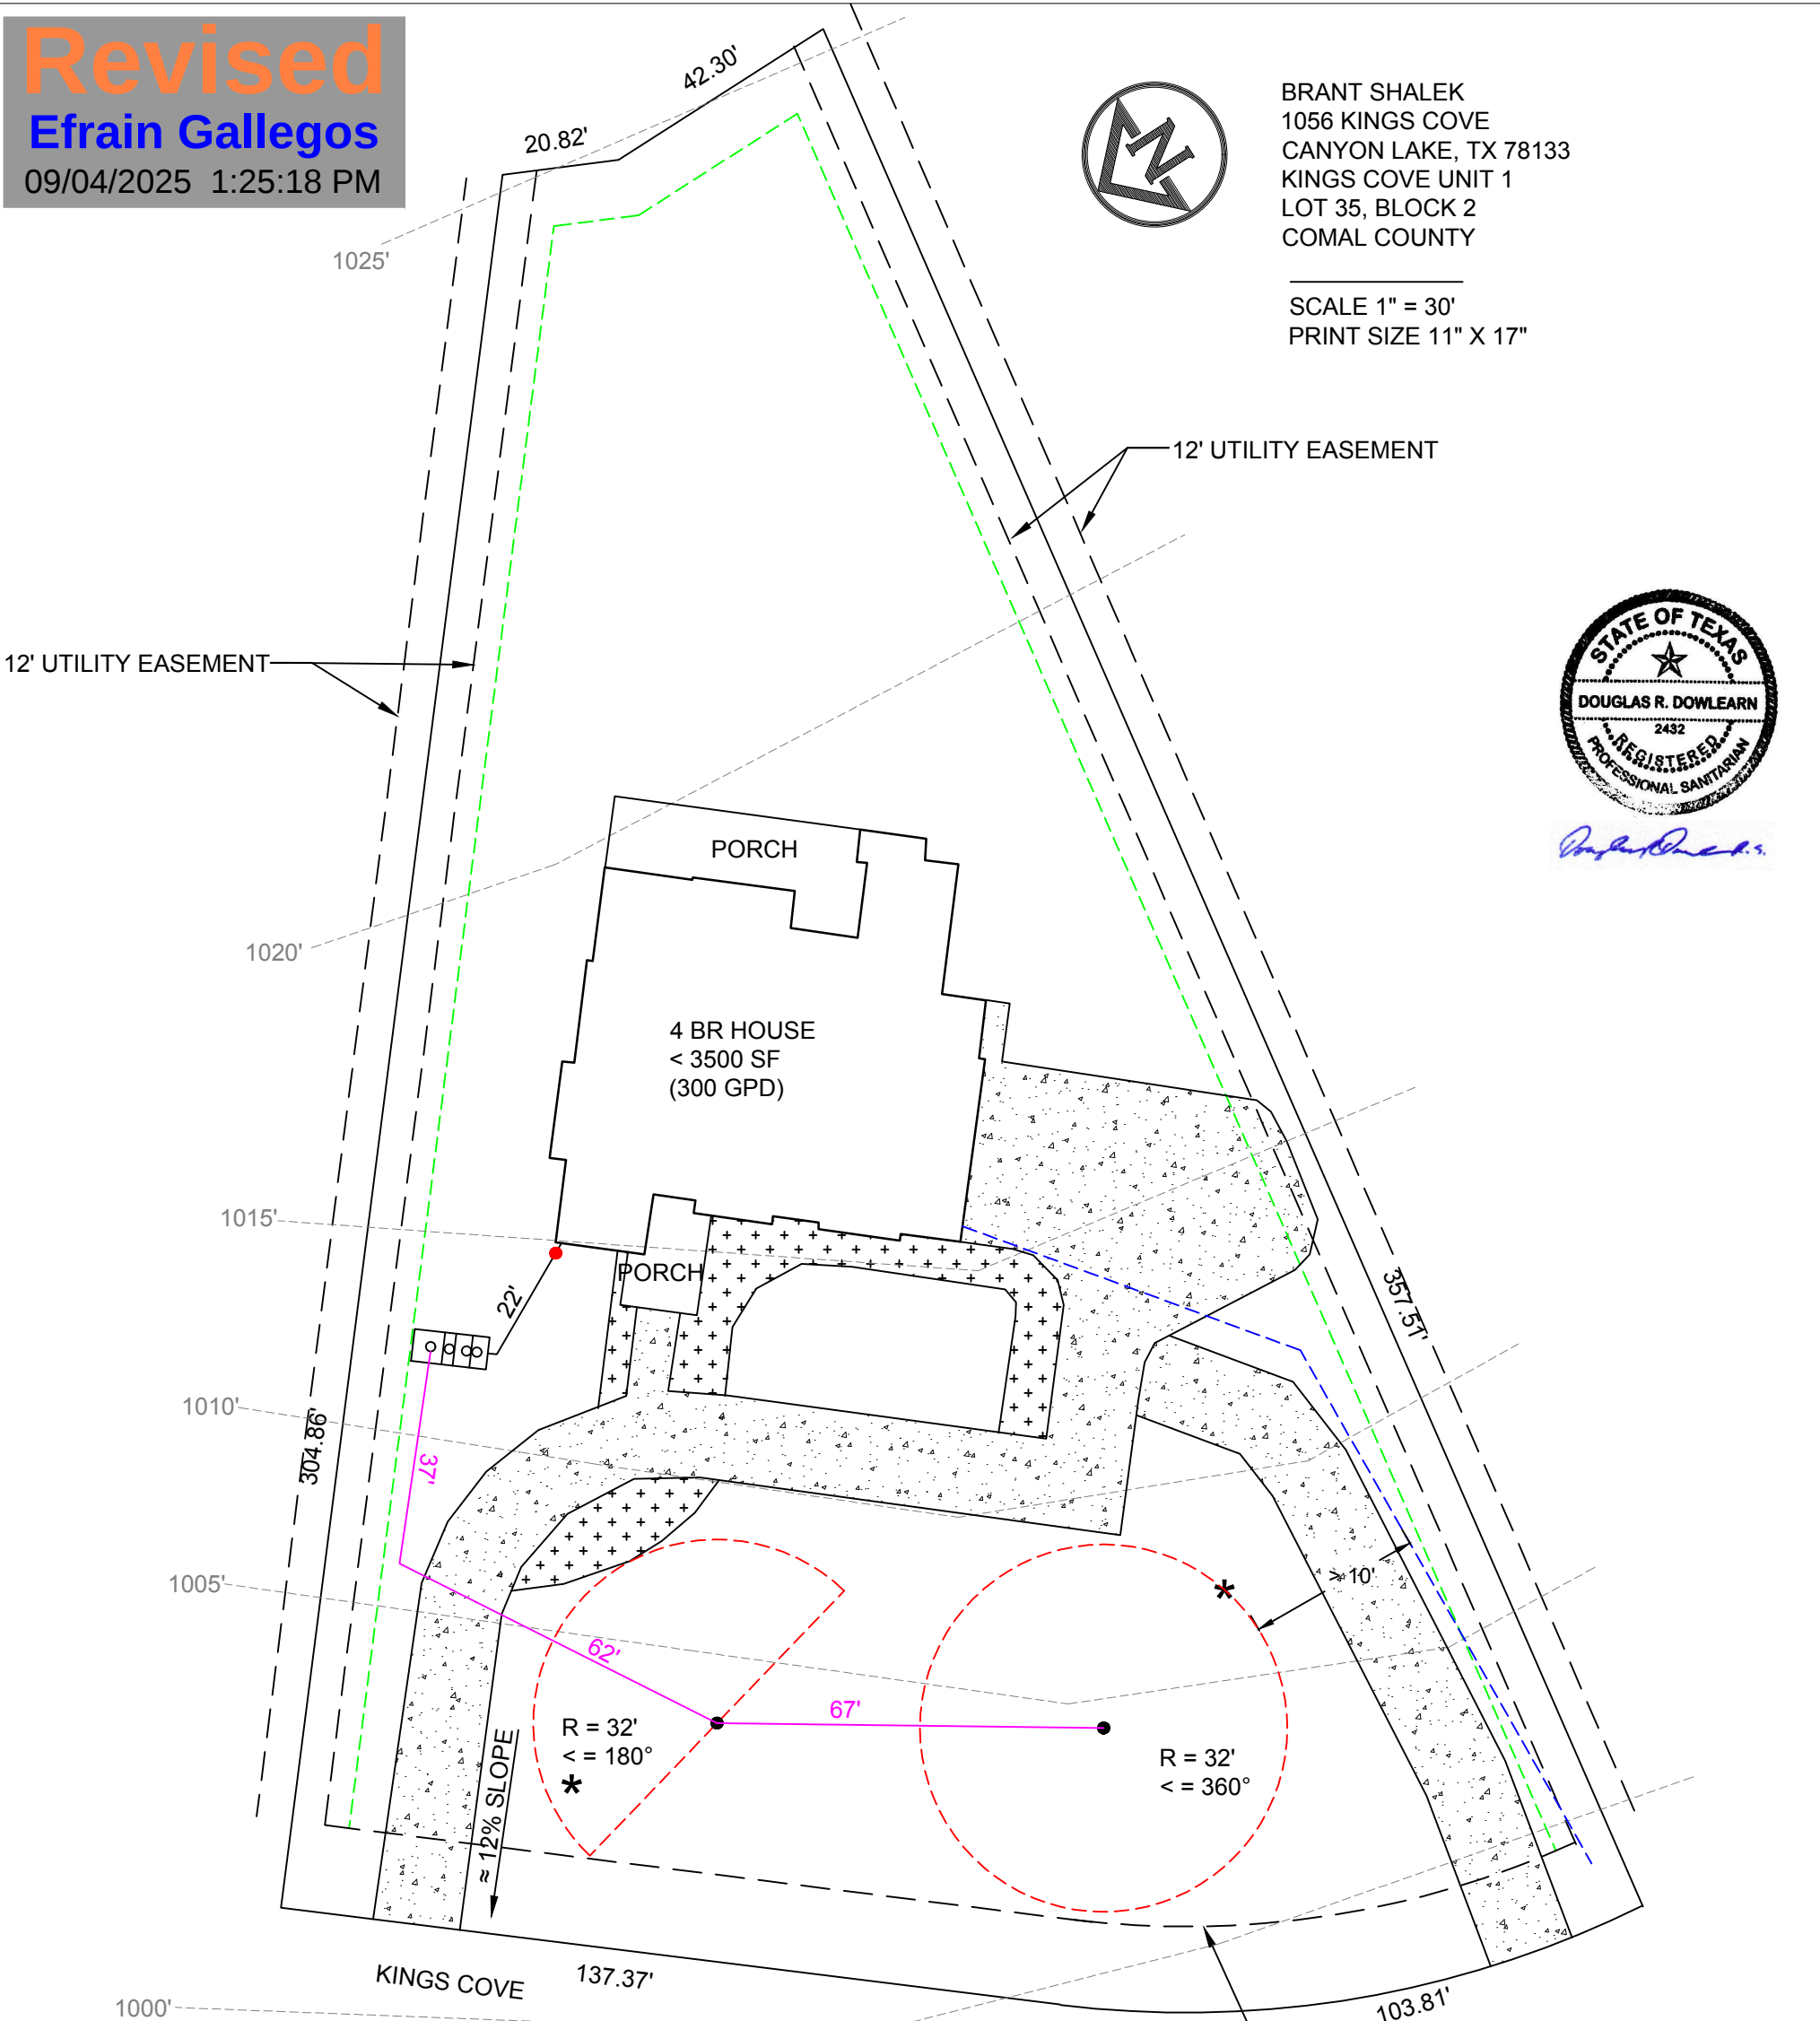

KEY

- 2 WAY CLEANOUT
- 10' OSSF SPRAY SETBACK FROM PROPERTY LINE
- 1" SCH 40 PVC PURPLE PIPE
- PROPOSED WATER LINE(VERIFY LOCATION ON SITE)
- TEST HOLE
- 600 GPD AEROBIC TREATMENT UNIT
- DRIVE/WALKWAY
- LANDSCAPING


NOTES:

- 1" SCH 40 PURPLE PIPE TO ALL SPRAY HEADS.
- 1" SCH 40 PURPLE PIPE WILL BE SLEEVED IN SCH 40 PVC PIPE WHERE IT CROSSES UNDER SURFACE IMPROVEMENTS, DRIVE, WALKWAY AND 5' BEYOND. THIS WILL PROVIDE EQUIVALENT PROTECTION FOR THE OSSF SETBACK REQUIREMENTS OF TAC 285.
- 3" OR 4" SCH 40 PVC PIPE FROM STRUCTURE TO TANK.
- SEWER PIPE CONNECTING THE STRUCTURE TO THE TANK MUST HAVE AT MINIMUM 1/8" FALL PER 1'.
- TANK TO BE > 5' FROM STRUCTURES AND SURFACE IMPROVEMENTS. THIS WILL PROVIDE EQUIVALENT PROTECTION FOR THE SETBACK REQUIREMENTS OF TAC 285.
- CLEANOUT WITHIN 3' OF STRUCTURE.
- TOTAL SPRAY AREA = 4824 SF.
- TANK WILL BE WATER TIGHT AND MANUFACTURED ACCORDING TO ASTM DESIGNATION: C 1227.
- DRAINFIELD SHALL BE GREATER THAN 100' FROM PRIVATE WELLS, AND GREATER THAN 150' FROM PUBLIC WELLS. VERIFY WELL LOCATION(S) ON SITE.
- SPRAY HEADS SHALL BE LOCATED AT LEAST 10' AWAY FROM TREES WITHIN THE DISTRIBUTION AREA.


Revised

Efrain Gallegos


09/04/2025 1:26:41 PM

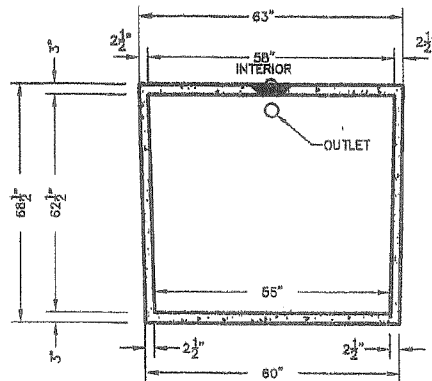

SECTION B-B

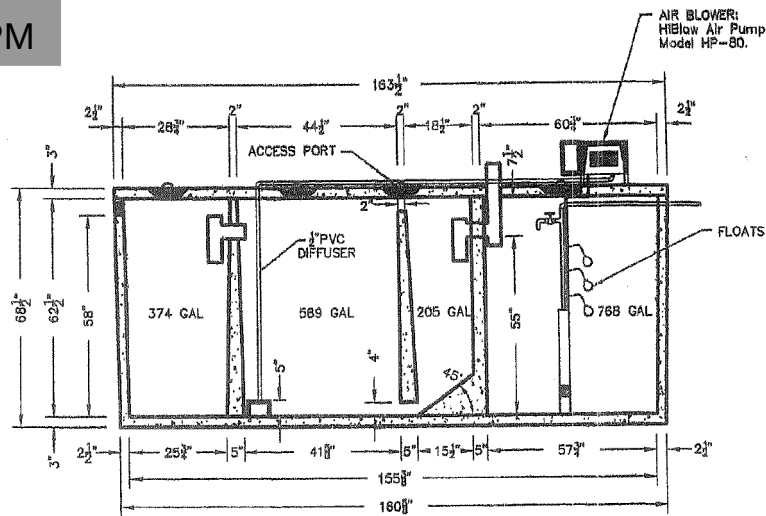


SECTION A-A

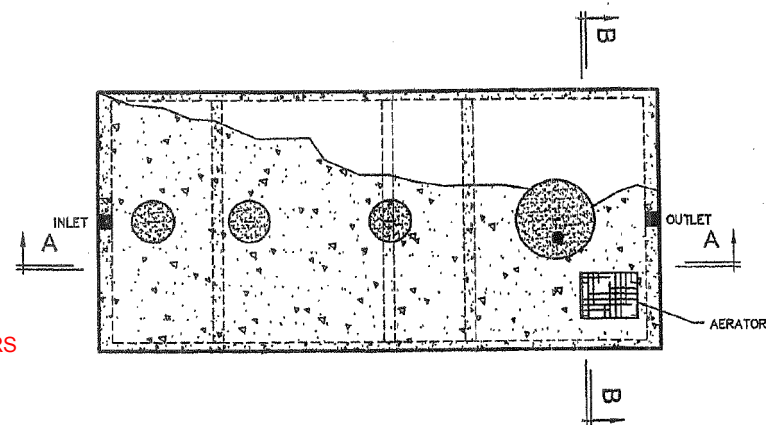

PLAN VIEW


13.96 GALLONS/INCH
 46" - 55" = RESERVE = 125.64 GALLONS
 12" - 46" = PUMP ON TO ALARM ON = 474.64 GALLONS
 10" - 12" = PUMP OFF TO PUMP ON = 27.92 GALLONS
 0 - 10" = SUMP = 139.6 GALLONS

NOTE: SET ON A TIMER TO ACTIVATE IN PRE DAWN HOURS
 BETWEEN MIDNIGHT TO 5 AM.




Douglas R. Dowlearn

DESIGNER: ESI		DATE: ESI	PROJECT: ESI	SCALE: ESI
MODEL SA600-768PT				
SEWER TREATMENT SYSTEM				
SOLAR AEROBIC				
6754 HWY 90 EAST				
LAKE CHARLES, LA 70615				
PHONE: (337) 439-0680				
TREATMENT PLANT				
SA-3				
JULY 2011		PROJECT: -		
SCALE: -				




Douglas R. Dowlearn



BRANT SHALEK
1056 KINGS COVE
CANYON LAKE, TX 78133
KINGS COVE UNIT 1
LOT 35, BLOCK 2
COMAL COUNTY

SCALE 1" = 30'
PRINT SIZE 11" X 17"

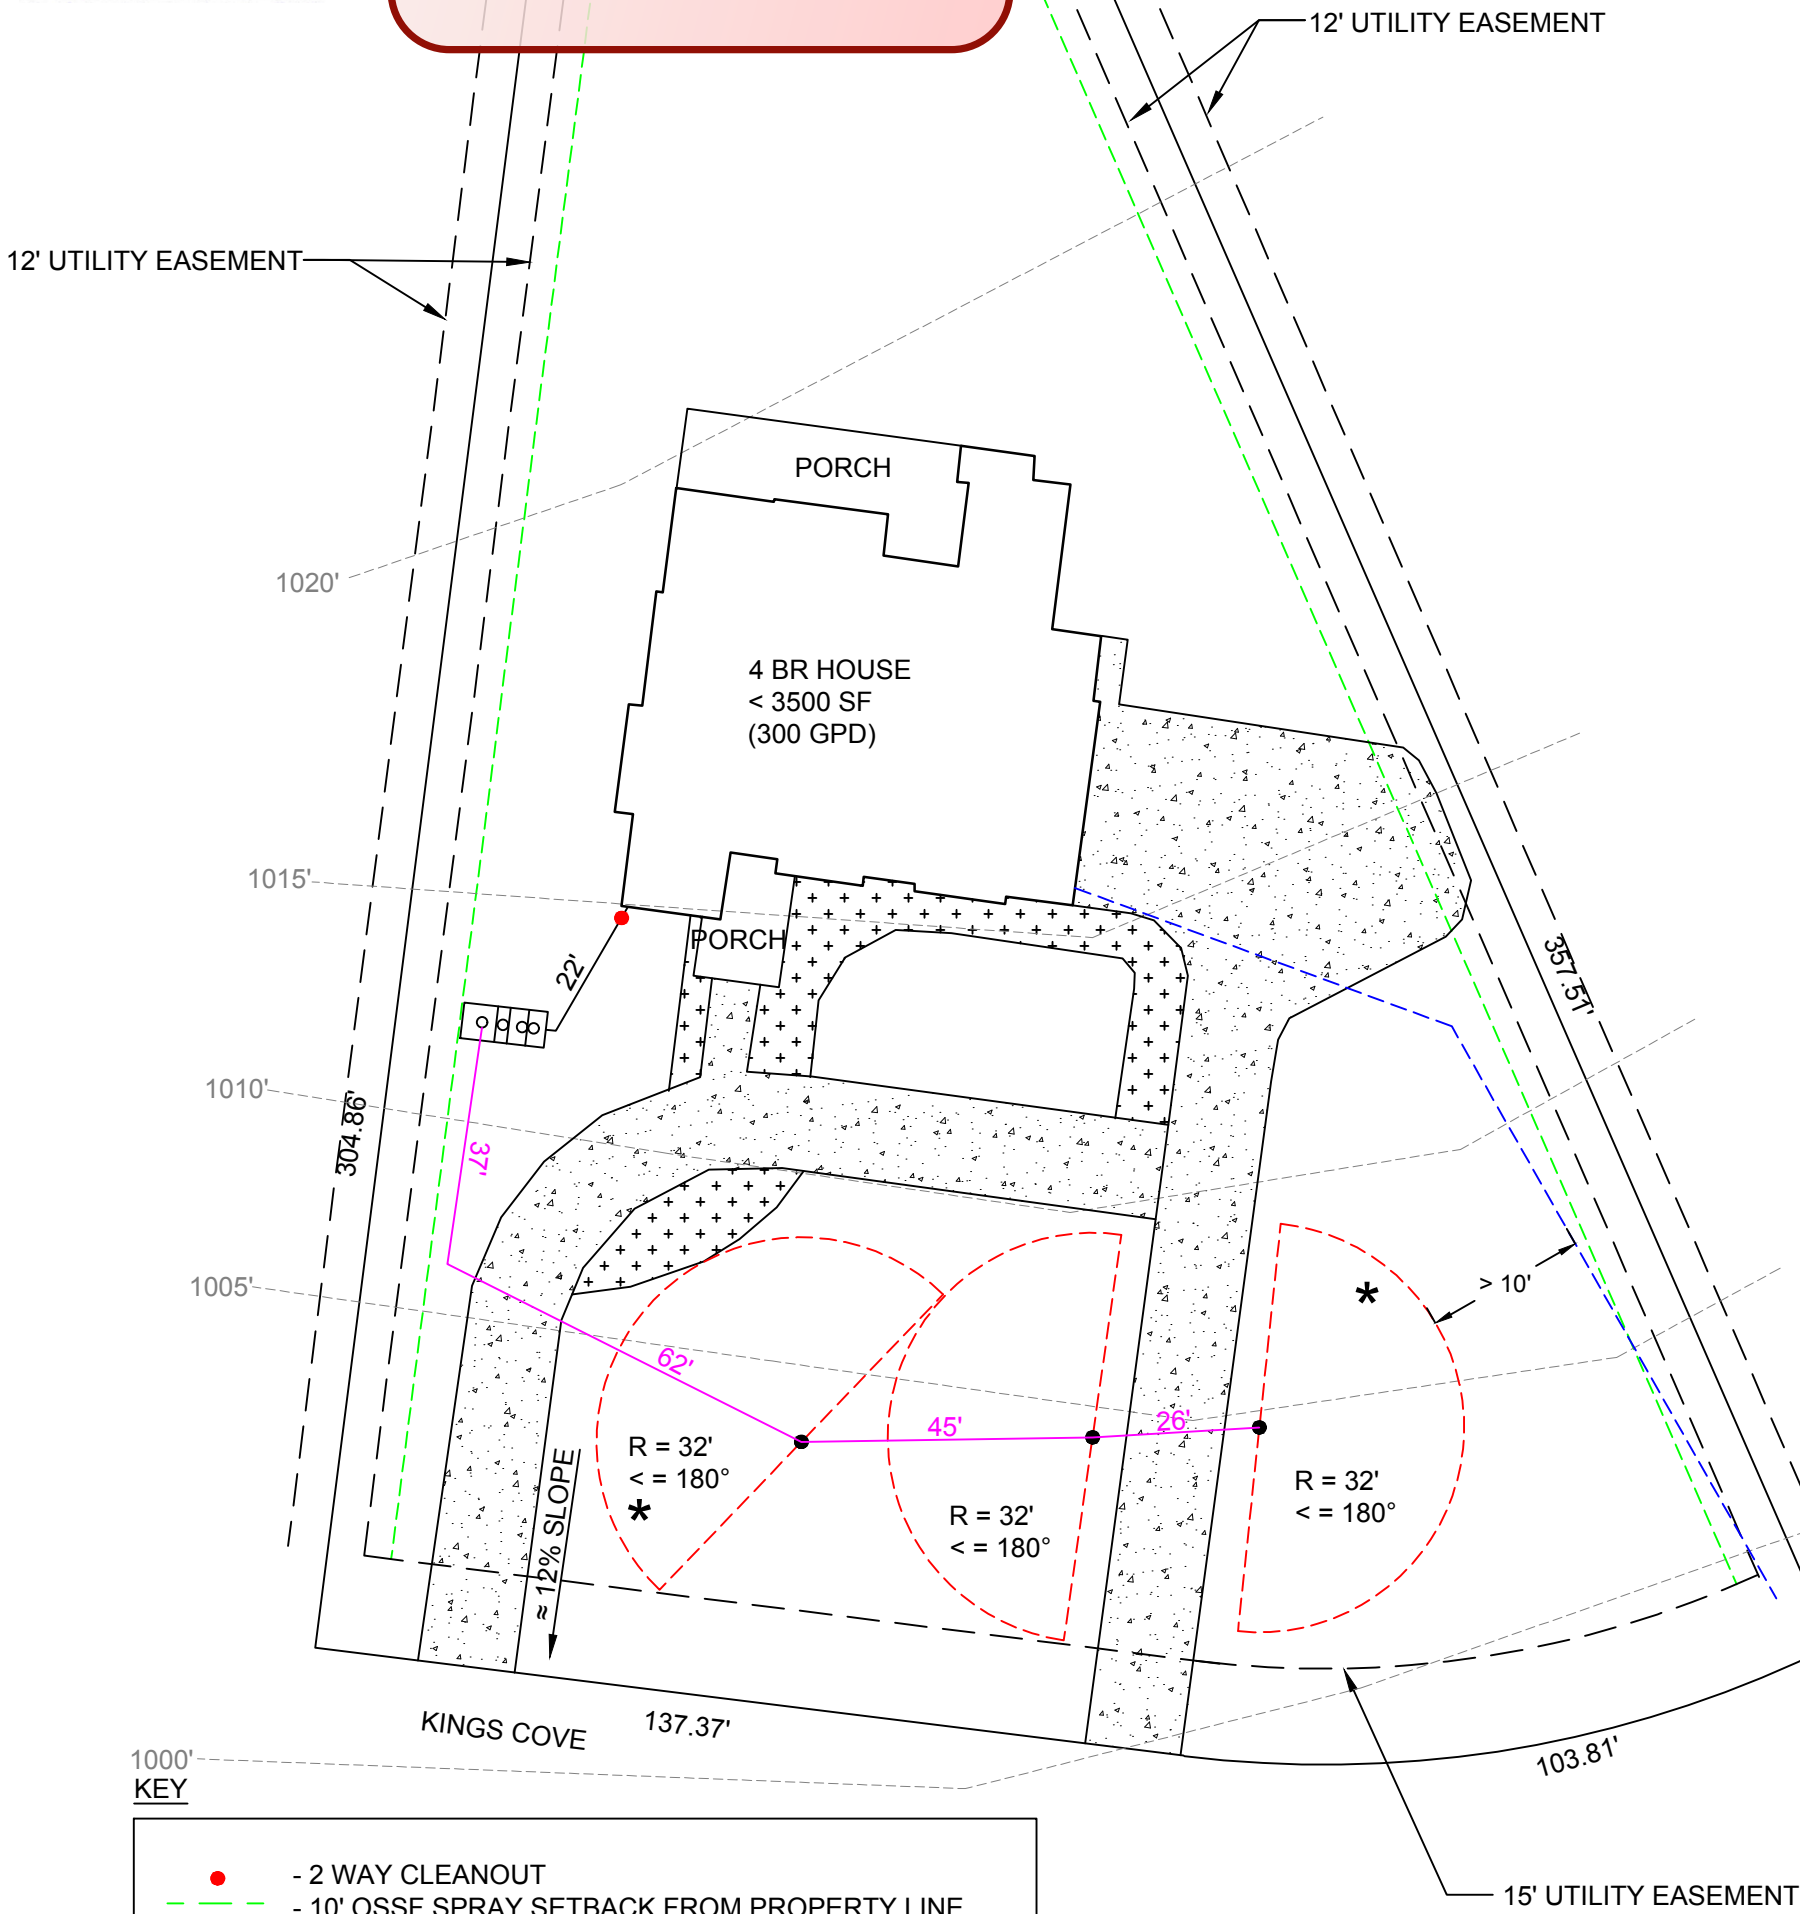


KEY

- - 2 WAY CLEANOUT
- - 10' OSSF SPRAY SETBACK FROM PROPERTY LINE
- - 1" SCH 40 PVC PURPLE PIPE
- - PROPOSED WATER LINE (VERIFY LOCATION ON SITE)
- * - TEST HOLE
- ○ ○ - 600 GPD AEROBIC TREATMENT UNIT
- ▨ - DRIVE/WALKWAY
- ▨ - LANDSCAPING

NOTES:

- 1" SCH 40 PURPLE PIPE TO ALL SPRAY HEADS.
- 1" SCH 40 PURPLE PIPE WILL BE SLEEVED IN SCH 40 PVC PIPE WHERE IT CROSSES UNDER SURFACE IMPROVEMENTS, DRIVE, WALKWAY AND 5' BEYOND. THIS WILL PROVIDE EQUIVALENT PROTECTION FOR THE OSSF SETBACK REQUIREMENTS OF TAC 285.
- 3" OR 4" SCH 40 PVC PIPE FROM STRUCTURE TO TANK.
- SEWER PIPE CONNECTING THE STRUCTURE TO THE TANK MUST HAVE AT MINIMUM 1/8" FALL PER 1'.
- TANK TO BE > 5' FROM STRUCTURES AND SURFACE IMPROVEMENTS. THIS WILL PROVIDE EQUIVALENT PROTECTION FOR THE SETBACK REQUIREMENTS OF TAC 285.
- CLEANOUT WITHIN 3' OF STRUCTURE.
- TOTAL SPRAY AREA = 4824 SF.
- TANK WILL BE WATER TIGHT AND MANUFACTURED ACCORDING TO ASTM DESIGNATION: C 1227.
- DRAINFIELD SHALL BE GREATER THAN 100' FROM PRIVATE WELLS, AND GREATER THAN 150' FROM PUBLIC WELLS. VERIFY WELL LOCATION(S) ON SITE.
- SPRAY HEADS SHALL BE LOCATED AT LEAST 10' AWAY FROM TREES WITHIN THE DISTRIBUTION AREA.

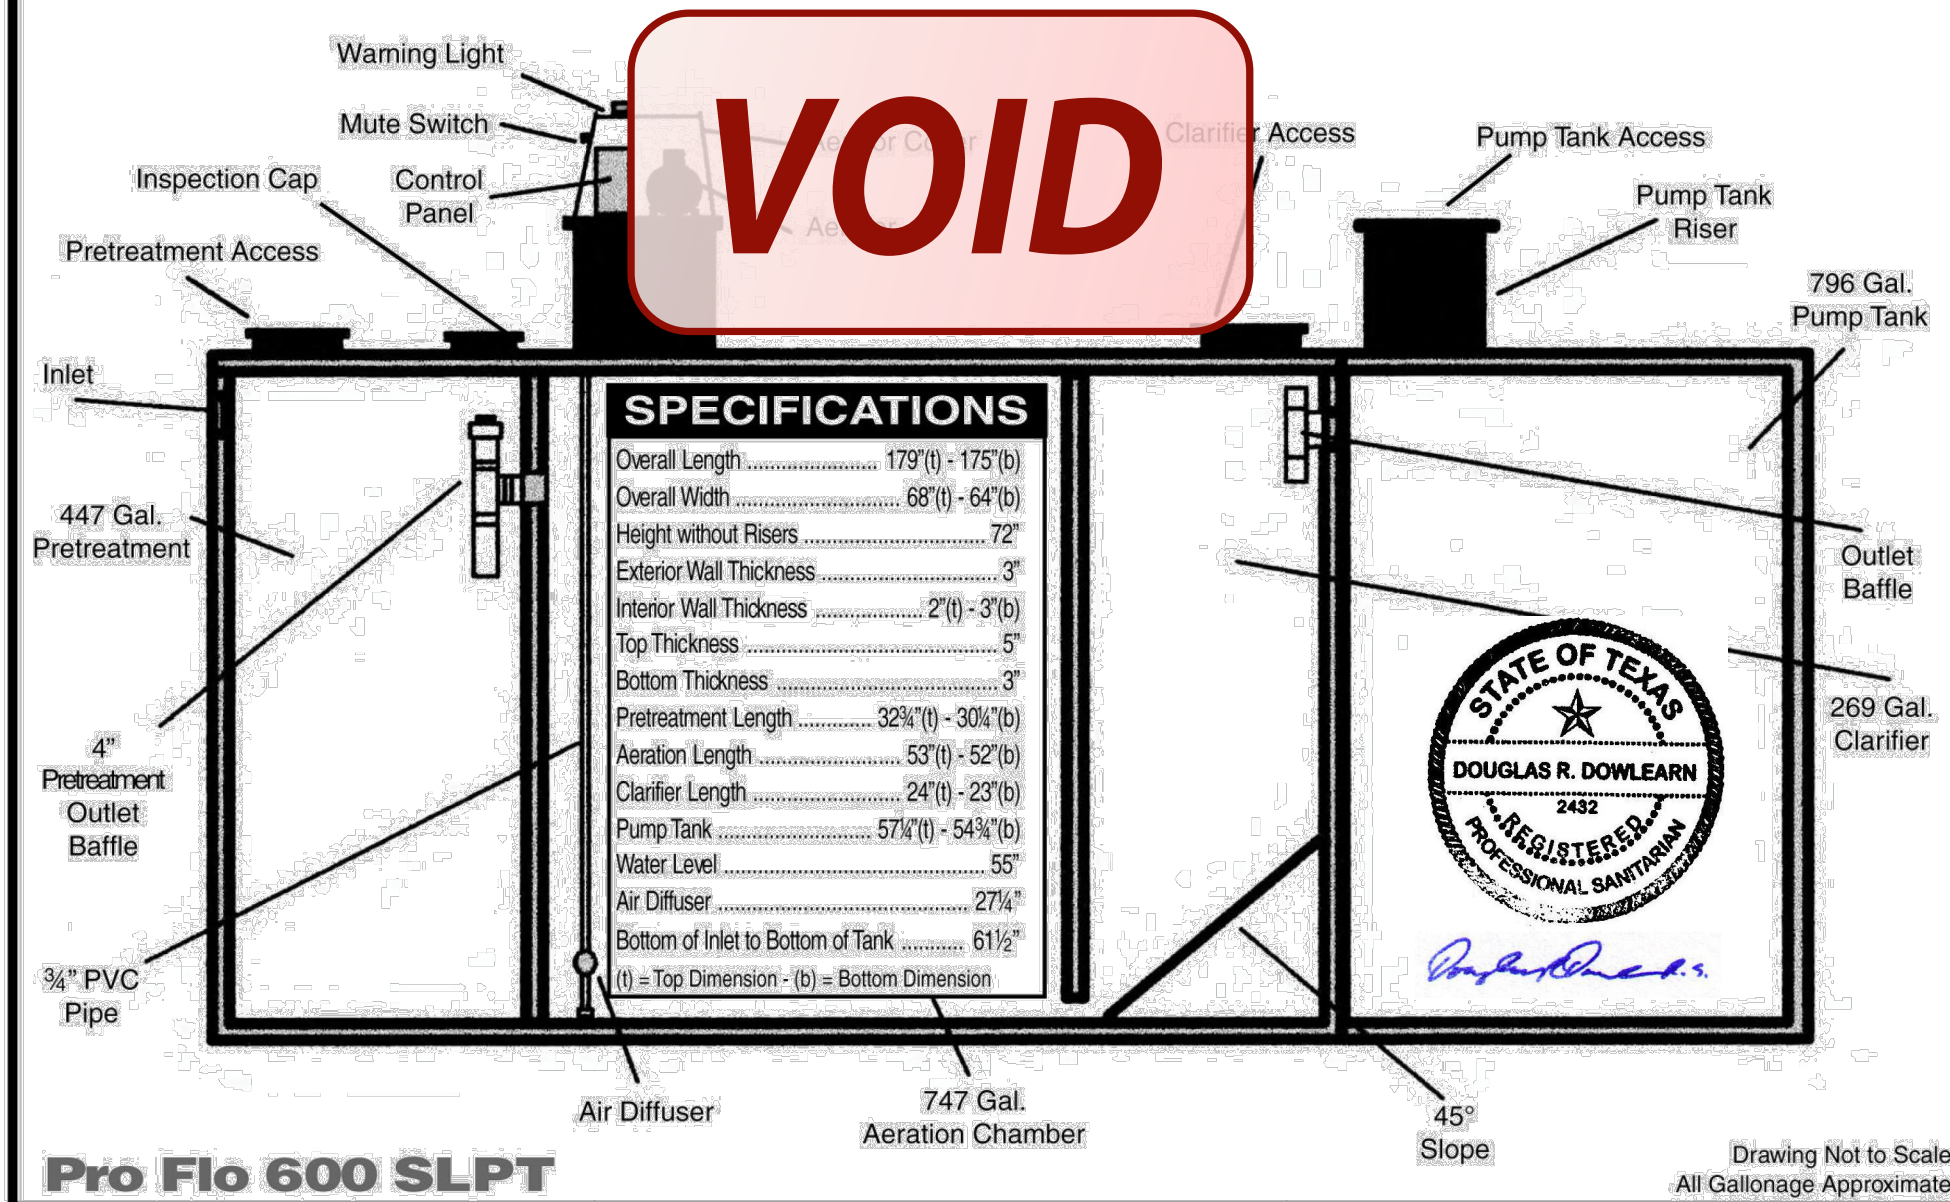**NOTES:**

- NOT TO SCALE.
- SET TO ACTIVATE IN PRE DAWN HOURS OF
MIDNIGHT TO 5:00 AM.

14.47 GALLONS PER INCH

46" - 55" = RESERVE(130.23 GALLONS)

46" = ALARM ON

12" - 46" - WORKING LEVEL (491.91 GALLONS)

10" - 12" = ON/OFF TETHER (28.94 GALLONS)

0" - 10" = SUMP (144.7 GALLONS)

Drawing Not to Scale
All Gallonage Approximate

C1 SERIES

CISTERN PUMPS

Designed for use in gray water / filtered effluent service applications, the C1 Series cistern pump provides high performance and long life in less than ideal water conditions. The C1 Series pump is able to pass solids up to 1/8" without having a negative effect on the internal hydraulic components.


The pump's unique bottom suction design allows for maximum fluid drawdown without compromising durability or overall life, and it does not require the use of a flow induction sleeve. Intended specifically for use in a cistern or tank, C1 Series pumps are suitable for use in agricultural, residential, and commercial installations.



Franklin Electric

franklinwater.com

C1 Series Family Curve

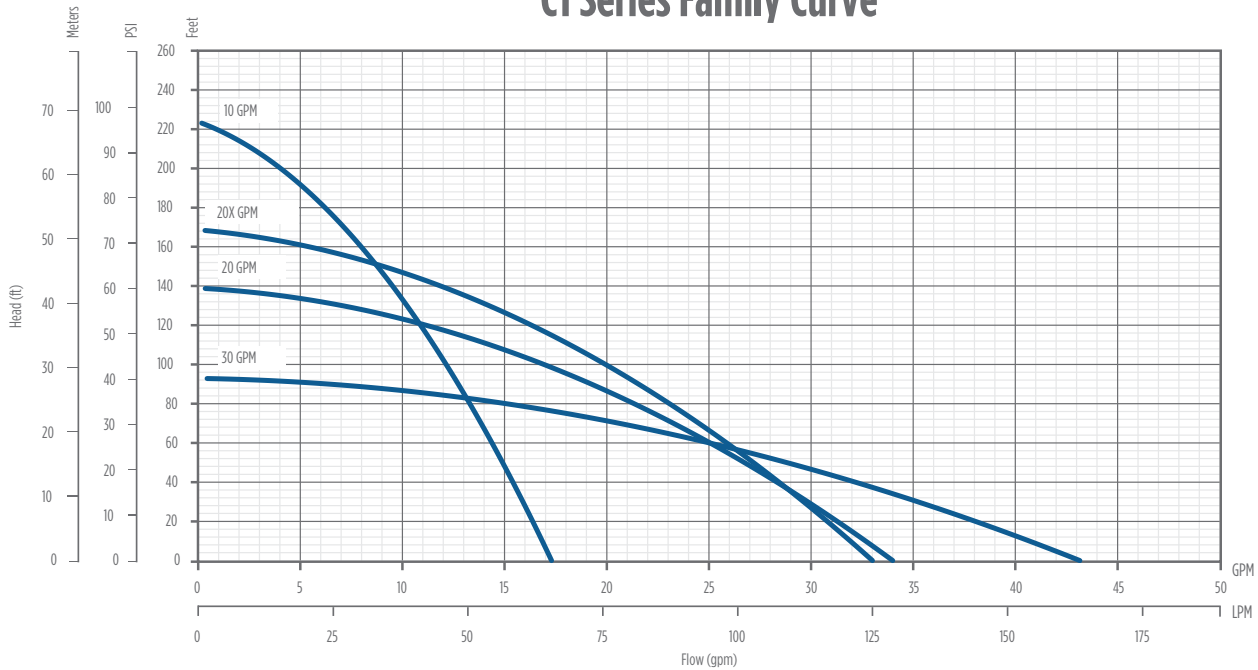

FEATURES

- Supplied with a removable 5" base for secure and reliable mounting
- Bottom suction design
- Robust thermoplastic discharge head design resists breakage during installation and operation
- Single shell housing design provides a compact unit while ensuring cool and quiet operation
- Hydraulic components molded from high quality engineered thermoplastics
- Optimized hydraulic design allows for increased performance and decreased power usage
- All metal components are made of high grade stainless steel for corrosion resistance
- Available with a high quality 115 V or 230 V, ½ hp motor
- Fluid flows of 10, 20, and 30 gpm, with a max shut-off pressure of over 100 psi
- Heavy duty 600 V 10 foot SJ00W jacketed lead

APPLICATIONS

- Gray water pumping
- Filtered effluent service water pumping
- Water reclamation projects such as pumping from rain catchment basins
- Aeration and other foundation or pond applications
- Agriculture and livestock water pumping

ORDERING INFORMATION

C1 Series Pumps							
GPM	HP	Volts	Stage	Model No.	Order No.	Length (in)	Weight (lbs)
10	1/2	115	7	10C1-05P4-2W115	90301005	26	17
		230	7	10C1-05P4-2W230	90301010	26	17
20		115	5	20C1-05P4-2W115	90302005	25	16
		230	5	20C1-05P4-2W230	90302010	25	16
20X		115	6	20XC1-05P4-2W115	90302015	26	17
		230	6	20XC1-05P4-2W230	90302020	26	17
30		115	4	30C1-05P4-2W115	90303005	25	16
		230	4	30C1-05P4-2W230	90303010	25	16

Note: All units have 10 foot long SJ00W leads.



Franklin Electric

franklinwater.com

M1698 07-14

From: [Ritzen,Brenda](#)
To: ["Lauren Dowlearn"](#)
Subject: RE: Permit 118025
Date: Tuesday, November 12, 2024 8:57:00 AM
Attachments: [118025.pdf](#)
[image001.png](#)

Lauren :

A copy of the Permit to Construct is attached.

Thank you,



Brenda Ritzen
Environmental Health Coordinator
195 David Jonas Dr.
New Braunfels, TX 78132
DR:OS00007722
830-608-2090
www.cceo.org

From: Ritzen,Brenda
Sent: Tuesday, November 12, 2024 8:57 AM
To: Lauren Dowlearn <txseptic@gmail.com>
Subject: RE: Permit 118025

Lauren,

The permit file has been updated.

Thank you,



Brenda Ritzen
Environmental Health Coordinator
195 David Jonas Dr.
New Braunfels, TX 78132
DR:OS00007722
830-608-2090
www.cceo.org

From: [Ritzen,Brenda](#)
To: [Lauren Dowlearn](#)
Subject: Permit 118025
Date: Tuesday, November 5, 2024 3:36:00 PM
Attachments: [image001.png](#)

Re: Brant Shalek
Kings Cove Section 6 Lot 57
Application for Permit for Authorization to Construct an On-Site Sewage Facility (OSSF)

Lauren :

The following information is needed before I can continue processing the referenced permit submittal:

- ✓. Maintain required 20 ft. setback from the edge of the spray areas to the property lines.
2. Revise as needed and resubmit.

Thank you,



Brenda Ritzen
Environmental Health Coordinator
195 David Jonas Dr.
New Braunfels, TX 78132
DR:OS00007722
830-608-2090
www.cceo.org

Independence Title Company
NCGF# 8059051-NBF

GENERAL WARRANTY DEED

NOTICE OF CONFIDENTIALITY RIGHTS: IF YOU ARE A NATURAL PERSON, YOU MAY REMOVE OR STRIKE ANY OR ALL OF THE FOLLOWING INFORMATION FROM ANY INSTRUMENT THAT TRANSFERS AN INTEREST IN REAL PROPERTY BEFORE IT IS FILED FOR RECORD IN THE PUBLIC RECORDS: YOUR SOCIAL SECURITY NUMBER OR YOUR DRIVER'S LICENSE NUMBER.

DATE: October 23, 2020

GRANTOR: Evan Pena

GRANTOR'S MAILING ADDRESS: 28238 Pass Knoll San Antonio,
TX 78266

GRANTEE: Brant Shalek

GRANTEE'S MAILING ADDRESS: 1623 Sunshine Peak
New Braunfels, TX 78130

CONSIDERATION:

Cash and other valuable consideration.

PROPERTY (including any improvements):

Lot 35, Block 2, KINGS COVE UNIT ONE, according to the map or plat thereof, recorded in Volume 11, Page 367, Map and Plat Records, Comal County, Texas.

RESERVATIONS FROM AND EXCEPTIONS TO CONVEYANCE AND WARRANTY:

This conveyance is made and accepted subject to all restrictions, covenants, conditions, rights-of-way, assessments, outstanding royalty and mineral reservations and easements, if any, affecting the above described property that are valid, existing and properly of record as of the date hereof and subject, further, to taxes for the year 2020 and subsequent years.

Grantor, for the consideration and subject to the reservations from and exceptions to conveyance and warranty, grants, sells and conveys to Grantee the property, together with all and singular the rights and appurtenances thereto in anywise belonging, to have and hold it to Grantee, Grantee's heirs, executors, administrators, successors, or assigns forever. Grantor binds Grantor and Grantor's heirs, executors, administrators, successors and assigns to warrant and forever defend all and singular the property to Grantee and Grantee's heirs, executors, administrators,

successors and assigns against every person whomsoever lawfully claiming or to claim the same or any part thereof, except as to the reservations from and exceptions to conveyance and warranty.

When the context requires, singular nouns and pronouns include the plural.


Evan Pena
Evan Pena

NOTICE: This instrument was prepared by Hancock McGill & Bleau, LLLP (HMB) at the request of Independence Title or the parties using information provided by the title company and the parties. Unless we have been provided with a copy of any contracts related to this transaction or been informed of any reservations required by the seller, the reservations will not be included in this warranty deed and by accepting this deed, all parties release HMB from any liability resulting from the failure to include undisclosed reservations. We have not investigated or verified information provided to us and do not warrant the validity of the information or quality of title to the real estate described above. We do not represent the parties named in this instrument. The parties should seek independent legal counsel for advice concerning the effect and consequences of this instrument.

Acknowledgement

State of Texas
County of Comal

This instrument was acknowledged before me on the 23rd day of October, 2020, by Evan Pena.



Nicole R. Cantu
Notary Public, State of Texas

Prepared By:
Hancock McGill & Bleau, LLLP
Attorneys at Law
File No. 2059051

After Recording Return To:

After recording, return to:
INDEPENDENCE TITLE COMPANY
417 W. San Antonio, Suite 100
New Braunfels, TX 78130
Do9051-fw


GENERAL WARRANTY DEED

Page 2

Filed and Recorded
Official Public Records
Bobbie Koepp, County Clerk
Comal County, Texas
10/26/2020 11:32:47 AM
CHRISTY 2 Pages(s)
202006047440



Bobbie Koepp



OSSF DEVELOPMENT APPLICATION CHECKLIST

Staff will complete shaded items

		118025
<i>Date Received</i>	<i>Initials</i>	<i>Permit Number</i>

Instructions:

Place a check mark next to all items that apply. For items that do not apply, place "N/A". This OSSF Development Application Checklist **must** accompany the completed application.

OSSF Permit

- ☒ Completed Application for Permit for Authorization to Construct an On-Site Sewage Facility and License to Operate
- ☒ Site/Soil Evaluation Completed by a Certified Site Evaluator or a Professional Engineer
- ☒ Planning Materials of the OSSF as Required by the TCEQ Rules for OSSF Chapter 285. Planning Materials shall consist of a scaled design and all system specifications.
- ☒ Required Permit Fee - See Attached Fee Schedule
- ☒ Copy of Recorded Deed
- ☒ Surface Application/Aerobic Treatment System
 - ☒ Recorded Certification of OSSF Requiring Maintenance/Affidavit to the Public
 - ☒ Signed Maintenance Contract with Effective Date as Issuance of License to Operate

I affirm that I have provided all information required for my OSSF Development Application and that this application constitutes a completed OSSF Development Application.

DocuSigned by:

Brant Shalek

FFB97B4CB9A24C5

Signature of Applicant

Signed by:

Miranda Shalek

14365FE6178E487...

10/4/2024

Date

___ COMPLETE APPLICATION

Check No. _____ Receipt No. _____

INCOMPLETE APPLICATION
____ (Missing Items Circled, Application Refeused)
