

Comal County Environmental Health

OSSF Inspection Sheet

Installer Name: _____

OSSF Installer #: _____

1st Inspection Date: _____

2nd Inspection Date: _____

3rd Inspection Date: _____

Inspector Name: _____

Inspector Name: _____

Inspector Name: _____

Permit#:

Address:

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
1	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Site and Soil Conditions Consistent with Submitted Planning Materials		285.31(a) 285.30(b)(1)(A)(iv) 285.30(b)(1)(A)(v) 285.30(b)(1)(A)(iii) 285.30(b)(1)(A)(ii) 285.30(b)(1)(A)(i)				
2	SITE AND SOIL CONDITIONS & SETBACK DISTANCES Setback Distances Meet Minimum Standards		285.91(10) 285.30(b)(4) 285.31(d)				
3	SEWER PIPE Proper Type Pipe from Structure to Disposal System (Cast Iron, Ductile Iron, Sch. 40, SDR 26)		285.32(a)(1)				
4	SEWER PIPE Slope from the Sewer to the Tank at least 1/8 Inch Per Foot		285.32(a)(3)				
5	SEWER PIPE Two Way Sanitary - Type Cleanout Properly Installed (Add. C/O Every 100' &/or 90 degree bends)		285.32(a)(5)				
6	PRETREATMENT Installed (if required) TCEQ Approved List PRETREATMENT Septic Tank(s) Meet Minimum Requirements		285.32(b)(1)(G) 285.32(b)(1)(E)(iii) 285.32(b)(1)(E)(iv) 285.32(b)(1)(F) 285.32(b)(1)(B) 285.32(b)(1)(C)(i) 285.32(b)(1)(C)(ii) 285.32(b)(1)(D) 285.32(b)(1)(E) 285.32(b)(1)(A) 285.32(b)(1)(E)(ii)(II) 285.32(b)(1)(E)(i) 285.32(b)(1)(E)(ii)(I)				
7	PRETREATMENT Grease Interceptors if required for commercial		285.34(d)				

Inspector Notes:

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
8	SEPTIC TANK Tank(s) Clearly Marked SEPTIC TANK If Single Tank, 2 Compartments Provided with Baffle SEPTIC TANK Inlet Flowline Greater than 3" and " T " Provided on Inlet and Outlet SEPTIC TANK Septic Tank(s) Meet Minimum Requirements		285.32(b)(1) (E) 285.91(2) 285.32(b)(1) (F) 285.32(b)(1)(E) (iii) 285.32(b)(1)(E)(ii) (II) 285.32(b)(1)(E)(ii) (I) 285.32(b)(1)(E) (i) 285.32(b)(1) (D) 285.32(b)(1)(C) (ii) 285.32(b)(1)(C) (i) 285.32(b)(1) (B) 285.32(b)(1) (A) 285.32(b)(1)(E)(iv)				
9	ALL TANKS Installed on 4" Sand Cushion/ Proper Backfill Used		285.32(b)(1)(F) 285.32(b)(1)(G) 285.34(b)				
10	SEPTIC TANK Inspection / Clean Out Port & Risers Provided on Tanks Buried Greater than 12" Sealed and Capped		285.38(d)				
11	SEPTIC TANK Secondary restraint system provided SEPTIC TANK Riser permanently fastened to lid or cast into tank SEPTIC TANK Riser cap protected against unauthorized intrusions		285.38(d) 285.38(e)				
12	SEPTIC TANK Tank Volume Installed						
13	PUMP TANK Volume Installed						
14	AEROBIC TREATMENT UNIT Size Installed						
15	AEROBIC TREATMENT UNIT Manufacturer AEROBIC TREATMENT UNIT Model Number						
16	DISPOSAL SYSTEM Absorptive		285.33(a)(4) 285.33(a)(1) 285.33(a)(2) 285.33(a)(3)				
17	DISPOSAL SYSTEM Leaching Chamber		285.33(a)(1) 285.33(a)(3) 285.33(a)(4) 285.33(a)(2)				
18	DISPOSAL SYSTEM Evapo-transpirative		285.33(a)(3) 285.33(a)(4) 285.33(a)(1) 285.33(a)(2)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
19	DISPOSAL SYSTEM Drip Irrigation		285.33(c)(3)(A)-(F)				
20	DISPOSAL SYSTEM Soil Substitution		285.33(d)(4)				
21	DISPOSAL SYSTEM Pumped Effluent		285.33(a)(4) 285.33(a)(3) 285.33(a)(1) 285.33(a)(2)				
22	DISPOSAL SYSTEM Gravelless Pipe		285.33(a)(3) 285.33(a)(2) 285.33(a)(4) 285.33(a)(1)				
23	DISPOSAL SYSTEM Mound		285.33(a)(3) 285.33(a)(1) 285.33(a)(2) 285.33(a)(4)				
24	DISPOSAL SYSTEM Other (describe) (Approved Design)		285.33(d)(6) 285.33(c)(4)				
25	DRAINFIELD Absorptive Drainline 3" PVC or 4" PVC						
26	DRAINFIELD Area Installed						
27	DRAINFIELD Level to within 1 inch per 25 feet and within 3 inches over entire excavation		285.33(b)(1)(A)(v)				
28	DRAINFIELD Excavation Width DRAINFIELD Excavation Depth DRAINFIELD Excavation Separation DRAINFIELD Depth of Porous Media DRAINFIELD Type of Porous Media						
29	DRAINFIELD Pipe and Gravel - Geotextile Fabric in Place		285.33(b)(1)(E)				
30	DRAINFIELD Leaching Chambers DRAINFIELD Chambers - Open End Plates w/Splash Plate, Inspection Port & Closed End Plates in Place (per manufacturers spec.)		285.33(c)(2)				
31	LOW PRESSURE DISPOSAL SYSTEM Adequate Trench Length & Width, and Adequate Separation Distance between Trenches		285.33(d)(1)(C)(i)				

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
32	EFFLUENT DISPOSAL SYSTEM Utilized Only by Single Family Dwelling EFFLUENT DISPOSAL SYSTEM Topographic Slopes < 2.0% EFFLUENT DISPOSAL SYSTEM Adequate Length of Drain Field (1000 Linear ft. for 2 bedrooms or Less & an additional 400 ft. for each additional bedroom) EFFLUENT DISPOSAL SYSTEM Lateral Depth of 18 inches to 3 ft. & Vertical Separation of 1ft on bottom and 2 ft. to restrictive horizon and ground water respectfully EFFLUENT DISPOSAL SYSTEM Lateral Drain Pipe (1.25 - 1.5" dia.) & Pipe Holes (3/16 - 1/4" dia. Hole Size) 5 ft. Apart		285.33(b)(3)(A) 285.33(b)(3)(A) 285.33(b)(3)(B)285.91(13) 285.33(b)(3)(D) 285.33(b)(3)(F)				
33	AEROBIC TREATMENT UNIT Is Aerobic Unit Installed According to Approved Guidelines.		285.32(c)(1)				
34	AEROBIC TREATMENT UNIT Inspection/Clean Out Port & Risers Provided AEROBIC TREATMENT UNIT Secondary restraint system provided AEROBIC TREATMENT UNIT Riser permanently fastened to lid or cast into tank AEROBIC TREATMENT UNIT Riser cap protected against unauthorized intrusions						
35	AEROBIC TREATMENT UNIT Chlorinator Properly Installed with Chlorine Tablets in Place.						
36	PUMP TANK Is the Pump Tank an approved concrete tank or other acceptable materials & construction PUMP TANK Sampling Port Provided in the Treated Effluent Line PUMP TANK Check Valve and/or Anti- Siphon Device Present When Required PUMP TANK Audible and Visual High Water Alarm Installed on Separate Circuit From Pump						
37	PUMP TANK Inspection/Clean Out Port & Risers Provided PUMP TANK Secondary restraint system provided PUMP TANK Riser permanently fastened to lid or cast into tank PUMP TANK Riser cap protected against unauthorized intrusions						
38	PUMP TANK Secondary restraint system provided						
39	PUMP TANK Electrical Connections in Approved Junction Boxes / Wiring Buried						

**Comal County Environmental Health
OSSF Inspection Sheet**

No.	Description	Answer	Citations	Notes	1st Insp.	2nd Insp.	3rd Insp.
40	APPLICATION AREA Distribution Pipe, Fitting, Sprinkler Heads & Valve Covers Color Coded Purple?		285.33(d)(2)(G)(iii)(II) 285.33(d)(2)(G)(iii)(III) 285.33(d)(2)(G)(v) 285.33(d)(2)(G)(iii) 285.33(d)(2)(G)(iv) 285.33(d)(2)(G)(i) 285.33(d)(2)(G)(ii) 285.33(d)(2)(G)(iii)(I)				
41	APPLICATION AREA Low Angle Nozzles Used / Pressure is as required APPLICATION AREA Acceptable Area, nothing within 10 ft of sprinkler heads? APPLICATION AREA The Landscape Plan is as Designed		285.33(d)(2)(G) (i)285.33(d)(2) (A)285.33(d)(2)(F)				
42	APPLICATION AREA Area Installed						
43	PUMP TANK Meets Minimum Reserve Capacity Requirements						
44	PUMP TANK Material Type & Manufacturer						
45	PUMP TANK Type/Size of Pump Installed						



COMAL COUNTY

ENGINEER'S OFFICE

Permit of Authorization to Construct an On-Site Sewage Facility Permit Valid For One Year From Date Issued

Permit Number: 118411
Issued This Date: 03/28/2025
This permit is hereby given to: Theodore and Madeline Bartling

To start construction of a private, on-site sewage facility located at:

5926 COLIN RDG
NEW BRAUNFELS, TX 78132

Subdivision: Copper Ridge, The Addition North Phase
Unit: -
Lot: 53
Block: M
Acreage: 2.0400

APPROVED MINIMUM SIZES AS PER ATTACHED DESIGN

Type of System: Aerobic
Surface Irrigation

This permit gives permission for the construction of the above referenced on-site facility to commence. Installation must be completed by an installer holding a valid registration card from the Texas Commission on Environmental Quality (TCEQ). Installation and inspection must comply with current TCEQ and Comal County requirements.

Call (830) 608-2090 to schedule inspections.



ON-SITE SEWAGE FACILITY APPLICATION

Date _____ Permit Number 118411

1. APPLICANT / AGENT INFORMATION

Owner Name Theodore Adams Bartling Jr. Agent Name Doug Dowlearn R.S.
 Mailing Address 827 Dreisam and Madeline Paige Bartling Agent Address 703 Oak Dr.
 City, State, Zip New Braunfels, TX 78130 City, State, Zip Blanco, TX 78606
 Phone # _____ Phone # 210-878-8100
 Email _____ Email TXSEPTIC@GMAIL.COM

2. LOCATION

Subdivision Name Copper Ridge, The Addition North Phase Unit _____ Lot 53 Block M
 Survey Name / Abstract Number _____ Acreage 2.04
 Address 5926 Colin Ridge City New Braunfels State TX Zip 78132

3. TYPE OF DEVELOPMENT

☒ Single Family ResidentialType of Construction (House, Mobile, RV, Etc.) HOUSENumber of Bedrooms 4Indicate Sq Ft of Living Area 3232☐ Non-Single Family Residential

(Planning materials must show adequate land area for doubling the required land needed for treatment units and disposal area)

Type of Facility _____

Offices, Factories, Churches, Schools, Parks, Etc. - Indicate Number Of Occupants _____

Restaurants, Lounges, Theaters - Indicate Number of Seats _____

Hotel, Motel, Hospital, Nursing Home - Indicate Number of Beds _____

Travel Trailer/RV Parks - Indicate Number of Spaces _____

Miscellaneous _____

Estimated Cost of Construction: \$ 996,005 (Structure Only)

Is any portion of the proposed OSSF located in the United States Army Corps of Engineers (USACE) flowage easement?

☐ Yes ☒ No (If yes, owner must provide approval from USACE for proposed OSSF improvements within the USACE flowage easement)Source of Water ☒ Public ☐ Private Well ☐ Rainwater

. SIGNATURE OF OWNER

By signing this application, I certify that:

The completed application and all additional information submitted does not contain any false information and does not conceal any material facts. I certify that I am the property owner or I possess the appropriate land rights necessary to make the permitted improvements on said property.

Authorization is hereby given to the permitting authority and designated agents to enter upon the above described property for the purpose of site/soil evaluation and inspection of private sewage facilities..

I understand that a permit of authorization to construct will not be issued until the Floodplain Administrator has performed the reviews required by the Comal County Flood Damage Prevention Order.

I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.

1/20/2025
1/20/2025



ON-SITE SEWAGE FACILITY APPLICATION

Planning Materials & Site Evaluation as Required Completed By Doug Dowlearn R.S.

REVISED

8:56 am, Mar 28, 2025

System Description Aerobic with spray disposal

Size of Septic System Required Based on Planning Materials & Soil Evaluation

Tank Size(s) (Gallons) 600 Absorption/Application Area (Sq Ft) 4688

Gallons Per Day (As Per TCEQ Table III) 300

(Sites generating more than 5000 gallons per day are required to obtain a permit through TCEQ.)

Is the property located over the Edwards Recharge Zone? ☒ Yes ☐ No

(If yes, the planning materials must be completed by a Registered Sanitarian (R.S.) or Professional Engineer (P.E.))

Is there an existing TCEQ approved WPAP for the property? ☒ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design complies with all provisions of the existing WPAP.)

Is there at least one acre per single family dwelling as per 285.40(c)(1)? ☒ Yes ☐ No

If there is no existing WPAP, does the proposed development activity require a TCEQ approved WPAP? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed WPAP. A Permit to Construct will not be issued for the proposed OSSF until the proposed WPAP has been approved by the appropriate regional office.)

Is the property located over the Edwards Contributing Zone? ☐ Yes ☒ No

Is there an existing TCEQ approval CZP for the property? ☐ Yes ☒ No

(If yes, the P.E. or R.S. shall certify that the OSSF design complies with all provisions of the existing CZP.)

If there is no existing CZP, does the proposed development activity require a TCEQ approved CZP? ☐ Yes ☒ No

(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed CZP. A Permit to Construct will not be issued for the proposed OSSF until the CZP has been approved by the appropriate regional office.)

Is this property within an incorporated city? ☐ Yes ☒ No

If yes, indicate the city:

By signing this application, I certify that:

- The information provided above is true and correct to the best of my knowledge.

- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.



Signature of Designer

3/27/2025

Date

1/c



202506002261 01/24/2025 09:34:03 AM 1/1

**COUNTY OF COMAL
STATE OF TEXAS**

AFFIDAVIT TO THE PUBLIC

CERTIFICATION OF OSSF REQUIRING MAINTENANCE

According to Texas Commission on Environmental Quality (TCEQ) Rules for On-Site Sewage Facilities (OSSFs), this document is filed in the Deed Records of Comal County, Texas.

I
The Texas Health and Safety Code, Chapter 366 authorizes the Texas Commission on Environmental Quality (TCEQ) to regulate on-site sewage facilities (OSSFs). Additionally, the Texas Water Code (TWC), § 5.012 and § 5.013, give the commission primary responsibility for implementing the laws of the State of Texas relating to water and adopting rules necessary to carry out its powers and duties under the TWC. The commission, under the authority of the TWC and the Texas Health and Safety Code, requires owners to provide notice to the public that certain types of OSSFs are located on specific pieces of property. To achieve this notice, the commission requires a recorded affidavit. Additionally, the owner must provide proof of the recording to the OSSF permitting authority. This recorded affidavit is not a representation or warranty by the commission of the suitability of this OSSF, nor does it constitute any guarantee by the commission that the appropriate OSSF was installed.

II
An OSSF requiring a maintenance contract, according to 30 Texas Administrative Code § 285.91 (12) will be installed on the property described as (insert legal description):

Copper Ridge, The Addition North Phase, Lot 53, Block M

The property is owned by (Insert owner's full name):

Theodore Adams Bartling Jr. and Madeline Paige Bartling

This OSSF must be covered by a continuous maintenance contract for the first two years. After the initial two-year service policy, the owner of an aerobic treatment system for a single family residence shall either obtain a maintenance contract within 30 days or maintain the system personally.

Upon sale or transfer of the above described property, the permit for the OSSF shall be transferred to the buyer or new owner. A copy of the planning materials for OSSF may be obtained from **Comal County Engineer's Office**.


WITNESS BY HAND(S) ON THIS 24 DAY OF January 2025

Owner(s) signature(s)

Madeline Bartling
Theodore Bartling
(PRINTED NAME) /TITLE

SWORN TO AND SUBSCRIBED BEFORE ME ON THIS 24 DAY OF January 2025

Notary Public, State of Texas
Notary's Printed Name: Peyton Kieslich
My Commission Expires: 7/30/25



Filed and Recorded
Official Public Records
Bobbie Koepf, County Clerk
Comal County, Texas
01/24/2025 09:34:03 AM
MARY 1 Page(s)
202506002261



Bobbie Koepf



PERMIT#

On-Site Sewage Facility (OSSF) Service Agreement

- I. **General:** This Work for Hire Agreement (hereinafter referred to as "Agreement") is entered into by and between Theodore Adams Bartling Jr., (hereinafter referred to as "Client") and SOTX Septic Services (hereinafter to as "Contractor"). By this agreement, Contractor agrees to render services, as described herein, and the Client agrees to fulfill his/her/their responsibilities under this agreement as described herein.
- II. **Effective Dates:** This agreement commences on receipt of full payment and runs for two (2) years. Agreement's... Starting Date: (Date License to Operate is Issued) Ending Date: (2yrs. From Date of LTO)
- III. **Services by Contractor:** Contractor will provide the following services (hereinafter referred to as the "Services"):
1. In compliance with Agency (TCEQ and/or County) and manufacturer's requirements, inspect and perform routine maintenance on the On-Site Sewage Facility (hereinafter referred to as the "OSSF") three (3) times per year (approximately once every four (4) months).
 2. Report to the appropriate regulatory authority and to the Client, as is required by both the State's on-site rules and the local Agency's rules, if more stringent. All findings must be reported to the local Agency within 14 days.
 3. If any components of the OSSF are found to need repair during the inspection, the Contractor will notify the Client of the repairs needed.
 4. Visit in response to Client's request(s) for unscheduled service(s) within two business days from the date of Contractor's receipt of Client's request. All unscheduled responses are in addition to the fee covered by this Agreement and will be billed to the Client.
 5. Provide notification of arrival to site to the homeowner or to site personnel. Additionally, written notification of the visit will be left at the site or with site personnel upon completion or inspection, as well as, forwarded to agency within 14 days.
- IV. **Site Location:** The Services are to be performed at the property located at:
5926 Colin Ridge
- V. **Payment(s):** The fee for this Agreement only covers the Services describes herein. This fee does not cover equipment, parts or labor supplied for the repairs or charges for unscheduled Client-request trips to the site. Payments for such additional services are due when service is provided or rendered. Payments not received within 30 days from due date will be subjected to a \$20.00 late penalty and / or a 1.5% carrying charge, whichever is greater, in addition the reasonable attorney's fees and all costs of collection incurred by Contractor in collection of any unpaid debt(s). By signing this contract, the Client is authorizing the Contractor to remove any parts which were installed but not paid for at the end of 30 days. The Client is still responsible for any labor costs associated with the installation and remove of said parts.

Initials...

Customer:

Contractor:

Client's Responsibilities: The Client is responsible for each and all the following:

1. Maintain chlorinator and provide proper chlorine supply, if OSSF is equipped with same.
 2. Provide all necessary yard or lawn maintenance and removal of obstacles as needed to allow the OSSF to function properly, and to allow Contractor easy access to all parts of the OSSF.
 3. Maintain a current license to operate and abide by the conditions and limitations of that license and all requirements for on-site sewage facilities (OSSF's) from the State and local regulatory agency, as well as manufacturer's recommendations.
 4. Immediately notify the Contractor and Agency of all problems with, including the failure of the OSSF.
 5. Upon receiving a written notification of services needed from the Contractor, it becomes the Client's responsibility to contact the Contractor to authorize the service. If the Client chooses to use a different contractor to perform the service, the Client's responsible for ensuring the contractor holds the proper license (installer II) and is certified by the manufacturer. Also, the Client is responsible for ensuring proper notification is given to the Agency, as required by the State and local Agency rules.
 6. Provide the Contractor with water usage records, upon request, for evaluation by the Contractor of the OSSF performance.
 7. Clients residing in Harris County should allow for samples at both the inlet and outlet to the OSSF to be obtained by the Contractor for the purpose of evaluating the OSSF's performance when requested by the Client. If these samples are sent to the lab for testing, the Client will directly pay the lab for the cost of the testing plus pay the Contractor for all man-hours expended in providing this additional service at the rate of \$75.00 per hour measured from office to site, site to lab, and lab to office, otherwise known as portal to portal.
 8. Not allow the backwash from water treatment or water conditioning equipment to enter the OSSF.
 9. Provide for pumping of tanks, when needed, at Clients expense.
 10. Maintain site drainage to prevent adverse effects on OSSF.
 11. Promptly and fully pay Contactor's bills, fees, or invoices as described herein.
- VI. **Access by Contractor:** Contractor, or personnel authorized by the Contractor, may enter the property at reasonable times without prior notice for the purpose of performing the above-described Services. Contractor will require access to the OSSF electrical and physical components, including tanks, by means of manways or risers for the purpose of evaluations required by manufacturer, and/ or rules. If such manways or risers are not in place, excavation together with other labor and materials will be required and will be billed to Client as additional service at the rate of \$75.00 per hour, plus materials billed at list price. Excavated soil is to be replaced as best as reasonably possible.
- VII. **Application or Transfer of Payments:** The fees paid for this agreement may transfer to subsequent owner(s); however, this agreement will not transfer. The subsequent owner(s) must sign a similar agreement authorizing Contractor to perform the above-described Services and accepting Client's responsibilities. This replacement Agreement must be signed and received within 30 days of transfer of ownership. Contractor will apply all funds received from Client first to any past due obligations arising from this Agreement including late charges, return check charges, and charges for repairs or services not paid within 30 days of invoicing. The consumption of the payment in this manner may lead to early termination of the agreement by Contractor.
- VIII. **Termination of Agreement:** This Agreement may be terminated by either party within 30 days written notice in the event of substantial failure to perform in accordance with its terms by the other party without fault of the terminating party. If this Agreement is so terminated, Contractor shall be paid at the rate of \$75.00 per hour for any work performed, but not yet paid. The party terminating will immediately notify the other party, the equipment manufacturer, and the regulatory agency of the termination.
- IX. **Limits of Liability:** In no event shall the Contractor be liable for indirect, consequential, incidental or punitive damages, whether in contact tort or any other theory. In no event the Contractor's liability for direct damages exceed the price for the Services described in this Agreement.
- X. **Severability:** If any provision in the Agreement shall be held to be invalid or unenforceable for any reason, the remaining provisions shall continue to be valid and enforceable. If court finds that any provision of this

Initials...

Customer:


MB

Contractor:


CDH

Agreement is invalid or unenforceable, but that by limiting such provision it would become valid and enforceable, then such provision shall be written, construed, and enforced as so limited.

- XI. **Performance of Agreement:** Commencement of performance by Contractor under this agreement is contingent on the following conditions (1) Contractor receiving a fully execute original copy of this agreement. (2) Contractor receiving payment in full for the fee as described in Section V. If the above conditions are not met, then Contractor is not obligated to perform any portion of this agreement.
- XII. **Entire Agreement:** This agreement contains the entire agreement parties, and there are no other promises or conditions in any other agreement, oral or written.

Client... (And/or authorized agent)

Printed Name: Theodore Adams Bartling Jr Signature: [Signature]

Date: 1/20/25

Printed Name: Madeline Paige Bartling Signature: [Signature]

Date: 1/20/25

Physical Address: 5926 Colin Ridge, New Braunfels Zip: 78132

Mailing Address: 827 Dreisam, Zip: 78130

Phone # 512-964-5150 Cell# 210-240-6664 County: COMAL

Email: Adrian Gate Code: Contact owner, AR code

=====Contractor=====Contractor=====

SOTX Septic Services

Clarence D. Hinds Jr Clarence D Hinds Jr.

15656 Cranes Mill Rd.

Lic #: OSSF Installer II #: OS0030965

Canyon Lake, TX 78133

Maintenance Provider #: MP0002439

830-481-3249

sotxservices@gmail.com

Installer Name: _____

Phone #: _____

Email: _____

Lic #: _____

Manufacturer: _____

GPD: 600 800 1000 Other: _____

Disposal: Spray Drip Other: _____

Initials...

Customer: _____

Contractor: CDH

OSSF SOIL EVALUATION REPORT INFORMATION

REVISED

8:56 am, Mar 28, 2025

Date: 2/21/2025**Applicant Information:****Name:** Theodore and Madeline Bartling**Address:** 827 Dreisam**City, State & Zip Code:** New Braunfels, TX 78130**Email:****Site Evaluator Information:****Name:** Doug Dowlearn**Company:** D.A.D. Services, Inc.**Address:** 703 Oak Drive**City, State & Zip:** Blanco, TX 78606**Phone:** (210)240-2101 **Fax:** (866)260-7687**Email:** txseptic@gmail.com**Property Location:****Subdivision:** Copper Ridge, The Addition North Phase **Lot:****53 Block :** M**Street/Road Address:** 5926 Colin Ridge**City :** New Braunfels **Zip:** 78132**Additional Info:** Comal County**Installer Information:****Name:****Company:****Address:****City, State & Zip:****Phone:**

Depth	Texture Class	Soil Texture	Structure (For Class III – blocky, platy or massive)	Drainage (Mottles/Water Table)	Restrictive Horizon	Observation
Soil Boring #1 60"	III	0-12" Clay Loam 12"+ Limestone	Blocky	<30% Gravel	12"+ Limestone	N/A
Soil Boring #2 60"		Same as above				

DESIGN SPECIFICATIONS

Application Rate (RA): 0.064

OSSF is designed for: 4 Bedroom 3232 Sq. Ft Residence

300 gallons per day

An aerobic with spray disposal system is to be utilized based on the site evaluation.

4688 sq. ft. disposal area required

600 gallon per day aerobic treatment unit

Calculations: Absorption Area: $Q/RA=300/0.064=4688$ Sq. Ft.

FEATURES OF SITE AREA

Presence of 100-year flood zone: NO

Existing or proposed water well in nearby area: NO

Presence of adjacent ponds, streams, water impoundments: NO

Presence of upper water shed: NO

Organized sewage service available to lot: NO

I certify that the findings of this report are based on my field observations and are accurate to the best of my ability. The site evaluation and OSSF design are subject to approval by the TCEQ or the local authorized agent. The planning materials and the OSSF design should not be considered final until a permit to construct has been issued.

Site Evaluator:**NAME:** Douglas Dowlearn**Signature:****License No.** OS9902 **Exp.** 6/30/2026**TDH:** #2432 **Exp.** 2/28/2027

D.A.D SERVICES, INC.
DOUG DOWLEARN
PO BOX 212, BULVERDE, TX 78163
Designed for:
Bartling Theodore A Jr & Madeline P

REVISED

8:54 am, Mar 28, 2025

The installation site is at block M, lot 53 of the Copper Ridge Addition North Phase subdivision in Comal County, TX. The proposed OSSF will treat the wastewater from a 4 Bedroom, 3232 sq. ft. residence. The proposed method of wastewater treatment is aerobic treatment with spray irrigation. This method was chosen because of unsuitable soil conditions.

PROPOSED SYSTEM:

A 3" or 4" PVC pipe will discharge from the residence to a pre-treatment tank, which flows into a 600 gpd aerobic treatment plant. The aerobic tank effluent flows to a storage/pump tank containing a liquid chlorinator and a single 20 gpm submersible pump. Distribution is set to spray in the pre-dawn hours of midnight to 5:00 am through 2 K-Rain Gear Driven pop-up sprinklers, with low angle (13 degrees) spray nozzles spraying at 40 psi. Each sprinkler will spray a radius of 30 feet and 360 degrees of arc. An audio and visual alarm monitoring both high water and aerator failure will be placed in a noticeable location.

DESIGN SPECIFICATIONS:

Daily Waste Flow: 300 gpd
Application rate: 0.064
Application area required: $300/.064 = 4688$ sq. ft.
Application area utilized: 5654 sq. ft.
Pump tank reserve capacity: 100 gal minimum



Douglas R. Dowlearn

SYSTEM COMPONENTS:

SCH 40 PVC sewer line
Clearstream 600NC3T
Pretreatment tank
600 GPD Aerobic Treatment Unit
Pump tank with timed controls set to spray in the pre-dawn hours of midnight to 5:00 am
C-1 20X, Model no. 20XC1-05P4-2W115 (or equivalent) submersible pump
Liquid chlorinator
1" purple PVC supply line
2 K-Rain Gear Driven pop-up sprinklers

LANDSCAPING:


The entire surface application area must consist of an area with vegetation capable of growth, before system start up. In the event the surface application area does not have vegetation capable of growth, the bare area shall be seeded or sodded. If the non-vegetative area consists of rock or caliche, 3" of class II or III soil, capable of growing and sustaining vegetative growth, will be added before it is seeded or sodded.



Douglas R. Dowlearn

REVISED

8:56 am, Mar 28, 2025

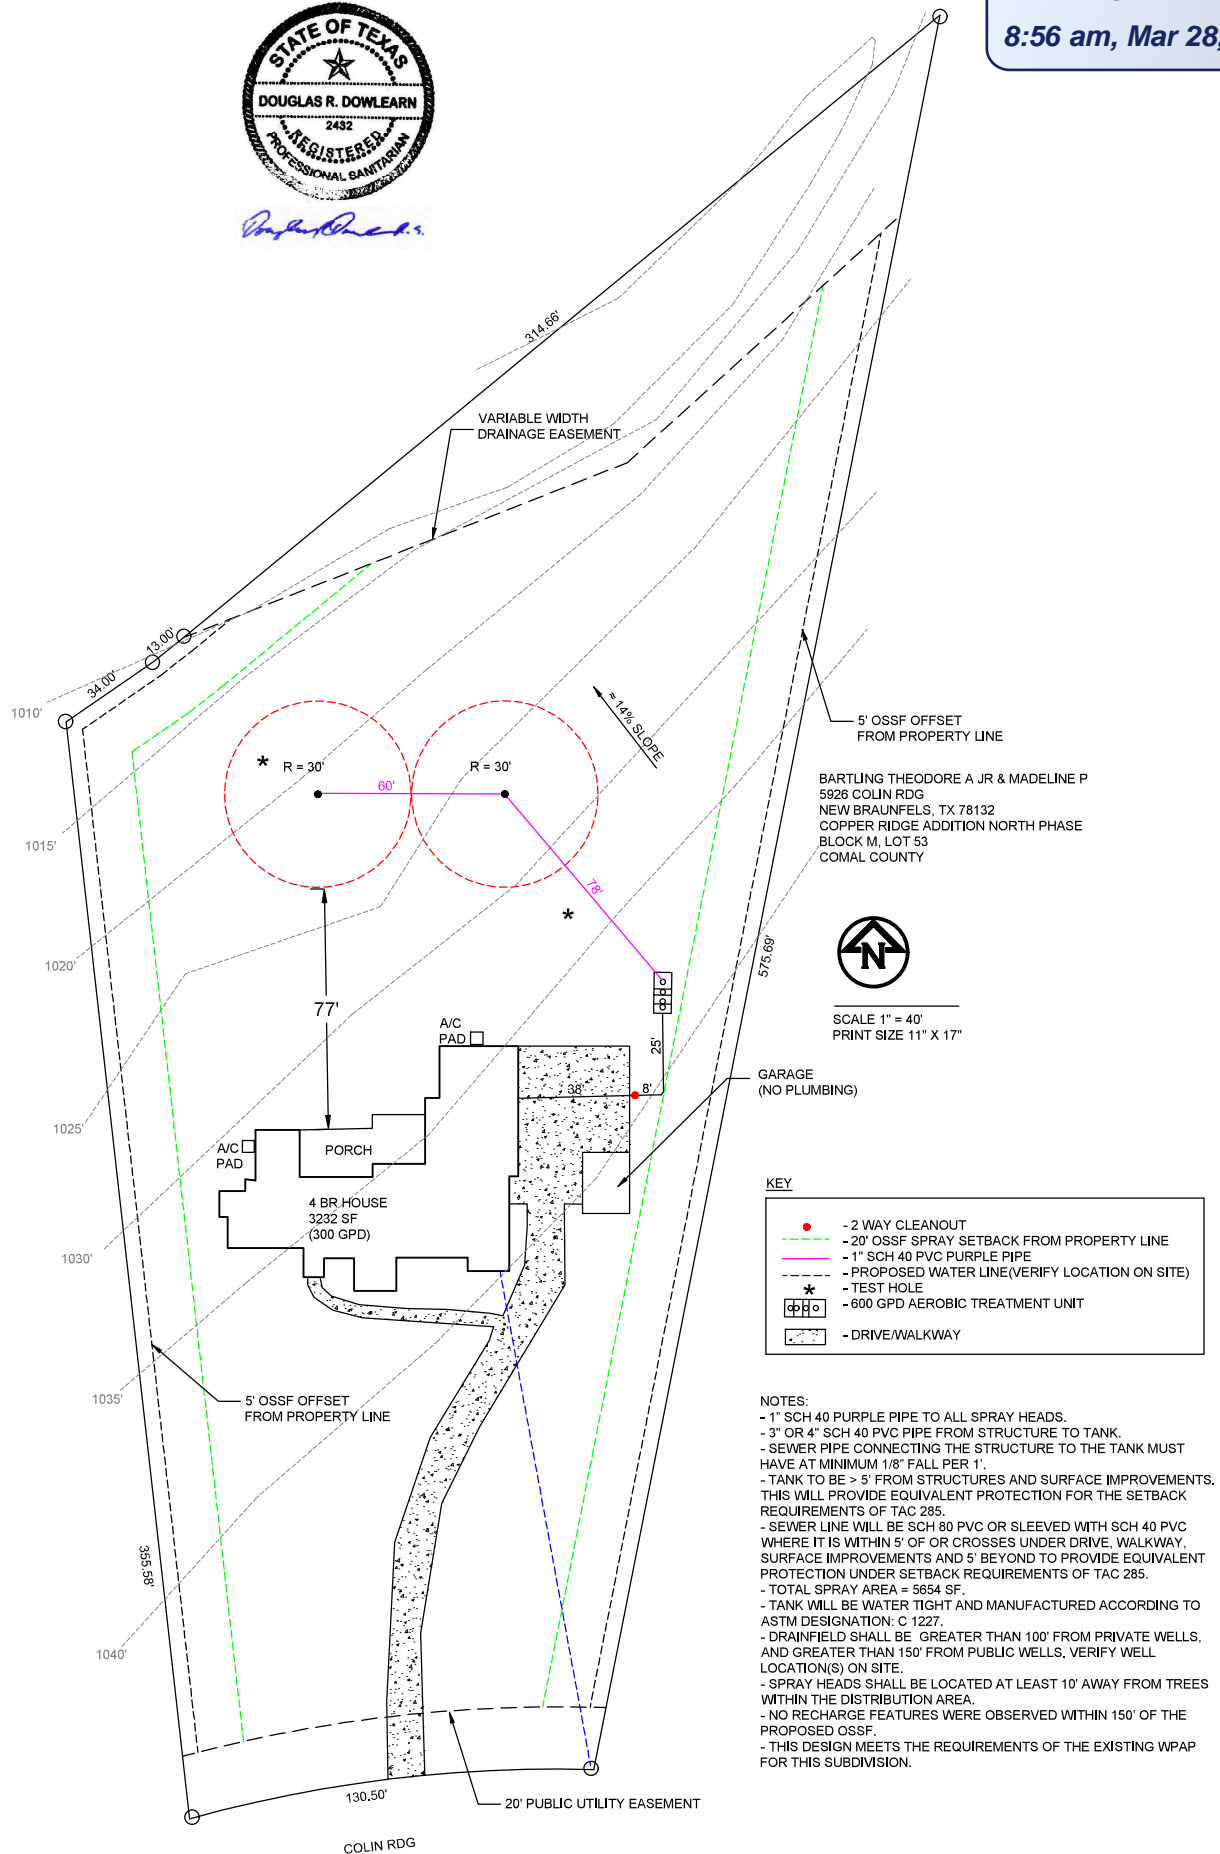

Top View Dimensions:

- Overall Length: 153.5"
- Overall Width: 82"
- Left Section Width: 76"
- Right Section Width: 3"

Side View Dimensions:

- Overall Height: 70.5"
- Trash Tank Height: 64"
- Pump Tank Height: 57"
- Bottom Section Height: 3"
- Overall Length: 151"

Component Labels:

- 3" EXTERIOR WALL TYP.
- WIRING JUNCTION BOX
- NSF CERTIFIED CHLORINATOR
- ALARM FLOAT
- EFFLUENT OUTLET WEIR
- CLARIFIER CHAMBER
- LGAS BAFFLE
- AIR LINE
- DIFFUSER
- TRASH TANK
- CONTROL FLOAT
- EFFLUENT PUMP
- 3" TAPER ON ALL EXTERIOR & INTERIOR WALLS

State of Texas Seal:

STATE OF TEXAS
DOUGLAS R. DOWLEARN
2432
REGISTERED PROFESSIONAL SANITARIAN

CLEARSTREAM®
WASTEWATER SYSTEMS, INC.
P.O. Box 7500 Houston, Texas 77228-7500
MODEL 600NC3T
600 G.P.D. TREATMENT SYSTEM

DRAWN: CWP	CHKD: JM	DATE: 07/04	REV: 2	REV. DATE: 11/06	NUMBER: 10000433
---------------	-------------	----------------	-----------	---------------------	---------------------

NOTE: SET ON A TIMER TO DOSE IN PREDAWN HOURS BETWEEN MIDNIGHT AND 5AM.

C1 SERIES

CISTERN PUMPS

Designed for use in gray water / filtered effluent service applications, the C1 Series cistern pump provides high performance and long life in less than ideal water conditions. The C1 Series pump is able to pass solids up to 1/8" without having a negative effect on the internal hydraulic components.


The pump's unique bottom suction design allows for maximum fluid drawdown without compromising durability or overall life, and it does not require the use of a flow induction sleeve. Intended specifically for use in a cistern or tank, C1 Series pumps are suitable for use in agricultural, residential, and commercial installations.



Franklin Electric

franklinwater.com

C1 Series Family Curve

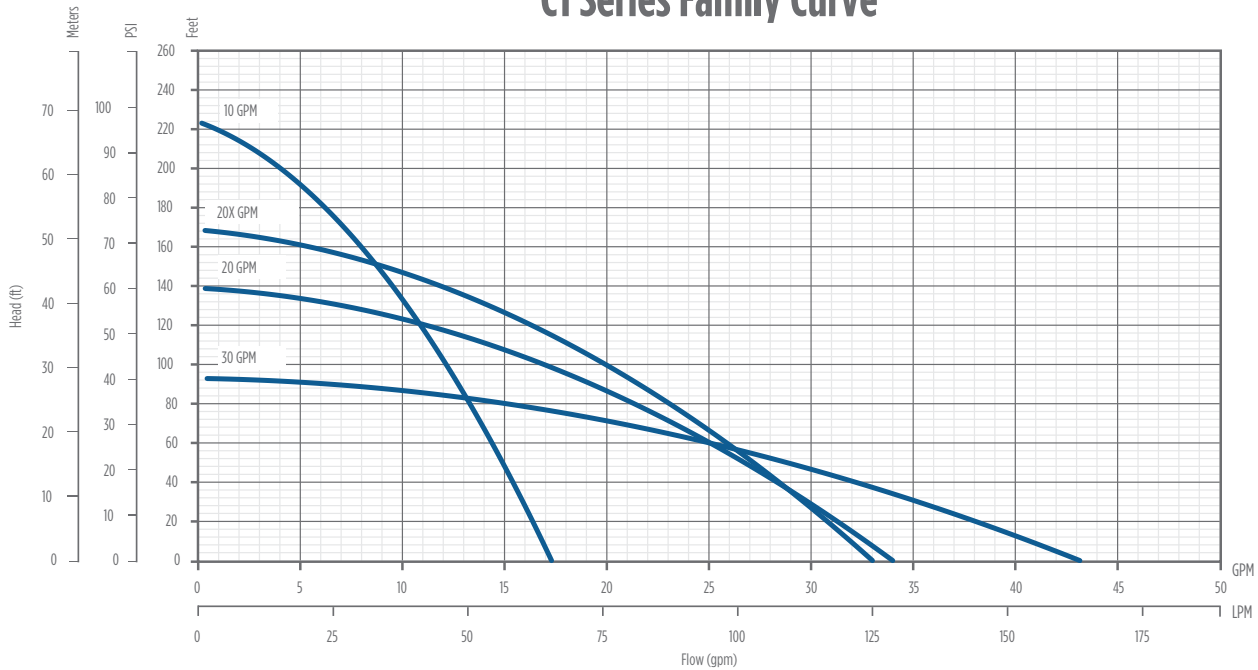

FEATURES

- Supplied with a removable 5" base for secure and reliable mounting
- Bottom suction design
- Robust thermoplastic discharge head design resists breakage during installation and operation
- Single shell housing design provides a compact unit while ensuring cool and quiet operation
- Hydraulic components molded from high quality engineered thermoplastics
- Optimized hydraulic design allows for increased performance and decreased power usage
- All metal components are made of high grade stainless steel for corrosion resistance
- Available with a high quality 115 V or 230 V, ½ hp motor
- Fluid flows of 10, 20, and 30 gpm, with a max shut-off pressure of over 100 psi
- Heavy duty 600 V 10 foot SJ00W jacketed lead

APPLICATIONS

- Gray water pumping
- Filtered effluent service water pumping
- Water reclamation projects such as pumping from rain catchment basins
- Aeration and other foundation or pond applications
- Agriculture and livestock water pumping

ORDERING INFORMATION

C1 Series Pumps							
GPM	HP	Volts	Stage	Model No.	Order No.	Length (in)	Weight (lbs)
10	1/2	115	7	10C1-05P4-2W115	90301005	26	17
		230	7	10C1-05P4-2W230	90301010	26	17
20		115	5	20C1-05P4-2W115	90302005	25	16
		230	5	20C1-05P4-2W230	90302010	25	16
20X		115	6	20XC1-05P4-2W115	90302015	26	17
		230	6	20XC1-05P4-2W230	90302020	26	17
30		115	4	30C1-05P4-2W115	90303005	25	16
		230	4	30C1-05P4-2W230	90303010	25	16

Note: All units have 10 foot long SJ00W leads.



Franklin Electric

franklinwater.com

M1698 07-14

From: [Ritzen,Brenda](#)
To: [Lauren Dowlearn](#)
Subject: Permit 118411
Date: Wednesday, March 26, 2025 4:23:00 PM
Attachments: [AFFIDAVIT OF A SINGLE FAMILY RESIDENCE.pdf](#)
[image001.png](#)

**Re: Theodore Adams Bartling Jr. & Madeline Paige Bartling
Copper Ridge, The Addition North Phase, Lot 53
Application for Permit for Authorization to Construct an On-Site
Sewage Facility (OSSF)**

Lauren :

The following information is needed before I can continue processing the referenced permit submittal:

- ✗ Add the gym to the permit application.
 - ✗ How is the gym connected to the system?
 - ✓ How will equivalent protection be provided to the clean out within the driveway
 - ✗ If the gym is for single family use then a notarized affidavit for single family use of both the home and the gym is needed. A sample affidavit form is attached.
5. Revise as needed and resubmit.

Thank you,



Brenda Ritzen
Environmental Health Coordinator
195 David Jonas Dr.
New Braunfels, TX 78132
DR:OS00007722
830-608-2090
www.cceo.org



VOID

Planning Materials & Site Evaluation as Required Completed By _____

System Description _____

Size of Septic System Required Based on Planning Materials & Soil Evaluation

Tank Size(s) (Gallons) _____ Absorption/Application Area (Sq Ft) _____

Gallons Per Day (As Per TCEQ Table III) _____

(Sites generating more than 5000 gallons per day are required to obtain a permit through TCEQ.)

Is the property located over the Edwards Recharge Zone? ☐ Yes ☐ No

(If yes, the planning materials must be completed by a Registered Sanitarian (R.S.) or Professional Engineer (P.E.))

Is there an existing TCEQ approved WPAP for the property? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design complies with all provisions of the existing WPAP.)

Is there at least one acre per single family dwelling as per 285.40(c)(1)? ☐ Yes ☐ No

If there is no existing WPAP, does the proposed development activity require a TCEQ approved WPAP? ☐ Yes ☐ No

(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed WPAP. A Permit to Construct will not be issued for the proposed OSSF until the proposed WPAP has been approved by the appropriate regional office.)

Is the property located over the Edwards Contributing Zone? ☐ Yes ☐ No

Is there an existing TCEQ approval CZP for the property? ☐ Yes ☐ No

(If yes, the P.E. or R.S. shall certify that the OSSF design complies with all provisions of the existing CZP.)

If there is no existing CZP, does the proposed development activity require a TCEQ approved CZP? ☐ Yes ☐ No


(If yes, the R.S. or P.E. shall certify that the OSSF design will comply with all provisions of the proposed CZP. A Permit to Construct will not be issued for the proposed OSSF until the CZP has been approved by the appropriate regional office.)

Is this property within an incorporated city? ☐ Yes ☐ No

If yes, indicate the city: _____

By signing this application, I certify that:

- The information provided above is true and correct to the best of my knowledge.
- I affirmatively consent to the online posting/public release of my e-mail address associated with this permit application, as applicable.



Signature of Designer

Date

OSSF SOIL EVALUATION REPORT INFORMATION

Date: 2/21/2025

Applicant Information:

Name: Theodore and Madeline Bartling

Address: 827 Dreisam

City, State & Zip Code: New Braunfels, TX 78130

Email:

VOID

Site Evaluator Information:

Name: Doug Dowlearn

Company: D.A.D. Services, Inc.

Address: 703 Oak Drive

City, State & Zip: Blanco, TX 78606

Phone: (210)240-2101 Fax: (866)260-7687

Email: txseptic@gmail.com

Property Location:

Subdivision: Copper Ridge, The Addition North Phase Lot:

53 Block : M

Street/Road Address: 5926 Colin Ridge

City : New Braunfels Zip: 78132

Additional Info: Comal County

Installer Information:

Name:

Company:

Address:

City, State & Zip:

Phone:

Depth	Texture Class	Soil Texture	Structure (For Class III – blocky, platy or massive)	Drainage (Mottles/Water Table)	Restrictive Horizon	Observation
Soil Boring #1 60"	III	0-12" Clay Loam 12"+ Limestone	Blocky	<30% Gravel	12"+ Limestone	N/A
Soil Boring #2 60"		Same as above				

DESIGN SPECIFICATIONS

Application Rate (RA): 0.064

OSSF is designed for: 4 Bedroom 3232 Sq. Ft Residence along with a 299 Sq. Ft Gym (No Plumbing)

360 gallons per day

An aerobic with spray disposal system is to be utilized based on the site evaluation.

5625 sq. ft. disposal area required

600 gallon per day aerobic treatment unit

Calculations: Absorption Area: $Q/RA=360/0.064=5625$ Sq.. Ft.

VOID

FEATURES OF SITE AREA

Presence of 100-year flood zone: NO

Existing or proposed water well in nearby area: NO

Presence of adjacent ponds, streams, water impoundments: NO

Presence of upper water shed: NO

Organized sewage service available to lot: NO

I certify that the findings of this report are based on my field observations and are accurate to the best of my ability. The site evaluation and OSSF design are subject to approval by the TCEQ or the local authorized agent. The planning materials and the OSSF design should not be considered final until a permit to construct has been issued.

Site Evaluator:

NAME: Douglas Dowlearn

Signature:



License No. OS9902 Exp. 6/30/2026

TDH: #2432 Exp. 2/28/2025

D.A.D SERVICES, INC.
DOUG DOWLEARN
PO BOX 212, BULVERDE, TX 78163
Bartling Theodor & Madeline P

VOID


The installation site is at block M, lot 53 of the Copper Ridge Addition North Phase subdivision in Comal County, TX. The proposed OSSF will treat the wastewater from a 4 Bedroom, 3232 sq. ft. residence along with a gym with 299 sq. ft. heated/cooled space. OSSF sizing is based off total living square footage between both structures, which is 4 BR/3531 sq. ft.(360 gpd). The proposed method of wastewater treatment is aerobic treatment with spray irrigation. This method was chosen because of unsuitable soil conditions.

PROPOSED SYSTEM:

A 3" or 4" PVC pipe will discharge from the residence to a pre-treatment tank, which flows into a 600 gpd aerobic treatment plant. The aerobic tank effluent flows to a storage/pump tank containing a liquid chlorinator and a single 20 gpm submersible pump. Distribution is set to spray in the pre-dawn hours of midnight to 5:00 am through 2 K-Rain Gear Driven pop-up sprinklers, with low angle (13 degrees) spray nozzles spraying at 40 psi. Each sprinkler will spray a radius of 30 feet and 360 degrees of arc. An audio and visual alarm monitoring both high water and aerator failure will be placed in a noticeable location.

DESIGN SPECIFICATIONS:

Daily Waste Flow: 360 gpd
Application rate: 0.064
Application area required: $360/.064 = 5625$ sq. ft.
Application area utilized: 5654 sq. ft.
Pump tank reserve capacity: 120 gal minimum



Douglas R. Dowlearn

SYSTEM COMPONENTS:


SCH 40 PVC sewer line
Clearstream 600NC3T
Pretreatment tank
600 GPD Aerobic Treatment Unit
Pump tank with timed controls set to spray in the pre-dawn hours of midnight to 5:00 am
C-1 20X, Model no. 20XC1-05P4-2W115 (or equivalent) submersible pump
Liquid chlorinator
1" purple PVC supply line
2 K-Rain Gear Driven pop-up sprinklers

VOID

LANDSCAPING:

The entire surface application area must consist of an area with vegetation capable of growth, before system start up. In the event the surface application area does not have vegetation capable of growth, the bare area shall be seeded or sodded. If the non-vegetative area consists of rock or caliche, 3" of class II or III soil, capable of growing and sustaining vegetative growth, will be added before it is seeded or sodded.

VOID

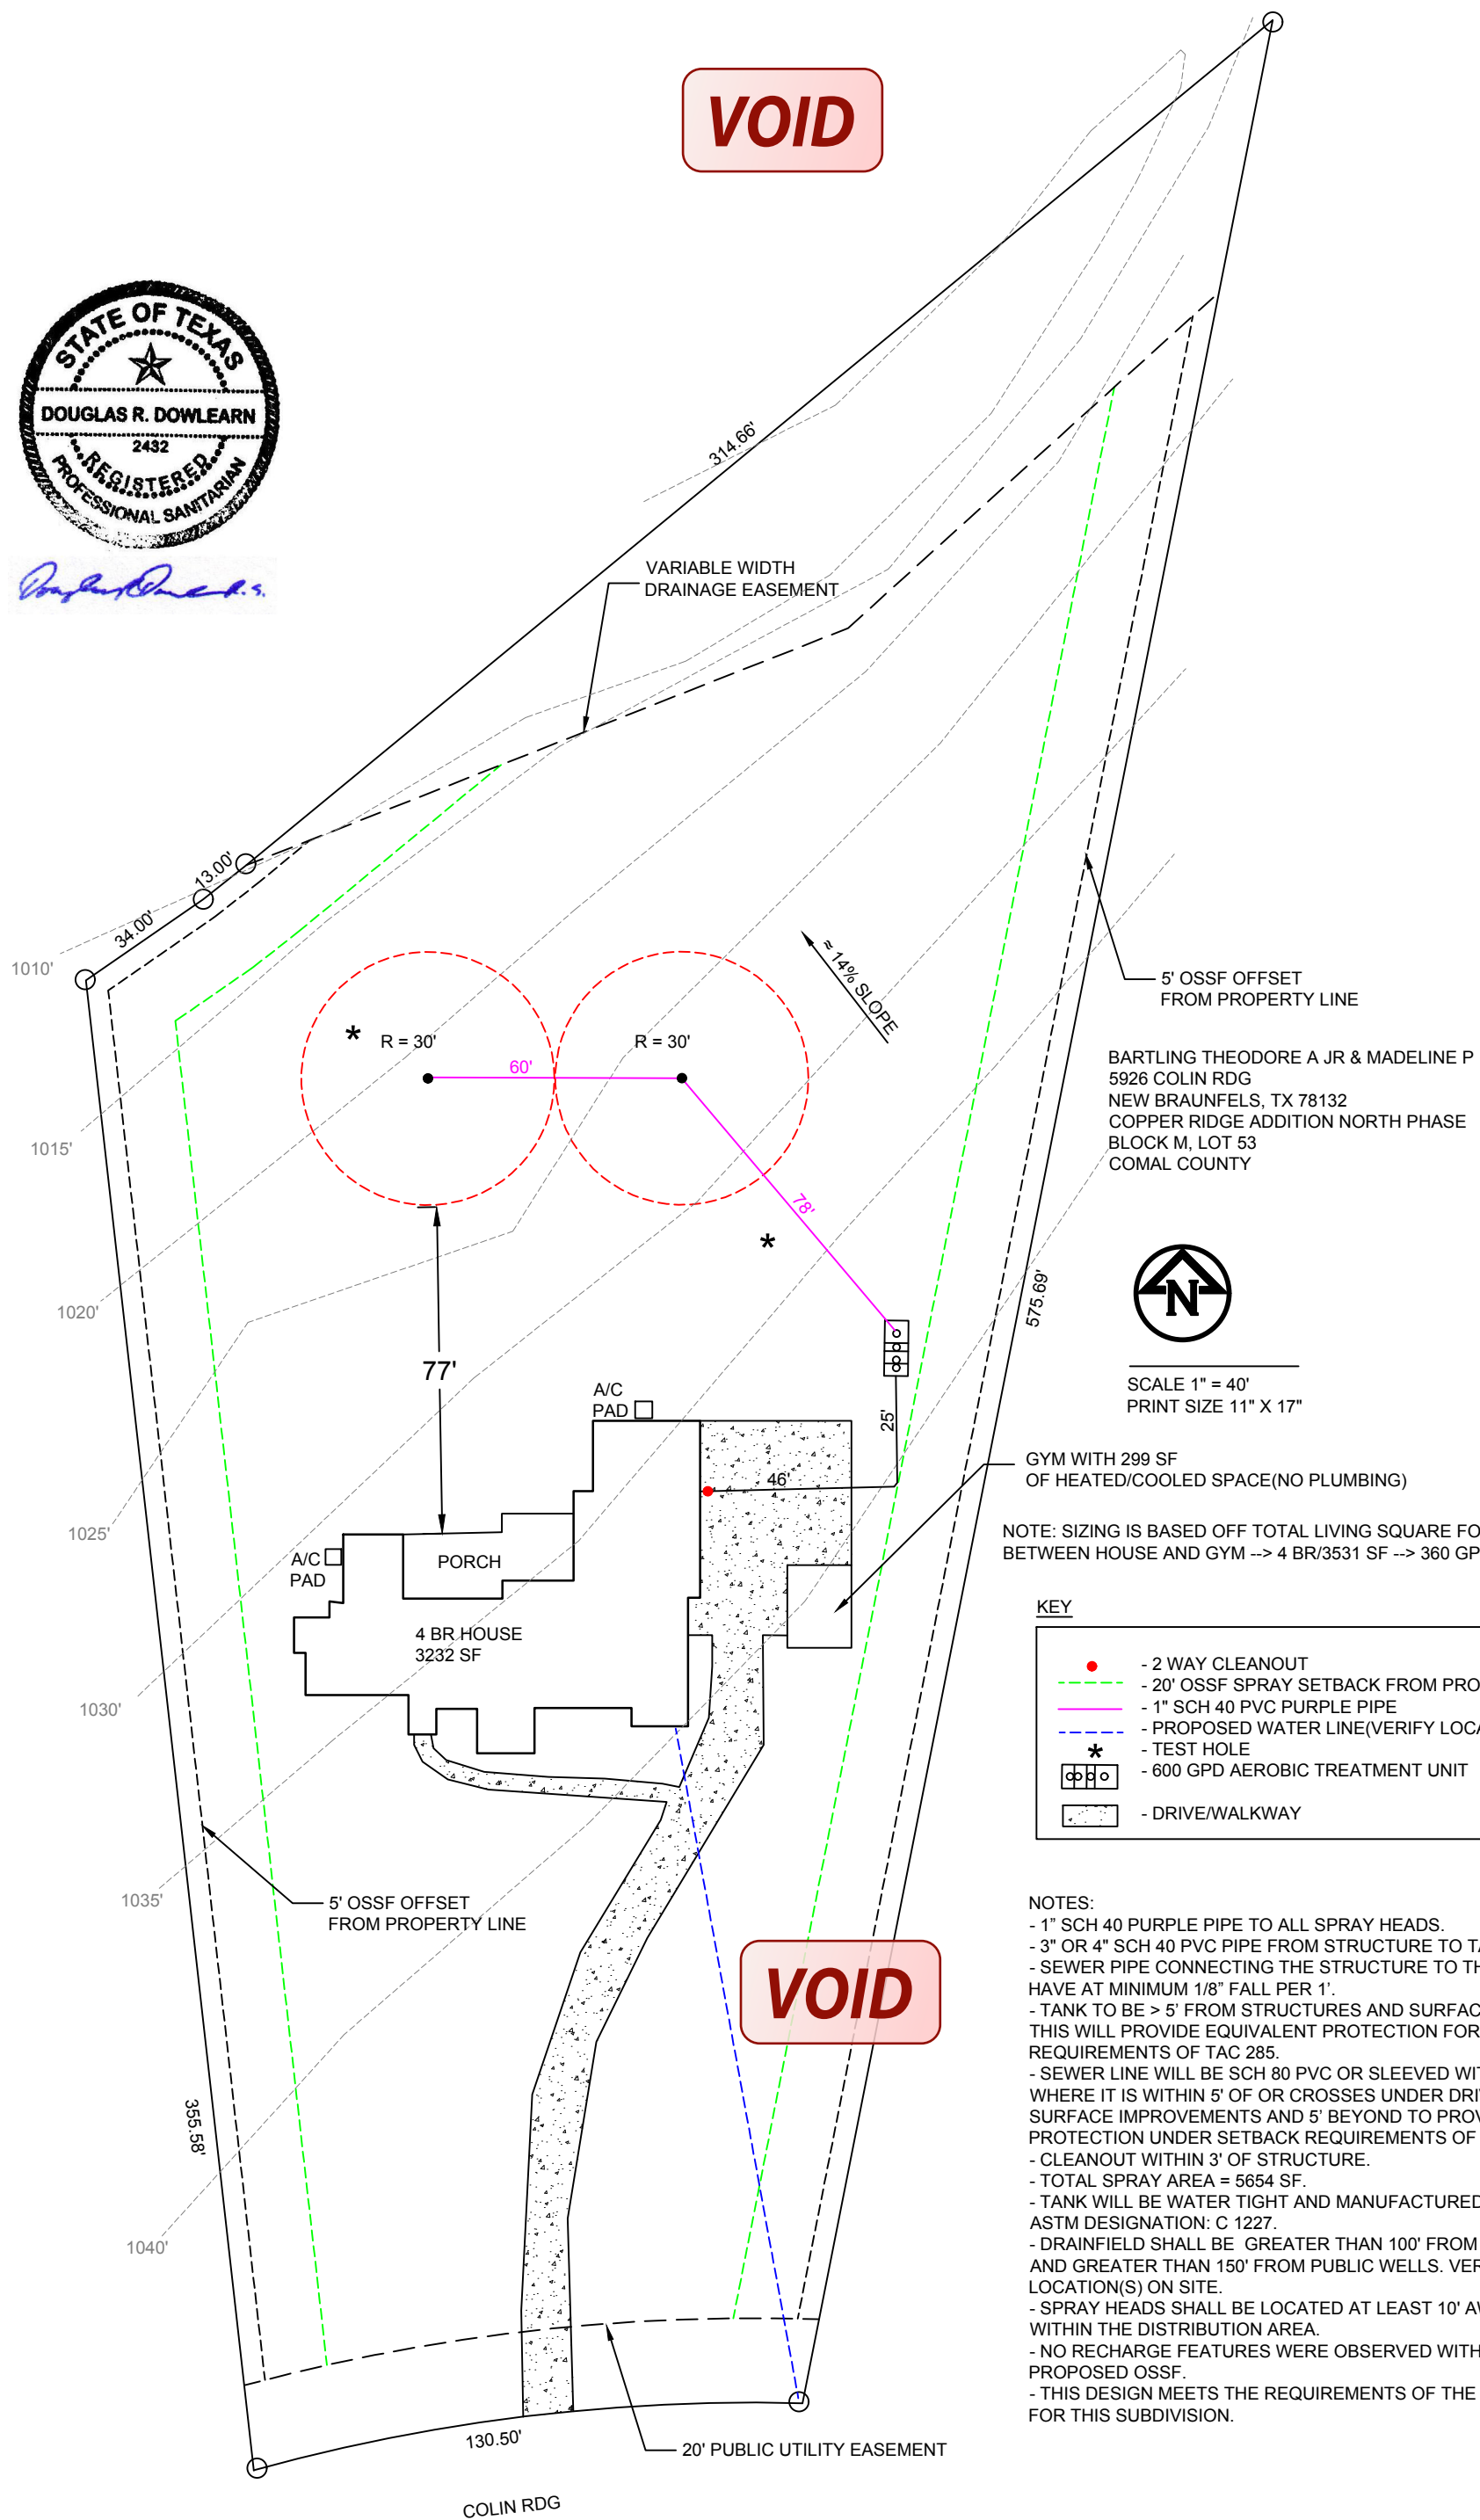

BARTLING THEODORE A JR & MADELINE P
5926 COLIN RDG
NEW BRAUNFELS, TX 78132
COPPER RIDGE ADDITION NORTH PHASE
BLOCK M, LOT 53
COMAL COUNTY










SCALE 1" = 40'
PRINT SIZE 11" X 17"

GYM WITH 299 SF
OF HEATED/COOLED SPACE(NO PLUMBING)

NOTE: SIZING IS BASED OFF TOTAL LIVING SQUARE FOOTAGE
BETWEEN HOUSE AND GYM --> 4 BR/3531 SF --> 360 GPD

KEY

-  - 2 WAY CLEANOUT
-  - 20' OSSF SPRAY SETBACK FROM PROPERTY LINE
-  - 1" SCH 40 PVC PURPLE PIPE
-  - PROPOSED WATER LINE(VERIFY LOCATION ON SITE)
-  - TEST HOLE
-  - 600 GPD AEROBIC TREATMENT UNIT
-  - DRIVE/WALKWAY

NOTES:

- 1" SCH 40 PURPLE PIPE TO ALL SPRAY HEADS.
- 3" OR 4" SCH 40 PVC PIPE FROM STRUCTURE TO TANK.
- SEWER PIPE CONNECTING THE STRUCTURE TO THE TANK MUST HAVE AT MINIMUM 1/8" FALL PER 1'.
- TANK TO BE > 5' FROM STRUCTURES AND SURFACE IMPROVEMENTS.
- THIS WILL PROVIDE EQUIVALENT PROTECTION FOR THE SETBACK REQUIREMENTS OF TAC 285.
- SEWER LINE WILL BE SCH 80 PVC OR SLEEVED WITH SCH 40 PVC WHERE IT IS WITHIN 5' OF OR CROSSES UNDER DRIVE, WALKWAY, SURFACE IMPROVEMENTS AND 5' BEYOND TO PROVIDE EQUIVALENT PROTECTION UNDER SETBACK REQUIREMENTS OF TAC 285.
- CLEANOUT WITHIN 3' OF STRUCTURE.
- TOTAL SPRAY AREA = 5654 SF.
- TANK WILL BE WATER TIGHT AND MANUFACTURED ACCORDING TO ASTM DESIGNATION: C 1227.
- DRAINFIELD SHALL BE GREATER THAN 100' FROM PRIVATE WELLS, AND GREATER THAN 150' FROM PUBLIC WELLS. VERIFY WELL LOCATION(S) ON SITE.
- SPRAY HEADS SHALL BE LOCATED AT LEAST 10' AWAY FROM TREES WITHIN THE DISTRIBUTION AREA.
- NO RECHARGE FEATURES WERE OBSERVED WITHIN 150' OF THE PROPOSED OSSF.
- THIS DESIGN MEETS THE REQUIREMENTS OF THE EXISTING WPAP FOR THIS SUBDIVISION.

GENERAL WARRANTY DEED WITH VENDOR'S LIEN

NOTICE OF CONFIDENTIALITY RIGHTS: If you are a natural person, you may remove or strike any or all of the following information from any instrument that transfers an interest in real property before it is filed for record in the public records: Your Social Security Number or your Driver's License Number

THAT Michael A. Bell and Deborah S. Bell, a married couple, hereinafter called "Grantor", for and in consideration of the sum of Ten Dollars (\$10.00) and other good and valuable consideration to Grantor in hand paid by Theodore Adams Bartling, Jr. and Madeline Paige Bartling, husband and wife, hereinafter called "Grantee", whose mailing address is 827 Dreisam, New Braunfels, TX 78130, the receipt and sufficiency of which is hereby acknowledged, and the further consideration of the execution and delivery by said Grantee of one certain Promissory Note in the principal sum of One Hundred Seventy-Five Thousand Dollars (\$175,000.00), of even date herewith, payable to the order of Security Service Federal Credit Union, hereinafter called "Mortgagee", bearing interest at the rate therein provided; said Note containing attorney's fee clause and various acceleration of maturity clauses in case of default, and being secured by Vendor's Lien and Superior Title retained herein in favor of said Mortgagee, and also being secured by Deed of Trust of even date herewith from Grantee to Ruth W. Garner, Trustee, Grantor has GRANTED, SOLD and CONVEYED, and by these presents does GRANT, SELL and CONVEY, unto said Grantee, the following described Property located in COMAL County, Texas, to-wit:

Lot 53, Block M, COPPER RIDGE, THE ADDITION NORTH PHASE, a subdivision in Comal County, Texas, according to the map or plat thereof recorded under Document No. 201806028385 Map and Plat Records of Comal County, Texas

Together with Grantor's right, title and interest in all system memberships and/or ownership certificates in any non-municipal water and/or sewer systems serving said Property.

Mortgagee has, at the special instance and request of Grantee, paid to Grantor a portion of the purchase price of the Property hereinabove described, as evidenced by the above described Note, and thus said Vendor's Lien against said Property securing the payment of the Note, is hereby assigned, transferred and delivered to Mortgagee, Grantor hereby conveying to Mortgagee the Superior Title to the Property, subrogating said Mortgagee to all the rights and remedies of Grantor in the Property by virtue of said lien.

TO HAVE AND TO HOLD the above described Property, together with all and singular the rights and appurtenances thereunto in anywise belonging to said Grantee, Grantee's heirs and assigns, forever, AND Grantor does hereby bind Grantor, Grantor's successors and assigns, to WARRANT and FOREVER DEFEND all and singular the said Property unto said Grantee, Grantee's heirs and assigns, against every person whomsoever lawfully claiming or to claim the same or any part thereof.

Grantee is taking the property in an arm's-length agreement between the parties. The consideration was bargained on the basis of an "as is, where is" transaction and reflects the agreement of the parties that there are no representations or express or implied warranties, except for the express warranty of title set forth herein. Grantee has not relied on any information other than grantee's inspection.

This conveyance is made subject to all and singular the restrictions, easements, exceptions, conditions and covenants, if any, applicable to and enforceable against the above-described Property as shown by the records of said County, as well as ad valorem taxes for current and subsequent years. But it is expressly agreed that the Vendor's Lien and Superior Title is retained in favor of the Payee of said Note against the above-described Property and improvements, until said Note and all interest thereon shall have been fully paid according to the terms thereof, when this Deed shall become absolute. When this Deed is executed by more than one person, or when the Grantee is more than one person, the instrument shall read as though pertinent verbs, nouns and pronouns were changed correspondingly, and when executed by or to a corporation, the words "heirs, executors and administrators" or "heirs and assigns" shall be construed to mean "successors and assigns".

Executed date: _____



Michael A. Bell
Michael A. Bell

Deborah S. Bell
Deborah S. Bell

State of TX
County of McKen

This instrument was acknowledged before me on (Date) 7-20-24 by Michael A. Bell, and Deborah S. Bell.

[Signature]
Notary Public (Signature of Notarial Officer)
(Signature is a tangible symbol)

THOMAS
(Printed Name of Notarial Officer)

My commission expires: 1/20/25

(Official Seal or Stamp)
AFTER RECORDING MAIL TO:
Theodore Adams Bartling, Jr.
827 Dreisam
New Braunfels, TX 78130

Prepared By:
Robertson Anschutz Vettors, LLC
10375 Richmond Avenue, Suite 200
Houston, TX 77042
Settlement Agent File Number: 24140277SA



Filed and Recorded
Official Public Records
Bobbie Koepp, County Clerk
Comal County, Texas
07/22/2024 03:41:47 PM
CHRISTY 2 Pages(s)
202406021810

Bobbie Koepp

Received 2-21-25



COMAL COUNTY
ENGINEER'S OFFICE

**OSSF DEVELOPMENT APPLICATION
CHECKLIST**

Staff will complete shaded items

--	--

Date Received

Initials

118411

Permit Number

Instructions:

Place a check mark next to all items that apply. For items that do not apply, place "N/A". This OSSF Development Application Checklist must accompany the completed application.

OSSF Permit

- ☒ Completed Application for Permit for Authorization to Construct an On-Site Sewage Facility and License to Operate
- ☒ Site/Soil Evaluation Completed by a Certified Site Evaluator or a Professional Engineer
- ☒ Planning Materials of the OSSF as Required by the TCEQ Rules for OSSF Chapter 285. Planning Materials shall consist of a scaled design and all system specifications.
- ☒ Required Permit Fee - See Attached Fee Schedule
- ☒ Copy of Recorded Deed
- ☒ Surface Application/Aerobic Treatment System
- ☒ Recorded Certification of OSSF Requiring Maintenance/Affidavit to the Public
- ☒ Signed Maintenance Contract with Effective Date as Issuance of License to Operate

I affirm that I have provided all information required for my OSSF Development Application and that this application constitutes a completed OSSF Development Application.

Signature of Applicant

Date

___ COMPLETE APPLICATION	
Check No. _____	Receipt No. _____

___ INCOMPLETE APPLICATION (Missing Items Circled, Application Refused)
--
